



**MARKET STREET AND KING STREET
INTERSECTION IMPROVEMENTS**

**BIDDING DOCUMENTS
SUPPLEMENTAL SPECIFICATIONS**

**TOWN OF LEESBURG
25 WEST MARKET STREET
LEESBURG, VIRGINIA 20176**

SEPTEMBER 9, 2021

**INVITATION FOR BID (IFB)
IFB NO. 17016-FY22-11**

NOTE: Effective January 1, 2021, and until further notice, all bids and proposals in response to a formal solicitation issued by the Town will be securely received via eVA, the Commonwealth's eProcurement website. All formal solicitations, including notices of addenda, will be posted on the Town's Bid Board (<http://www.leesburgva.gov/bidboard>) and eVA (www.eva.virginia.gov). Courtesy notifications will be provided to interested parties who have registered to receive updates. Interested parties are responsible for providing the correct contact information to the Town.

TABLE OF CONTENTS

ADVERTISEMENT FOR BID	6
REQUIRED BID RESPONSE FORMS.....	7-26
Checklist	7
Bid Submission Form (Including Conflict of Interest and Collusion Certifications)	8-9
Acknowledgement of Addenda.....	10
Bid Form – Pricing (Submitted Electronically via eVA)	11-19
Escrow of Retained Funds.....	20
Bid Bond.....	21-22
Qualification Form	23
Reference Form	24-25
Subcontractor Form.....	26
INSTRUCTIONS TO BIDDERS	27-39
Background.....	27
Scope of Work.....	27
Comments Concerning Specifications (VPPA 2.2-4316)	27-28
Incomplete Documents.....	28
Town of Leesburg Business Professional and Occupation License (BPOL).....	28
Form and Style of Bids.....	28-29
Bid Bond.....	29
Submission of Bids.....	29-30
Modification/Withdrawal of Bid.....	30
Consideration of Bids & Bid Opening.....	31
Award	31
Negotiations with the Lowest Responsive Bidder.....	32
Qualifications of the Lowest Responsive Bidder	32
Protest.....	33
Acceptance of Bid (VPPA 2.2-4337).....	33
SCC Identification Number (VPPA 2.2-4311.2).....	33
Virginia Contractor’s License Number (Code of Virginia §54.1-1115, A1 and A6).....	33
Stipulated Prices	33-34
Compensation and Payment.....	34
Coordination with Utilities.....	34
Contract Time.....	34
Trees.....	34
Contract Items of Work.....	35-37
Maintenance of Traffic	37-39
TREE PROTECTION SPECIFICATIONS.....	40-43
Site Clearing, Demolition.....	40-41
Pruning Specifications.....	41-42

Construction Specifications	42-43
SAMPLE AGREEMENT.....	44-52
Sample Agreement	44-48
Sample Payment Bond	49-50
Sample Performance Bond.....	51-52
GENERAL CONDITIONS	GC-1 – GC-85
ARTICLE 1: CONTRACT DOCUMENTS	GC-2 – GC-5
1.1 DEFINITIONS	GC-2 – GC-3
1.2 EXECUTION, CORRELATION AND INTENT	GC-3 – GC-5
1.3 OWNERSHIP AND USE OF DOCUMENTS.....	GC-6
ARTICLE 2: OWNER'S PROJECT MANAGER.....	GC-6
2.1 DEFINITIONS	GC-6
2.2 SERVICES OF THE OWNER'S PROJECT MANAGER.....	GC-6
ARTICLE 3: OWNER.....	GC-7-GC-10
3.1 DEFINITIONS	GC-7
3.2 INFORMATION, SERVICES AND RIGHTS OF THE OWNER.....	GC-7
3.3 OWNER'S RIGHT TO STOP OR TO SUSPEND WORK	GC-7 – GC-8
3.4 OWNER'S RIGHT TO CARRY OUT THE WORK.....	GC-8 – GC-9
3.5 EXAMINATION OF RECORDS	GC-10
ARTICLE 4: CONTRACTOR.....	GC-11 – GC-35
4.1 DEFINITION.....	GC-11
4.2 REVIEW OF CONTRACT DOCUMENTS	GC-11
4.3 SUPERVISION AND CONSTRUCTION PROCEDURES.....	GC-11 – GC-12
4.4 INSPECTION OF CONSTRUCTION	GC-12
4.5 CONTRACTOR'S REPRESENTATIONS	GC-13 – GC-15
4.6 LABOR AND MATERIALS	GC-15 – GC-20
4.7 WARRANTY	GC-20 – GC-21
4.8 TAXES	GC-21 – GC-22
4.9 PERMITS, FEES AND NOTICES	GC-22
4.10 SUPERINTENDENT	GC-22 – GC-23
4.11 PROJECT SCHEDULES	GC-23 – GC-26
4.12 RESPONSIBILITY FOR COMPLETION	GC-26 – GC-27
4.13 DOCUMENTS, OTHER SUBMITTALS AT THE SITE; AS-BUILT DRAWINGS.....	GC-27
4.14 SHOP DRAWINGS, PRODUCT DATA, SAMPLES AND OTHER SUBMITTALS	GC-27 – GC-30
4.15 CUTTING AND PATCHING OF WORK	GC-30
4.16 DRUG FREE WORKPLACE.....	GC-30 – GC-31
4.17 NON-DISCRIMINATION IN EMPLOYMENT	GC-31
4.18 SIGNS.....	GC-31

4.19	CLEANING UP.....	GC-32
4.20	ROYALTIES AND PATENTS.....	GC-32
4.21	ANTI-TRUST.....	GC-33
4.22	INDEMNIFICATION.....	GC-33 – GC-34
4.23	PERSONS AUTHORIZED TO SIGN DOCUMENTS.....	GC-34
4.24	ASBESTOS.....	GC-34 – GC-35
4.25	RIGHT TO PUBLISH.....	GC-35
4.26	MATERIALS AND EQUIPMENT LIST.....	GC-35
ARTICLE 5: SUBCONTRACTORS..... GC-36 – GC-38		
5.1	DEFINITIONS.....	GC-36
5.2	AWARD OF SUBCONTRACTS AND OTHER CONTRACTS FOR PORTIONS OF THE WORK.....	GC-36 – GC-37
5.3	SUBCONTRACTUAL RELATIONS.....	GC-37
5.4	QUALIFICATION SUBMITTALS.....	GC-37 – GC-38
ARTICLE 6: WORK BY OWNER OR BY SEPARATE CONTRACTORS..... GC-39 – GC-40		
6.1	OWNER'S RIGHT TO PERFORM WORK AND TO AWARD SEPARATE CONTRACTS.....	GC-39
6.2	MUTUAL RESPONSIBILITY.....	GC-39
6.3	OWNER'S RIGHT TO PERFORM DISPUTED WORK.....	GC-40
6.4	COORDINATION OF THE WORK.....	GC-40
ARTICLE 7: MISCELLANEOUS PROVISIONS..... GC-41 – GC-44		
7.1	GOVERNING LAW.....	GC-41
7.2	SUCCESSORS AND ASSIGNS.....	GC-41
7.3	CLAIMS FOR DAMAGES.....	GC-42
7.4	DISPUTES.....	GC-42
7.5	TESTS.....	GC-43 – GC-44
7.6	UNENFORCEABILITY OF ANY PROVISION.....	GC-44
7.7	AVAILABILITY OF LANDS.....	GC-44
7.8	NONEXCLUSIVITY OF REMEDIES.....	GC-44
ARTICLE 8: TIME..... GC-45 – GC-49		
8.1	DEFINITIONS.....	GC-45
8.2	PROGRESS AND COMPLETION.....	GC-46
8.3	DELAYS AND EXTENSIONS OF TIME.....	GC-46 – GC-49
ARTICLE 9: PAYMENTS AND COMPLETION..... GC-50 – GC-59		
9.1	CONTRACT PRICE.....	GC-50
9.2	SCHEDULE OF VALUES.....	GC-50
9.3	APPLICATIONS FOR PAYMENT.....	GC-51 – GC-53
9.4	CERTIFICATES FOR PAYMENT.....	GC-53
9.5	PROGRESS PAYMENTS.....	GC-53 – GC-55
9.6	PAYMENTS WITHHELD.....	GC-55 – GC-56

9.7	SUBSTANTIAL COMPLETION	GC-56 – GC-57
9.8	FINAL COMPLETION AND FINAL PAYMENT	GC-57 – GC-59
9.9	PARTIAL OCCUPANCY OR USE	GC-59
ARTICLE 10: PROTECTION OF PERSONS AND PROPERTY		
10.1	SAFETY PRECAUTIONS AND PROGRAMS.....	GC-60
10.2	SAFETY OF PERSONS AND PROPERTY	GC-60 – GC-63
10.3	EMERGENCIES	GC-63
ARTICLE 11: BONDS AND INSURANCE.....		
11.1	BONDS	GC-64
11.2	CONTRACTOR'S LIABILITY INSURANCE	GC-65 – GC-67
11.3	WAIVERS OF SUBROGATION	GC-68
11.4	ADDITIONAL INSURANCE PROVISIONS	GC-68
ARTICLE 12: CHANGES IN THE WORK.....		
12.1	CHANGES IN THE WORK.....	GC-69 – GC-77
12.2	FIELD ORDER	GC-69
12.3	REQUEST FOR PROPOSAL.....	GC-69 – GC-70
12.4	PROPOSED CHANGE ORDER	GC-70
12.5	CHANGE ORDER	GC-71 – GC-73
12.6	UNILATERAL CHANGE ORDER.....	GC-73
12.7	DECREASES AND WORK NOT PERFORMED.....	GC-73 – GC-74
12.8	CHANGES IN LINE AND GRADE.....	GC-74 – GC-75
12.9	DIFFERING SITE CONDITIONS.....	GC-75
12.10	CLAIMS FOR ADDITIONAL COST AND/OR TIME	GC-76
12.11	ATTORNEYS' FEES AND OTHER EXPENSES	GC-76 – GC-77
ARTICLE 13: UNCOVERING AND CORRECTION OF WORK.....		
13.1	UNCOVERING OF WORK	GC-78 – GC-79
13.2	CORRECTION OF WORK	GC-78 – GC-79
13.3	ACCEPTANCE OF DEFECTIVE OR NON-CONFORMING WORK.....	GC-79
ARTICLE 14: TERMINATION OF THE CONTRACT.....		
14.1	TERMINATION FOR THE CONVENIENCE OF THE OWNER.....	GC-80 – GC-85
14.2	ALLOWABLE CONVENIENCE TERMINATION COSTS	GC-80 – GC-81
14.3	DEFAULT TERMINATION	GC-82 – GC-83
14.4	GENERAL TERMINATION PROVISIONS	GC-83 – GC-85
2015 Test Hole Data		
		1-7
2020 & 2021 Test Hole Data		
		1-15
TrafficPatternsXD Spec Sheet		
		1-2
eVA New Vendor Registration Guide		
		1-7
eVA Electronic Bid Submission Guide for IFBs		
		1-3

END OF TABLE OF CONTENTS

**TOWN OF LEESBURG
ADVERTISEMENT FOR BID**

**IFB NO. 17016-FY22-11
MARKET STREET AND KING STREET INTERSECTION IMPROVEMENTS**

****NOTE: Effective January 1, 2021, all bids and proposals in response to a formal solicitation issued by the Town will be securely received via eVA, the Commonwealth's eProcurement website. Additionally, at this time the Town is not conducting in-person public bid openings. ****

SEALED BIDS to construct the above project WILL BE RECEIVED by the Town of Leesburg, electronically via the Commonwealth's e-procurement website (www.eva.virginia.gov), **UNTIL BUT NO LATER THAN 3:00 P.M. ON THURSDAY, SEPTEMBER 30, 2021.** Bids shall be submitted electronically using the following naming convention: the IFB number and the name of the bidder (i.e. "IFB No. 17016-FY22-11_Your Company's Name").

All questions regarding this bid must be submitted in writing via email to CapitalBidQuestions@leesburgva.gov until but no later than 5:00 P.M. on Tuesday, September 21, 2021.

Bids will be publicly opened via Microsoft Teams using the eVA e-Procurement website at the due date and time listed above. The bid opening will be livestreamed via Microsoft Teams and made available to the public.

- To join the meeting and view the video shared by the Town of Leesburg from your computer, please see the following link(s): [Click here to join the meeting](#) or go to: https://teams.microsoft.com/l/meetup-join/19%3ameeting_NzA1NTg4MwYtYTkyYi00MjZlZWYyMmYtZTBhMWVjYjhkZjgz%40thread.v2/0?context=%7b%22Tid%22%3a%22fcff6f14-98e4-4734-bf54-941f010e77b7%22%2c%22Oid%22%3a%22b08c9db0-f4a3-4eed-87b5-2fe32ac2c53a%22%7d
- To join the meeting via phone, please see the following dial-in info:
Dial In #: +1 689-218-0588
Meeting Conference ID: 806 745 0#
- For more information: [Learn More](#)

Work will be done at night between the hours of 9:00 p.m. and 7:00 a.m. Sunday night through Thursday night and includes excavation, storm drainage, waterline improvements, curb, gutter, brick sidewalk, installation of electrical and communication conduits, traffic signal upgrades, pedestrian signals, paving, maintenance of traffic, miscellaneous site work, and all incidentals related thereto. The Town reserves the right to perform all, part, or none of the work.

Bid Documents are available for download from the Town's Bid Board at <http://www.leesburgva.gov/bidboard>. Any addenda issued for this project will be posted on the Town's Bid Board and eVA (<https://eva.virginia.gov>) with a courtesy email to those firms who have registered on the Town's Bid Board. It is the bidders' responsibility to provide a correct email address and to be aware of any addenda.

Renée LaFollette, Director
Department of Public Works and Capital Projects



REQUIRED BID RESPONSE FORMS
IFB NO. 17016-FY22-11
MARKET STREET AND KING STREET
INTERSECTION IMPROVEMENTS

Bidders shall submit bids to the Town in accordance with the Submission of Bids section of the Bid Documents and shall include the following completed documents with their bid submission:

Checklist

- _____ **Bid Submission Form (includes Conflict of Interest and Collusion Certifications)**
- _____ **Acknowledgement of Addenda**
- _____ **Bid Form – Pricing (For Reference Only) ** SUBMITTED ELECTRONICALLY VIA EVA****
- _____ **Escrow of Retained Funds**
- _____ **Bid Bond ** The original bid security shall be delivered to the Town within two (2) business days after the bids are due to the Town. See the Bid Bond section of the Bid Documents for details and instructions. ****
- _____ **Qualification Form**
- _____ **Reference Form**
- _____ **Subcontractor Plan**

Bidders shall use the required bid response forms included in the Bid Documents when submitting their bid to the Town. Bidders who do not provide all required bid response forms may be deemed non-responsive.



BID SUBMISSION FORM
IFB NO. 17016-FY22-11
MARKET STREET AND KING STREET
INTERSECTION IMPROVEMENTS

SUBMIT A SIGNED BID FORM VIA EVA, WWW.EVA.VIRGINIA.GOV

**FORMAL BIDS WILL BE DUE NO LATER THAN:
3:00 P.M. ON THURSDAY, SEPTEMBER 30, 2021**

The undersigned agrees to furnish all necessary labor, equipment, materials, and all things necessary to perform the work as set forth in accordance with the plans and specifications at the following prices.

SECTION I – COMPANY IDENTIFICATION AND OWNERSHIP DISCLOSURE

Company _____

Address _____

Contact Person _____ Title _____

Telephone No. _____ Fax No. _____

Email _____

Business Type (check one):

Corporation Limited Partnership Limited Liability Company

General Partnership Unincorporated Assoc. Sole Proprietorship

Organized under the laws of the State of _____

State Corp. Commission Registration No. _____ (attach Certificate of Good Standing)

Virginia Contractor's License No. _____

Federal Identification No. _____

The Town of Leesburg requests, as a matter of policy, that any bidder receiving a contract of award resulting from a formal solicitation issued by the Town shall make certification as specified below. Receipt of such certification, shall be a prerequisite to the award of contract and payment thereof.

SECTION II – EMPLOYEES NOT TO BENEFIT - I (we) hereby certify that if the contract is awarded to our company, partnership, or corporation, that no employee of the Town of Leesburg, or members of his/her immediate family, including spouse, parents or children has received or been promised, directly or indirectly, any financial benefit, by way of fee, commission, finder’s fee, political contribution or any similar form of remuneration on account of the act of awarding and/or executing this contract.

SECTION III – CONFLICTS OF INTEREST - This solicitation is subject to the provisions of VA Code Ann. Section 2.1-639.2 et seq., the State and Local Government Conflict of Interests Act. **The Bidder [] is [] is not aware of any information bearing on the existence of any potential organizational conflict of interest.**

SECTION IV – COLLUSION - I certify that this offer is made without prior understanding, agreement, or connection with any corporation, firm, or person submitting an offer for the same services, materials, supplies, or equipment and is in all respects fair and without collusion or fraud. I understand collusive bidding is a violation of the State and federal law and can result in fines, prison sentences, and civil damage awards. I hereby certify that the responses to the above representations, certifications, and other statements are accurate and complete. I agree to abide by all conditions of this IFB and certify that I am authorized to sign for my company.

Signature _____ Date _____
Name (Printed) _____ Title _____

BIDDER MUST RETURN THIS FORM WITH THEIR BID



**ACKNOWLEDGEMENT OF ADDENDA
IFB NO. 17016-FY22-11
MARKET STREET AND KING STREET
INTERSECTION IMPROVEMENTS**

Bidder acknowledges receipt of the following ADDENDA, which have been considered in the preparation of this bid.

Addendum No. _____
Addendum No. _____
Addendum No. _____
Addendum No. _____

Dated: _____
Dated: _____
Dated: _____
Dated: _____

BIDDER MUST RETURN THIS FORM WITH THEIR BID

BID FORM – FOR REFERENCE ONLY

**** Submit bid pricing electronically via eVA. This form is for reference only and should not be submitted with a bid. ****

Item	Description	Unit	Quantity	Unit Price	Extended Price
<i>Miscellaneous</i>					
1	Mobilization / Demobilization	LS	1		
2	Pre-survey and Post-survey of Buildings and Structures Within the Construction Limits	LS	1		
3	Construction Survey	LS	1		
4	Inlet Protection, Complete in Place incl. Maintenance and Removal	EA	13		
5	Safety Fence Complete in Place Incl. Maintenance & Removal	LF	500		
6	Reset Planter as directed by Town Engineer	EA	1		
7	Remove and Reset Existing Fence (If Required)	LF	30		
8	Test Pits as Noted on the Plans and as Required by Miss Utility. Test Pits to be Performed Ten (10) Days Prior to Start of Construction. Inform the Town Project Manager of any Conflicts.	EA	20		
9	Wall waterproofing, Fluid-Applied Dry-Lock waterproof coating	SF	250		
10	Parking Meter Base, 6" PVC Pipe Complete in place per Plan Details including Excavation, Bedding & Backfill	EA	2		
<i>Subtotal Miscellaneous</i>					
<i>Utilities</i>					
11	12" RCP Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	LF	8		
12	15" RCP Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	LF	13		
13	18" RCP Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	LF	88		
14	18"x12" ERCP Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	LF	14		
15	23"x14" RCP Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	LF	17		

16	102.1 Storm Structure DI-3B (L=8', H=4.7'), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
17	102.2 Storm Structure DI-3C (L=8', H=4.6'), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
18	102.3 Storm Structure (Modified Structure per Plan Details Including MH Frame & Cover), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
19	102.5 Storm Structure DI-3B (L=6', H=5.3'), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
20	102.6 Storm Structure (Modified Structure per Plan Details Including MH Frame & Cover), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
21	102.7 Storm Structure DI-3C (L=8', H=4'), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
22	102.7A Storm Structure (Modified Junction Box per Plan Details), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
23	102.9 Storm Structure DI-3C (L=8', H=3.1'), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
24	102.10 Storm Structure DI-3C (L=8', H=4.6'), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
25	102.11 Storm Structure (Modified Structure per Plan Details Including MH Frame & Cover), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
26	102.14 Storm Structure (Modify Existing MH and Adjust to Grade) Including Frame & Cover, Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	LS	1		
27	102.15 Storm Structure (Modify Existing MH and Adjust to Grade) Including Frame & Cover, Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	LS	1		
28	3.1 Storm Structure DI-3B (L=10', H=3.4'), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
29	3.2 Storm Structure (Doghouse MH Including Frame & Cover), Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
30	Replace Pipe at Structure 102.15 and Connect to Structure 102.15	LS	1		
31	Cut and Plug Existing 24" Pipe at Structure EX39	LS	1		
32	Remove & Dispose of Existing Inlet	EA	3		

33	Adjust to grade Existing Structure EX42, Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
34	Concrete Piers per Plan Details, complete in place including excavation, bedding and backfill	EA	4		
35	8" Zinc Coated D.I.P, complete in place including excavation, bedding and backfill	LF	40		
36	8"X8" TEE, complete in place including excavation, bedding and backfill	EA	4		
37	8"X6" TEE, complete in place including excavation, bedding and backfill	EA	1		
38	8"X6" Reducer, complete in place including excavation, bedding and backfill	EA	1		
39	8" Gate Valve, complete in place including excavation, bedding and backfill	EA	4		
40	6" Gate Valve, complete in place including excavation, bedding and backfill	EA	1		
41	8" Cap, complete in place including excavation, bedding and backfill	EA	4		
42	FH Assembly per Town DCSM WS-16, complete in place including excavation, bedding and backfill	EA	1		
43	Connect to existing 8" D.I.P CL 52 water main with 8" Sleeve, complete in place including excavation, bedding and backfill	EA	6		
44	Connect to existing 6" D.I.P CL 52 water main with 6" Sleeve, complete in place including excavation, bedding and backfill	EA	2		
45	Foster Adapters, complete in place including excavation, bedding and backfill	EA	4		
46	Anchor Coupling, complete in place including excavation, bedding and backfill	EA	8		
47	Remove Existing Water Valve	EA	4		
48	Remove Existing Fire Hydrant	EA	1		
49	Remove & Replace Existing Concrete Collar, Complete Incl. Installation per DCSM TS-12E	EA	8		

50	Post Installation Video Inspection of Sanitary Laterals (After Completion of Storm Sewer Improvements)	LF	80		
51	4" DIP Pipe Roof Drain Connect to Structure 102.2, Complete in place including Excavation, Bedding & Backfill	LS	1		
52	4" DIP Pipe Roof Drain Connect to Structure 102.9, Complete in place including Excavation, Bedding & Backfill	LS	1		
53	4" DIP Pipe Roof Drain Connect to Structure 102.10, Complete in place including Excavation, Bedding & Backfill	LS	1		
54	Tie in Sump Pump Drain Pipe to Storm Structure, Complete Incl backflow preventer	EA	1		
				Subtotal Utilities	
Concrete / Pavement					
55	Saw Cut Asphalt	LF	1000		
56	Remove and Dispose of Existing Curb and Curb & Gutter	LF	450		
57	Remove and Dispose of Existing Header Curb	LF	50		
58	Remove and Dispose of Existing Brick Sidewalk Incl. Concrete and Base Course to the Depth Shown on the Plans.	SF	3000		
59	Unclassified Excavation - Demo & Dispose of Asphalt Pavement including Stone Base etc.. to the depth shown on the plans	SF	3000		
60	Curb and Gutter CG-6 on a properly prepared subgrade. Complete incl. Excavation , 4" VDOT 21-A Stone Under Curb and Backfill	LF	350		
61	Modified Curb and Gutter CG-6 on a properly prepared subgrade. Complete incl. Excavation , 4" VDOT 21-A Stone Under Curb and Backfill	LF	150		
62	CG-2 Curb on a properly prepared subgrade. Complete incl. Excavation , 4" VDOT 21-A Stone Under Curb and Backfill	LF	10		
63	MOD CG-12 Type A, Handicap Ramp per plans, Complete in place incl. Excavation, Stone Base, Detectable Warning Surface & Backfill	EA	5		
64	MOD CG-12 Type B, Handicap Ramp per plans, Complete in place incl. Excavation, Stone Base, Detectable Warning Surface & Backfill	EA	3		

65	Brick Sidewalk with Concrete Cradle, Complete in place as per Plans and Specifications incl. Excavation, VDOT 21-A, Concrete & Brick (TOL standard TS-12A)	SF	2200		
66	Full Depth Pavement, Complete in place as per plan Details and specifications incl. excavation, 8" VDOT 21-A and 8" Asphalt Base Course BM-25.0	SF	3000		
67	Asphalt, Intermediate course, VDOT type IM-19.0 for Pavement Build-Up	TN	100		
68	Bituminous Concrete Pavement Milling - Variable Depth but not less than 2"	SY	1000		
69	Asphalt, Surface course, VDOT type SM-9.5A	TN	250		
70	Extra Cost for Concrete Plant to be open at night	DAY	20		
Subtotal Concrete/Pavement					
Maintenance of Traffic (MOT)					
71	Supply, Install, Relocate Type III Barricade (8')	EA	20		
72	Supply, Install, Relocate & Remove R9-9 (SIDEWALK CLOSED) 24"x12" Sign Incl. Post/Stand	EA	2		
73	Supply, Install, Relocate & Remove R9-10 (SIDEWALK CLOSED ←→ USE OTHERSIDE) 24"x12" Sign Incl. Post/Stand	EA	2		
74	Supply, Install, Relocate & Remove R9-11L or R9-11R (SIDEWALK CLOSED AHEAD CROSS HERE) 24"x18" Sign Incl. Post/Stand	EA	2		
75	Supply, Install, Relocate & Remove R11-2 (ROAD CLOSED) 30"x24" Sign Incl. Post/Stand	EA	4		
76	Supply, Install, Relocate & Remove R11-4 (ROAD CLOSED TO THRU TRAFFIC) 30"x24" Sign Incl. Post/Stand	EA	7		
77	Supply, Install, Relocate & Remove R11-4 (ROAD CLOSED TO THRU TRAFFIC) 48"x24" Sign Incl. Post/Stand	EA	2		
78	Supply, Install, Relocate & Remove M4-VI (DETOUR ↑) 30"x24" Sign Incl. Post/Stand	EA	11		
79	Supply, Install, Relocate & Remove M4-9R (DETOUR →) 30"x24" Sign Incl. Post/Stand	EA	4		
80	Supply, Install, Relocate & Remove M4-9L 30"x24" "DETOUR ←" Sign Incl. Post/Stand	EA	3		

81	Supply, Install, Relocate & Remove M4-10R (→DETOUR) 24"x8" Sign Incl. Post/Stand	EA	3		
82	Supply, Install, Relocate & Remove M4-10L (←DETOUR) 24"x8" Sign Incl. Post/Stand	EA	1		
83	Supply, Install, Relocate & Remove M4-VP1A (W Market St) Varx12" Sign Incl. Post/Stand	EA	2		
84	Supply, Install, Relocate & Remove M4-VP1A (N King St) Varx12" Sign Incl. Post/Stand	EA	4		
85	Supply, Install, Relocate & Remove G20-2 (END ROAD WORK) 36"x18" Sign Incl. Post/Stand	EA	4		
86	Supply, Install, Relocate & Remove W20-1 (ROAD WORK AHEAD) 30"x30" Sign Incl. Post/Stand	EA	9		
87	Supply, Install, Relocate & Remove W20-2 (DETOUR AHEAD) 30"x30" Sign Incl. Post/Stand	EA	5		
88	Supply, Install, Relocate & Remove W20-3 (ROAD CLOSED 000 FT) 30"x30" Sign Incl. Post/Stand	EA	10		
89	Short Term Traffic Control - Flagger Services (Including 2EA W20-7 "Flagman", 2EA W3-4 "Be Prepared To Stop", EA W20-4 "One Lane Road Ahead" & 2EA W20-1 "Road Work Ahead" Signs)	HR	80		
90	Portable Changeable Message Board (Required 6 PCMB)	WK	84		
Subtotal Maintenance of Traffic					
Pavement Marking / Signs					
91	Double Solid 4" Yellow Line with 4" Spacing Type B CL I	LF	300		
92	Single Solid 4" White line - Parking Space Marking Type B CL I	LF	20		
93	24" Wide White Line (Stop Bar) Type B CL I	LF	70		
94	Single Solid 6" White line Type B CL I (Pedestrian Crosswalks)	LF	350		
95	TrafficPatternsXD Impresses Performed Thermoplastic Crosswalk, per Plan Details and Specification - Color: Colonial Brick Red, Running Bond Pattern	SF	2650		

96	Install New Special Sign - Street Name- (48" x 8") Diamond Grade - Prismatic Lens, Reflective Sheeting, Complete incl. 2x2, 14 Gauge Galv Steel Post (per DCSM TS-5)	EA	4		
97	Relocate Sign as Directed by Town Engineer	EA	2		
98	Remove Sign and Post and Deliver to Towns Street Operation Shop	EA	13		
99	Remove, Store and/or Reset Existing Sign as directed by Town Engineer	EA	1		
100	Remove Parking Meter and Deliver to Town Street Operation Shop	EA	2		
Subtotal Pavement Marking/Signs					
Traffic Signal					
101	1" PVC Conduit, Complete in place incl. excavation, bedding & backfill	LF	100		
102	3" PVC Conduit, Complete in place incl. excavation, bedding & backfill	LF	100		
103	4" PVC Conduit, Complete in place incl. excavation, bedding & backfill	LF	175		
104	14/2C (S) Conductor Cable Shielded	LF	500		
105	14/2C Conductor Cable	LF	800		
106	14/7C Conductor Cable	LF	800		
107	14/1 Enclosed Conductor Cable	LF	1500		
108	#6 AWG/3C	LF	500		
109	Junction Box, JB - R1, Complete in place as per plans and specifications	EA	4		
110	Junction Box, JB - R2, Complete in place as per plans and specifications	EA	4		
111	Pedestrian Pole (Black Powder Coated), Complete as per plans and specifications	EA	4		
112	Pedestrian Push Button with Sign R10-3E, Complete as per plans and specifications	EA	4		
113	Concrete Foundation Pedestal Pole, Incl. excavation, backfill and all incidentals	EA	4		

114	Relocate Pedestrian Pole, Complete as per plans and specifications	EA	2		
115	Provide Power Source SE-6 (Meter / Disconnect Switch), complete as per plans and specifications	LS	1		
116	Remove Pedestrian Signal and Deliver to Towns Street Operation Shop	EA	4		
117	SP-8 pedestrian signal Head (Black Powder Coated Enclosure)	EA	4		
118	Supply and install 360 CMOS video detection camera and processor with extender; complete installation (1 camera system)	LS	1		
119	GTT 764 Phase Selector, Complete as per plans and specifications	EA	1		
120	GTT Preemption 722 detector with single confirmation light per approach, Complete as per plans and specifications	EA	2		
121	OPTICOM Cable GTT 138	LF	500		
122	Sawcut for Loops	LF	650		
	Subtotal Traffic Signal				
	Street Lights				
123	1-3" Metal Conduit, Complete in place incl. excavation, bedding & backfill	LF	350		
124	2-4" Metal Conduit, Complete in place incl. excavation, bedding & backfill	LF	300		
125	3-4" Metal Conduit, Complete in place incl. excavation, bedding & backfill	LF	200		
126	Demo Existing Light Pole Foundation, Remove Concrete to 12" Below Proposed Sidewalk Grade	EA	2		
127	Street Light Foundation, per plan and DCSM specifications, complete in place including, concrete removal, excavation, and backfill.	EA	4		
128	Install TOWN SUPPLIED Street Lights , Complete as per plans and specifications	EA	4		
129	#10 Cable, Complete as per plans and specifications	LF	300		

130	Connectors, Complete as per plans and specifications	EA	8		
131	Tie Proposed Ductbank to Existing Ductbank, Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	LS	1		
132	Connect to Existing Junction Box	EA	1		
133	Cap Proposed Ductbank, Complete in Place incl. Excavation, Bedding and backfill w/VDOT 21-A	EA	1		
134	Remove and Dispose of Existing Junction Box	EA	1		
	Subtotal Street Lights				
	TOTAL BID PRICE (SUM OF EXTENDED PRICES OF ITEMS 1 – 134)				

NOT A PART OF THE BID PACKAGE. DO NOT RETURN THIS FORM WITH BID.

ESCROW OF RETAINED FUNDS

In accordance with Section 2.2-4334 of the Virginia Public Procurement Act (VPPA), any Contract valued at \$200,000.00 or more for construction of highways, roads, streets, bridges, parking lots, demolition, clearing, grading, excavating, paving, pile driving miscellaneous drainage structures, and the installation of water, gas, sewer lines and pumping stations where portions of the Contract price are to be retained, at the time of submitting a bid, the CONTRACTOR shall have the option to indicate preference for using the escrow account procedure for utilization of the Town retained funds by so indicating in the space provided in the proposal documents. In the event the successful Contract elects to use the escrow account procedure, the "Escrow Agreement" included in the Contract documents shall be executed and submitted to the Manager, Office of Capital Projects within 15 days after receipt of the Notice to Award. If the "Escrow Agreement" form is not submitted, the CONTRACTOR shall forfeit his rights to the use of the escrow account procedure within the 15-day period.

In order to have retained funds paid to an escrow agent, the CONTRACTOR, the escrow agent, and the surety shall execute the "Escrow Agreement" furnished by the TOWN, and submit same to the Manager of Capital Projects for approval. The CONTRACTOR's escrow agent shall be a trust company, approved bank or savings and loan institution with its principal office located in the Commonwealth of Virginia. The "Escrow Agreement" shall contain the complete address of the escrow agent and surety, and the executed "Escrow Agreement" will be authority for the TOWN to make payment of retained funds to the escrow agent. After approving the agreement, the TOWN will pay to the escrow agent the funds retained as provided herein, except that funds retained for lack of progress or other deficiencies on the part of the CONTRACTOR will not be paid to the escrow agent. The escrow agent may, in accordance with the stipulations contained in the "Escrow Agreement", invest the funds paid into the escrow account and pay earnings on such investments to the CONTRACTOR, or release the funds to the CONTRACTOR, provided such funds are fully secured by approved securities.

Retained funds invested, and securities held as collateral for retainage may be released only as and when directed by the Manager, Office of Capital Projects. When the final estimate is released for payment, the Manager, Office of Capital Projects will direct the escrow agent to settle the escrow amount by paying the CONTRACTOR or the TOWN monies due them as determined by the Manager, Office of Capital Projects. The TOWN reserves the right to recall retained funds and to release same to the surety upon receipt of written request from the CONTRACTOR or in the event of default.

- We elect to use the escrow account procedure for the deposit of retained funds.

- We elect not to use the escrow account procedure for the deposit of retained funds.

BIDDER MUST RETURN THIS FORM WITH THEIR BID

BID BOND

BOND NO. _____

AMOUNT: \$ _____

KNOW ALL MEN BY THESE MEN PRESENTS, that _____ hereinafter called the PRINCIPAL, and _____ a corporation duly organized under the laws of the State of _____ having its principal place of business at _____ in the State of _____ and authorized to do business in the Commonwealth of Virginia, as SURETY, are held and firmly bound unto _____, as OWNER, hereinafter called the OBLIGEE, in the sum of _____ DOLLARS (\$ _____) for the payment for which we bind ourselves, our heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents.

THE CONDITION OF THIS BOND IS SUCH THAT:

WHEREAS, the PRINCIPAL is herewith submitting his or its Bid Proposal for _____ said Bid Proposal, by reference thereto, being hereby made a part hereof.

NOW THEREFORE,

- (A) If the bid shall remain open for a period of not less than 60 days following opening of the bids and be rejected, or in the alternate,
- (B) If the bid shall remain open for a period of not less than 60 days following opening of the bids and be accepted and the PRINCIPAL shall execute and deliver a Contract in the form of Contract attached hereto (properly completed in accordance with the bid) and shall furnish a performance and payment deposit or surety bond for his faithful performance of the Contract, and for the payment of all persons performing labor or furnishing materials in connection therewith,
- (C) THEN, this obligation shall be void; otherwise the same shall remain in force and effect, it being expressly understood and agreed that the liability of the SURETY for any and all claims hereunder shall, in no event, exceed the said amount of this obligation as herein stated. Provided, however, that in addition to the amount of this obligation as herein stated, the SURETY shall be liable for all costs and attorney's fees incurred by the OBLIGEE in enforcing the obligations hereunder.

The SURETY, for value received, hereby stipulates and agrees that the obligation of the SURETY and its bond shall be in no way impaired or affected by any extension of the time

within which the OWNER may accept such bid; and the SURETY does hereby waive notice of such extension.

IN WITNESS WHEREOF, the PRINCIPAL and the SURETY have hereunto set their hands and seals, and have executed this instrument and such of them as are corporations have caused their corporate seals to be hereto affixed and these presents to be signed by their proper officers, the day and year first set forth above.

Signed and sealed this _____ day of _____, 20_____ .

PRINCIPAL

By _____

SURETY

By _____
Attorney-In-Fact

IMPORTANT: The SURETY executing bonds must appear on the Treasury Department's most current list (Circular 570 as amended) and be authorized to transact business in the Commonwealth of Virginia.

BIDDER MUST RETURN THIS FORM WITH THEIR BID

QUALIFICATION FORM

Note: Please refer to the QUALIFICATIONS OF THE LOWEST BIDDER SECTION of the Bid Documents. The following information is required as part of your response to this solicitation. Failure to complete and provide this form with your bid response may result in the Town deeming your bid as non-responsive.

1. Qualification: Bidder must have the capability and capacity in all respects to satisfy fully all of the contractual requirements.

2. Years in Business: Indicate the length of time you have been in business providing this type of good or service:

Years: _____ Months: _____

3. Contractor’s Primary Contact(s) for this project:

Project Manager: _____ Email: _____ Phone: _____

Superintendent: _____ Email: _____ Phone: _____

Other (list title): _____ Email: _____ Phone: _____

4. Indicate below a listing of at least three (3) projects of similar size and scope within the past ten (10) years for which both the Project Manager and Superintendent specified and assigned for this project have successfully worked. Include reference contact information (name, email, and phone number), a description of work performed, the dates of service, and the contract value of the referenced project.

Company (Owner): _____ Contact: _____

Phone: (____) _____ Email Address: _____

Project Description: _____

Dates of Service: _____ Value (\$): _____

Company (Owner): _____ Contact: _____

Phone: (____) _____ Email Address: _____

Project Description: _____

Dates of Service: _____ Value (\$): _____

Company (Owner): _____ Contact: _____

Phone: (____) _____ Email Address: _____

Project Description: _____

Dates of Service: _____ Value (\$): _____

BIDDER MUST RETURN THIS FORM WITH THEIR BID

REFERENCE FORM

Note: Please refer to the *QUALIFICATIONS OF THE LOWEST BIDDER SECTION* of the Bid Documents. Indicate below a listing of at least three (3) current or recent municipal clients for whom the Contractor has performed and completed this type of work. Include reference contact information (email and phone number), a short description of work performed, the dates of service, and the name, email address, and telephone number of the point of contact. Failure to complete and provide this form with your bid response may result in the Town deeming your bid as non-responsive.

Reference No. 1 (Required):

Customer (Owner) Representative's Name

Description of Work Performed & Dates of Service

Representative's Name

Phone Number

Email Address

Reference No. 2 (Required):

Customer (Owner) Representative's Name

Description of Work Performed & Dates of Service

Representative's Name

Phone Number

Email Address

Reference No. 3 (Required):

Customer (Owner) Representative's Name

Description of Work Performed & Dates of Service

Representative's Name

Phone Number

Email Address

Reference No. 4 (Optional):

Customer (Owner) Representative's Name

Description of Work Performed & Dates of Service

Representative's Name

Phone Number

Email Address

Reference No. 5 (Optional):

Customer (Owner) Representative's Name

Description of Work Performed & Dates of Service

Representative's Name

Phone Number

Email Address

BIDDER MUST RETURN THIS FORM WITH THEIR BID

SUBCONTRACTOR FORM

Note: Please note QUALIFICATIONS OF THE LOWEST BIDDER SECTION of the Bid Documents. The following information is required as part of your response to this solicitation. Failure to complete and provide this form with your bid response may result in the Town deeming your bid as non-responsive.

If you are NOT using any subcontractor(s), please initial here _____

If you are using subcontractor(s), please list them in the following table:

<i>Subcontractor(s) Name & Address</i>	<i>Contact Name, Email Address, & Phone Number</i>	<i>Type of Work to Be Performed</i>	<i>Percentage of Work</i>

I/We agree that the information provided herein is accurate, current, and complete to the best of my/our knowledge.

Signature: _____

Title of Company Official: _____

Date: _____

BIDDER MUST RETURN THIS FORM WITH THEIR BID

INSTRUCTIONS TO BIDDERS

BACKGROUND

The Market Street and King Street Intersection Improvements project includes drainage improvements at the intersection of Market Street and King Street. Existing inlets currently located at each corner of the intersection will be replaced with seven (7) new inlets set back away from the corners. Also included in the project is the replacement of the 50-year-old street lights with four (4) new lights and adding conduit to reroute power to the lights and signal pole underground. The intersection will be regraded to drain to the new structures and will also include installation of four (4) new pedestrian poles, eight (8) new ADA ramps, pavement restoration, new striping and relocation/replacement of signage.

Construction is scheduled to begin in January 2022.

SCOPE OF WORK

The Town of Leesburg, Virginia (“Town”) is requesting sealed bids from qualified Bidders to provide construction services for the Market Street and King Street Intersection Improvements project.

The awarded bidder, also referred to herein as “Contractor”, shall provide construction services, including, but not limited to excavation, storm drainage, waterline improvements, curb, gutter, brick sidewalk, installation of electrical and communication conduits, traffic signal upgrades, pedestrian signals, paving, maintenance of traffic, miscellaneous site work, and all incidentals related thereto to complete all of the construction work as shown on the attached plans and specifications.

Work will be done at night between the hours of 9:00 p.m. and 7:00 a.m. Sunday night through Thursday night.

The Town reserves the right to perform all, part, or none of the work.

COMMENTS CONCERNING SPECIFICATIONS (VPPA 2.2-4316)

General and Technical questions relating to this solicitation shall be submitted in writing to the Office of Capital Projects by email at CapitalBidQuestions@leesburgva.gov. Please put the title of this IFB in the subject line of the email.

If any questions or responses require revisions to the solicitation as originally published, such revisions will be by formal addendum only. Bidders are cautioned that any written or oral representations made by any Town representative or other person that appear to change materially any portion of the solicitation shall not be relied upon unless subsequently ratified by a written addendum to this solicitation issued by the Office of Capital Projects. For determination as to whether an oral or written representation of any Town representative or other person requires that an addendum be issued, contact the Manager, Office of Capital Projects in writing

via email at CapitalBidQuestions@leesburgva.gov.

INCOMPLETE DOCUMENTS

The Contractor, as a bidder, is responsible for having determined the accuracy and completeness of bid documents upon which it relied in making its bid, and having notified the Manager, Office of Capital Projects immediately upon discovery of an apparent inaccuracy, error in, or omission of any pages, drawings, sections, or addenda whose omission from the documents was apparent from a reference or page numbering in the bidding documents.

If the Contractor proceeds with any activity that may be affected by an inaccuracy, error in, or omission described above, of which it has not notified the Manager, Office of Capital Projects, the Contractor hereby agrees to perform any work described in such missing or incomplete documents at no additional cost to the Town.

TOWN OF LEESBURG BUSINESS PROFESSIONAL AND OCCUPATION LICENSE (BPOL)

Bidders do not have to obtain a BPOL license in order to submit a bid to the Town; however, the successful bidder must obtain a license, if applicable, prior to award of the contract.

The successful bidder must comply with the provisions of Section 20-233 (License requirement) of the Town of Leesburg Code, if applicable. For information on the provisions of this chapter and its applicability to this Contract, contact the Town of Leesburg Accounting Associate, Finance Department, Town of Leesburg, Virginia, at telephone number 703-771-2753 or email BusinessLic@leesburgva.gov.

FORM AND STYLE OF BIDS

NOTE: THIS SECTION CONTAINS REVISED PROCUREMENT PROCEDURES

Bids shall be submitted electronically via the Commonwealth's electronic procurement website (eVA). Unless otherwise specified or permitted herein, prices shall be submitted on all line items shown in eVA. In addition to submitting bid pricing electronically via eVA, bidder shall also upload all completed bid response forms as required by the Town with their Bid.

Bids shall include the legal name of the Bidder and a statement that the Bidder is a sole proprietor, partnership, corporation, or other legal entity. Bids shall be signed by the person or persons legally authorized to bind the Bidder to a contract. During the COVID-19 State of Emergency, and for the duration of the Emergency or until further notice, electronic signatures will be accepted by the Town; submission of a bid through the eVA system constitutes your representation that your firm authorizes the use of electronic signatures. A Bid by a corporation shall further give the state of incorporation and have the corporate seal affixed. All names shall be typed or printed in ink below the signatures. The address, phone number and email address for communication regarding the bid shall be shown.

Bids shall contain evidence of the Bidder's authority to do business in the Commonwealth of Virginia. Bidder's Virginia State Contractor license number shall also be shown on the Bid Response Form.

BID BOND

NOTE: THIS SECTION CONTAINS REVISED PROCUREMENT PROCEDURES

Each bid shall be accompanied with a copy of the bid security (on enclosed form or cashier's check), in the amount of five percent (5%) of the bidder's Total Bid Price, pledging that the Bidder will enter into a Contract with the TOWN on the terms stated in the Bid. Should the Bidder refuse to enter into such Contract the amount of the bid security shall be forfeited to the TOWN as liquidated damages, not as a penalty. The amount of the bid security shall not be forfeited to the TOWN in the event the TOWN fails to prove financial capability if requested in writing by the successful bidder. Pursuant to VPPA Section 2.2-4336.

The original bid security shall be delivered to the Town within two (2) business days after the bids are due to the Town. The original bid security shall be mailed to: Town of Leesburg, Virginia, Attn: Procurement Office, 25 W. Market Street, Leesburg, VA 20176. The Town reserves the right to deem bidders non-responsive for failure to provide the original bid security within the timeframe specified.

The TOWN will have the right to retain the bid security of Bidders to whom an award is being considered until either (a) the Contract has been executed or (b) the specified time has elapsed so that Bids may be withdrawn, or (c) all Bids have been rejected.

SUBMISSION OF BIDS

NOTE: THIS SECTION CONTAINS REVISED PROCUREMENT PROCEDURES

In order to be considered for a contract award, bidders must complete and submit a response to this IFB via the Commonwealth's electronic procurement website eVA (www.eva.virginia.gov). eVA streamlines and automates government purchasing activities in the Commonwealth. The eVA portal is the gateway for vendors to conduct business with state agencies and public bodies. Bidders desiring to provide goods and/or services to the Town must be a registered vendor in eVA. eVA Vendor Registration is free.

On the eVA website, www.eva.virginia.gov, applicants must login as a vendor using their eVA username and password. Please contact eVA Customer Care for instructions and/or assistance in registering to become a vendor, login, and/or uploading documents. eVA Customer Care:

Hours: 8:00 AM to 4:45 PM, Monday through Friday
Phone Toll Free: 866-289-7367
Email: eVACustomerCare@DGS.Virginia.gov

Guides for registering as a new vendor and submitting bids on eVA are included at the end of this bid document.

Bids shall be submitted electronically to the Town via the Commonwealth's eVA website **prior** to the bid submission deadline stipulated for this IFB or as amended via any subsequent addenda issued by the Town. Bidders assume full responsibility for the electronic delivery of the completed proposal to www.eva.virginia.gov on or before the deadline for submission. The Town is not responsible for any loss or delay with respect to the submission of bids. Late bids will **not** be accepted. Bids submitted by any method other than via the eVA website will **not** be accepted.

All required forms and documentation submitted in response to this IFB must be uploaded as one (1) pdf attachment to eVA (www.eva.virginia.gov). The attachment should use the following naming convention: the IFB number and the name of the bidder (i.e. IFB No. _____ - Your Company's Name).

NOTE: eVA will not allow a bidder to upload documents after the deadline set for receipt of bids. Any submission partially uploaded at the deadline date and time will be considered incomplete and will not be accepted. ANY PROPOSAL RECEIVED BY THE TOWN AFTER THE DEADLINE FOR SUBMISSION WILL NOT BE ACCEPTED.

MODIFICATION/WITHDRAWAL OF BID

NOTE: THIS SECTION CONTAINS REVISED PROCUREMENT PROCEDURES

A Bid may not be modified, withdrawn, or cancelled by the Bidder during the stipulated time period following the time and date designated for the receipt of Bids, and each Bidder so agrees in submitting a Bid.

Prior to the time and date designated for receipt of Bids, a Bid submitted electronically to the Town via the Commonwealth's eVA website may be modified or withdrawn.

Withdrawn Bids may be resubmitted up to the date and time designated for the receipt of Bids, provided that they are then fully in conformance with these Instructions to Bidders.

Bid security, if required, shall be in an amount sufficient for the Bid as modified or resubmitted.

If within two (2) business days after Bids are opened and Bidder files a duly signed written notice, accompanied by original work papers, with the TOWN that there was a material and substantial mistake in the preparation of its Bid, that Bidder may withdraw its Bid, and the Bid security will be returned. Withdrawal of bids submitted to the TOWN is governed by Section 2.2-4330 of the Virginia Public Procurement Act (VPPA).

CONSIDERATION OF BIDS & BID OPENING

NOTE: THIS SECTION CONTAINS REVISED PROCUREMENT PROCEDURES

The TOWN shall have the right to reject any or all Bids, reject a Bid not accompanied by a required bid security or by other data required by the Bidding Documents, or reject a Bid, which is in any way incomplete or irregular. Though the eVA website does not reject multiple bid submissions, the TOWN permits only one bid to be submitted by the same firm in response to this IFB. Accordingly, the Town reserves the right to reject multiple bids submitted by the same firm in eVA. If a bidder submits more than one bid in response to this IFB, only the most recent submission will be considered, and previously submitted bids will be rejected.

All bids received will be opened publicly and read aloud utilizing the Commonwealth's eVA website. The bid opening for this project will be held at date and time specified in the Advertisement for Bid. The bid opening will be livestreamed via Microsoft Teams for accessibility to the public.

After the bids are opened and publicly read aloud, the Town will recalculate the arithmetic of all bids. The recalculation will consist of the following:

1. The Extended Price will be the Quantity x Unit Price. The accuracy of this calculation will be verified for all unit price items of work. All mathematical errors will be corrected to arrive at the correct extended price. If a bidder submits "NO BID" or no price is shown or entered for the Unit Price, the bidder shall be deemed non-responsive. If a bidder submits a price of "0" for the Unit Price, it will be understood to be at a unit price of zero or no cost to the Town.
2. The sum of all extensions will be calculated and any mathematical errors will be corrected.
3. If there are multiple sections to the bid, for example the Total Base Bid = Section 'A' + 'B', the sum of the sections will be calculated. All mathematical errors will be corrected.

The corrected price and correct sum thereof will be used to determine the lowest responsive, responsible bidder and will become the value of the recommended contract award.

AWARD

It is the intent of the TOWN to award a Contract to the lowest responsive and responsible Bidder, provided the low bid does not exceed the funds available. The Town reserves the right to accept or to reject any or all bids in whole or in part, to make multiple awards, and to waive informalities in the process of awarding this contract. The Notice of Intent to Award a contract resulting from this Invitation for Bid will be posted on the Public Notice Board at 25 W. Market Street, Leesburg, VA and on the Town's Bid Board (<https://www.leesburgva.gov/bidboard>).

NEGOTIATIONS WITH THE LOWEST RESPONSIVE BIDDER

Unless all bids are cancelled or rejected, the Town reserves the right granted by 2.2-4318 of the *Code of Virginia* to negotiate with the lowest responsive, responsible bidder to obtain a contract price within the funds available. Funds available shall mean those funds, which were budgeted for this contract prior to the issuance of the written Invitation for Bids. Negotiations with the low bidder may include both modifications of the bid price and the Scope of Work/Specifications to be performed. The Town shall initiate such negotiations by written notice to the lowest responsive, responsible bidder that its bid exceeds the available funds and the Town wishes to negotiate a lower contract price. The times, places, and manner of negotiating shall be agreed to by the Town and the lowest responsive, responsible bidder.

QUALIFICATIONS OF THE LOWEST RESPONSIVE BIDDER

This project requires specialized knowledge and expertise. The Contractor shall be well versed in the scope of work for this project. If the Contractor does not have specific experience with regards to projects similar in complexity they will not be considered for the award of this project. The Contractor must submit written information demonstrating experience by having completed a minimum of three (3) similar projects within the last ten (10) years and commit to the availability of key, skilled personnel necessary to complete the entire scope of work required for the project.

All qualification documentation shall be submitted as part of the bidder's bid package. Bids received without the required documentation shall be deemed non-responsive.

1. Project descriptions (3 similar projects, maximum of three (3) pages per project) indicating client, project scope, location, time frame).
2. The Superintendent and the Project Manager specified by the Contractor and assigned to this contract shall each have successfully worked on three (3) projects, similar in both size and scope, within the past ten (10) years. For work to be considered similar, work must be comparable to that shown in the scope of work.
3. Provide a reference list of three (3) municipal clients for whom the Contractor has performed and completed this type of work. Include reference contact information (email and phone number), and a description of work.
4. The Contractor shall self-perform a majority of the work. At the time of the bid, the Contractor shall name any anticipated subcontractors and define the work expected to be performed on the contract by each subcontractor.

PROTEST

Any bidder or offeror who desires to protest the award or decision to award a contract shall submit such protest in writing to the TOWN, no later than 10 days after public notice of award or the announcement of the decision to award, whichever occurs first, pursuant to Section 2.2-4360 of the VPPA.

ACCEPTANCE OF BID (VPPA 2.2-4337)

The bids received shall be open to acceptance and is irrevocable for **sixty (60) days** from the Bid Closing date.

If the bid is accepted by the Town within the period specified above, the Contractor shall provide a certificate of insurance, Payment bond, and Performance Bond within 10 days of the Notice of Award or Notice of Intent to Award. Each bond, the Performance Bond and the Payment Bond, shall be in the amount of 100% of the Contract Amount. The bonds shall be corporate surety bonds issued by a surety company authorized to do business in the Commonwealth of Virginia and acceptable to the Town. The Performance Bond will be conditioned upon the faithful performance of all of the work shown, described and required in the Contract Documents. The Payment Bond will be conditioned upon the payment of all persons who have and fulfill contracts for the Contractor for providing labor, equipment of material in the performance of the work provided for in the Contract Documents.

If this bid is accepted within the time stated, and the Contractor fails to provide the required Bonds, or commence the project as directed, the security deposit shall be forfeited as damages to the Town by reason or failure, limited in amount to the lesser of the face value of the security deposit or the difference between this Bid and the Bid upon which the Contract is signed.

SCC IDENTIFICATION NUMBER (VPPA SECTION 2.2-4311.2)

Every Bidder must include their State Corporation Commission (SCC) Identification Number or reason for exemption with his/her bid. If this information is not included, the Bid may be rejected.

VIRGINIA CONTRACTOR'S LICENSE NUMBER (CODE OF VIRGINIA §54.1-1115, A1 AND A6)

Bidder certifies that he/she is properly registered as a licensed Contractor under Title 54 of the Code of Virginia. Bidder shall provide his/her Virginia Contractor's License Number in the designated location on the Bid Response Form or the Bid may be rejected.

STIPULATED PRICES

The term "STIPULATED PRICE ITEM" means and includes an item of Work, unanticipated at the time of issuance of the solicitation for a Bid and determined to be executed, based on the actual field conditions during the progress of Work under the contract, mutually by the Engineer and the Contractor. The Unit Price for the "STIPULATED PRICE ITEM", as identified in the

“Stipulated Price Items” section of the Bid Form, is predetermined by the Town as the current reasonably workable rate for the Item inclusive of all necessary labor, equipment, materials, overhead (provision and installation), and the Contractor’s profit. Work on the “STIPULATED PRICE ITEM” shall be carried out either at the written request of the Contractor followed by a written approval by the Engineer or at the written order by the ENGINEER to the Contractor. The payment for a “STIPULATED PRICE ITEM” shall be made by the Town to the Contractor at the related Unit Price specified in the ‘Stipulated Price Items’ section of the Bid Form on the same basis as the payment for any other regular Bid Item.

COMPENSATION AND PAYMENT

Payments are due and payable forty-five (45) days from the date of the Contractor’s invoice. Amounts unpaid sixty (60) days after the invoice date shall bear interest at the base rate on corporate loans (prime rate) at large United States money center commercial banks as reported daily in the Publication entitled The Wall Street Journal.

COORDINATION WITH UTILITIES

The Contractor shall coordinate the work of his forces with the utility companies during the contract to ensure the continuing progress of all work to be performed within the project area.

The Contractor shall notify “MISS UTILITY” at 1-800-552-7001, 72 hours prior to beginning construction.

It shall be the responsibility of the Contractor to notify operators who maintain underground utility lines in the area of proposed excavation or blasting at least five (5) business days prior to any construction, subsequent maintenance or repair.

The Contractor shall dig test holes over all existing utilities prior to construction to determine their exact location and shall notify the construction manager of any necessity for redesign.

CONTRACT TIME

Substantial Completion:	Ninety (90) calendar days from Notice to Proceed
Final Completion:	Fifteen (15) calendar days from Substantial Completion
Liquidated Damages:	Five Hundred Dollars and Zero Cents (\$500.00) per day

TREES

In the event that a tree is injured or damaged, the Contractor should contact the Town’s inspector immediately.

CONTRACT ITEMS OF WORK

Work Hour Restrictions: Work hours will be 9:00 p.m. to 7:00 a.m. Sunday night through Thursday night. The Town must approve any other work time.

Traffic Control Plans: Traffic control plans must be prepared in accordance with the latest editions of Federal Highway Administration *Manual on Uniform Traffic Control Devices* and the Virginia Department of Transportation *Work Area Protection Manual*. The traffic control plan must include all signing (including variable message signing), lighting, and flaggers necessary to provide a safe work zone. The Contractor shall submit the traffic control plan as part of the Town Right of Way Permit application.

Traffic Lanes: All traffic lanes affected by construction shall be opened to traffic at the conclusion of each work day except where detours have been established.

Private Entrances and Driveways: The Contractor shall maintain continuous access to commercial buildings and minimize the duration of any blockage to private entrances and driveways. The affected property owner shall be notified a minimum of 24 hours in advance of such activities and the Contractor shall make all private entrances and driveways accessible at the conclusion of each work day.

Construction Survey: This item is to include all survey and layout required to build the project.

Pre-survey and Post-survey of Buildings Structures and Walls: A thorough structural inspection will be required for buildings and structures within the limits of construction to document existing and post construction conditions. The inspection will include the foundation, walls, interior and exterior, etc.

Utility Trenches: Haul-off excavation material shall be incidental to work items and Contractor shall include its cost in relevant pay items. The utility trenches shall be backfilled to the level of the roadway at the end of each work day, except in the location where steel plates will be used. At no time should the trench be left with exposed stone as the driving surface for longer than three (3) calendar days, or over a weekend. The trench is to be capped with hot mix asphalt within the stipulated time frame.

Storm Drainage: All storm drainage installed in paved areas shall be backfilled utilizing 21-A material, from the top of the bedding material used for the pipe to the sub-grade elevation. Storm drainage installed under sidewalks or grass areas shall be backfilled in accordance with the Town of Leesburg DCSM, and/or VDOT specifications, whichever is most stringent.

Waterline: Payment for this line item shall include all necessary tracer wire, marking tape, and appurtenances needed to have a functional waterline. Backfill material shall be VDOT 21-A, and is to be compacted in 8" lifts from the bedding material to subgrade elevation. Removal of existing fire hydrants, valves, valve boxes with covers, and waterlines, if encountered, shall be considered incidental to all other items of work. Abandon existing waterline in place including caps or bulkheads to close the system. All waterline work shall be in accordance with the Town of

Leesburg DCSM.

All water line salvageable materials shall be returned to the Town's maintenance yard at 1385 Russell Branch Parkway, SE Leesburg, VA 20175.

Waterline Connection(s): Prior to any waterline connections, the Contractor shall set up a meeting with the Town's project manager to review the proposed schedule for the connections, and must obtain approval for the time of connection and duration of any potential interruption in water service to residents and/or businesses.

Hydrant Meter: The Contractor is required to obtain a fire hydrant meter from Town's Utility Department to be used for withdrawing water during construction. Any illegal hookup to a fire hydrant will result in a \$1,000 fine for the first offense and a \$2,500 fine for each subsequent offense on the same job.

Temporary paving-cold mix: Temporary paving cold mix and the installation of cold mix shall be considered incidental to all other line items of work and not compensable.

Damage to Existing Fence: In the event that a fence is damaged by the Contractor, the Contractor shall replace in kind at no additional cost to the Town.

Steel Plates: Steel plating shall be considered incidental to all other line items of work and not compensable. The Contractor may use steel plates in accordance with the Manual on Uniform Traffic Control Devices (MUTCD) to cover excavation and allow flow of traffic only when utility work is not underway and when approved by the Town of Leesburg Public Works Department and the Project Manager. Steel plating is not permitted during snow season plowing events.

Rock Excavation:

- Mass excavation is defined as any material which cannot be dislodged by a D-8 Caterpillar tractor, or equivalent, equipped with hydraulically operated, single tooth power ripper without the use of hoe-ramming or blasting.
- Trench excavation is defined as any material which cannot be dislodged by a Caterpillar 330 hydraulic backhoe or equivalent.

Testing: Third party testing is required for all soil compaction and concrete. The Contractor is responsible for the cost of this testing as an incidental to the appropriate line items in the contract.

Trash and Recycling: The Contractor is responsible for proper disposal of generated waste, trash, and/or debris or other materials generated by the work. The Contractor shall be responsible to clean up all work areas at the end of each day and shall ensure all trash and construction debris is removed off site and properly disposed of. The Contractor shall reimburse the Owner for cleanup of any trash or debris left on site by the Contractor after the work is complete.

As-Built Drawings: As per Article 4.13 and DCSM requirements.

Staging Area: Liberty Parking Lot (see below)



MAINTENANCE OF TRAFFIC

The Contractor shall conduct its operations in a manner that will ensure that traffic will be uninterrupted except as approved by the Town. At the close of each workday, the Contractor shall make all private entrances and driveways accessible. The Contractor shall make provisions to maintain a safe area for pedestrian traffic at all times during the project. No excavation shall remain open within the roadway without the approval of the Town except when the excavation can be safely bridged with the use of steel plates or other materials acceptable to the Town. When areas of excavation outside of the roadway do remain open, the area shall be barricaded and warning signs shall be posted.

At all times the Contractor shall use the personnel and traffic control signs and devices necessary to comply with Part VI of the "National Manual on Uniform Traffic Control Devices". During the progress of the work when the street may be obstructed to any extent by construction equipment or construction operations, in addition to the signs and barricades, special workers, equipped with VDOT required "STOP/SLOW" double-sided traffic control paddles, shall be designated by the Contractor to direct traffic. These workers so designated shall not be assigned to any other duties while engaged in directing traffic. The workers assigned to the flagging duties shall be VDOT-certified. The Contractor has sole responsibility for ensuring that its operations are conducted in a safe manner and notwithstanding any other provision to the contrary, shall fully indemnify the Town of Leesburg, its officers, agents and employees for any

damage or injury related to traffic operations which is caused by negligent or otherwise improper or deficient performance under the Contract or nonperformance of the terms of the Contract.

1. All personnel, signs, barricades and any other items necessary for the maintenance of traffic and safety shall be provided by the Contractor. This item is to be considered incidental to all other items of work.
2. The Contractor will not be permitted to work on the following holidays:
 - Annual Flower and Garden Show
 - Memorial Day
 - Juneteenth Day
 - Independence Day
 - Labor Day
 - Columbus Day
 - Veterans Day
 - Thanksgiving
 - Day after Thanksgiving
 - Christmas Day
 - Day after Christmas
 - New Year’s Day
 - Downtown Leesburg Events (See Table 1 below)

TABLE – 1 (Downtown Leesburg Events)

Event Dates*	Location and Impact of Event	Event	Restoration needed for Construction happening in Market/King Intersection* (see Notes below)
Saturday and Sunday, April 16 & 17	Market and King Closure all weekend	Flower and Garden Show	Remove plates, hot mix asphalt, reestablish handicap ramps. Asphalt sidewalk and curb acceptable. Eliminate all trip hazards.
Monday, July 4	King Closure for Parade	Parade and Fireworks	Eliminate all trip hazards. Plates must be removed and smooth asphalt installed.
Saturday, August 13	Market, King, Cornwall Closure	TASTE Leesburg	Eliminate all trip hazards. Plates can remain unless wet weather is forecasted
Friday, August 19	King Closure for Parade	America's 9/11 Ride	Eliminate all trip hazards Plates can remain unless wet weather is forecasted
1st Friday of each Month	No road Closure but lots of people on sidewalks	1st Friday each Month	Eliminate all trip hazards. Plates can remain unless wet weather is forecasted

Notes:

- * Dates are tentative based on previous years. Confirmation of dates will be provided at time of preconstruction meeting.
- * Restoration work must be completed by the end of the Thursday night work night.
- * Work may recommence on Monday night if the event occurs on Sunday. If work does not recommence within 2 weeks of the event, final restoration of the entire work area must be completed.

3. Work hours on the project will be limited to 9:00 p.m. to 7:00 a.m., Sunday through Thursday. Weekend work will not be allowed without written permission from the Project

Manager.

4. The Contractor is required to submit a Maintenance of Traffic Plan for review and approval. Approval of the Maintenance of Traffic Plan is required prior to beginning any construction activities on the project. **The Contractor shall submit for Town review and approval a Vehicular and Pedestrian Maintenance of Traffic Plans as part of the required Right-of-Way permit issued by the Town of Leesburg.**

END OF SECTION

TREE PROTECTION SPECIFICATIONS

SITE CLEARING, DEMOLITION

The following work must be accomplished before any demolition or site-clearing activity occurs within 100 feet of the tree(s) to be saved.

1. The site Contractor is required to meet with the Town Urban Forester at the site prior to beginning work to review all work procedures, access and haul routes, and tree protection measures.
2. The limits of all tree protection zones shall be staked in the field.
3. Tree(s) to be removed that have branches extending into the canopy of tree(s) to remain must be removed by a qualified arborist and not by demolition or construction contractors. A qualified arborist shall remove the tree in a manner that causes no damage to the tree(s) and understory to remain.
4. Any brush clearing required within the tree protection zone shall be accomplished with hand-operated equipment.
5. Trees to be removed shall be felled so as to fall away from tree protection zones and to avoid pulling and breaking of roots of trees to remain. If roots are entwined, the Town Urban Forester may require first severing the major woody root mass before extracting the trees. This may be accomplished by cutting through the roots by hand, with a vibrating knife, rock saw, narrow trencher with sharp blades, and other approved root-pruning equipment.
6. Trees to be removed from within the tree protection zone shall be removed by a qualified arborist. The trees shall be cut near ground level and the stump ground out.
7. All downed brush and trees shall be removed from the tree protection zone either by hand or with equipment sitting outside the tree protection zone. Extraction shall occur by lifting the material out, not by skidding it across the ground.
8. Brush shall be chipped and placed in the tree protection zone to a maximum depth of 6 inches leaving the trunk clear of mulch.
9. Structures and underground features to be removed within the tree protection zone shall use the smallest equipment possible, and operate from outside the tree protection zone. The Town Urban Forester shall be on site during all operations within the tree protection zone to monitor demolition activity.
10. All trees shall be pruned in accordance with the provided Pruning Specifications.

11. A 4-foot high, welded wire fence with steel T-posts shall be erected to enclose the tree protection zone.
12. Any damage to trees due to demolition activities, shall be reported to the Town Urban Forester within 6-hours so that remedial action can be taken. Timeliness is critical to tree health.
13. If temporary haul or access roads must pass over the root area of trees to be retained, a road bed of 6 inches of mulch with ½ inch sheets of plywood on top shall be created to protect the soil. The roadbed material shall be replenished as necessary to maintain a 6-inch depth.

PRUNING SPECIFICATIONS

1. Specifications for individual trees, indicated by tree identification number, and describing which branches should be pruned and how, may be needed. Also consider requirements for crown reduction and crown raising where structures will be close to trees.
2. All trees within the project area shall be pruned to:
 - 2.1 Clear the crown of diseased, crossing, weak, and dead wood to a minimum size of 1-inch diameter;
 - 2.2 Provide 14 feet of vertical clearance over streets and 8 feet of vertical clearance over sidewalks;
 - 2.3 Remove stubs, cutting outside the wound wood tissue that has formed around the branch;
 - 2.4 Reduce end weight on heavy, horizontal branches by selectively removing small diameter branches, no greater than 2 to 3 inches, near the ends of the scaffolds.
 - 2.5 Where temporary clearance is needed for access, branches shall be tied back to hold them out of the clearance zone.
 - 2.6 Pruning shall not be performed during periods of flight of adult boring insects because fresh wounds attract pests. Pruning shall be performed only when the danger of infestation is past.
 - 2.7 A qualified arborist shall perform all pruning.
 - 2.8 All pruning shall be in accordance with the International Society of Arboriculture Tree-Pruning Guidelines and/or the ANSI A300 Pruning Standard (American National Standard for Tree Care Operations) and adhere to the most recent edition of ANSI Z133.1.

- 2.9 Interior branches shall not be stripped out.
- 3.0 Pruning cuts larger than 4 inches in diameter, except for dead wood, shall be avoided.
- 3.1 Pruning cuts that expose heartwood shall be avoided whenever possible.
- 3.2 No more than 20 percent of live foliage shall be removed within the trees.
- 3.3 While in the tree, the arborist shall perform an aerial inspection to identify defects that require treatment. Any additional work needed shall be reported to the Town Urban Forester.
- 3.4 Brush shall be chipped and chips shall be spread underneath trees within the tree protection zone to a maximum depth of 6 inches leaving the trunk clear of mulch.

CONSTRUCTION SPECIFICATIONS

1. Fences have been erected to protect trees to be preserved. Fences define a specific protection zone for each tree or group of trees. Fences are to remain until all site work has been completed. Fences may not be relocated or removed without the written permission of the Town Urban Forester.
2. Construction trailers and traffic and storage areas must remain outside fenced areas at all times.
3. All underground utilities and drain or irrigation lines shall be routed outside the tree protection zone. If lines must traverse the protection area, they shall be tunneled or bored under the tree(s).
4. No materials, equipment, spoil, or waste or washout water may be deposited, stored, or parked within the tree protection zone (fenced area).
5. Additional tree pruning required for clearance during construction must be performed by a qualified arborist and not by construction personnel.
6. Any herbicides placed under paving materials must be safe for use around trees and labeled for that use. Any pesticides used on site must be tree-safe and not easily transported by water.
7. If injury should occur to any retained tree during construction, it shall be reported to the Town Urban Forester within 6-hours so that remedial action can be taken.
8. All trees shall be irrigated. Each irrigation event shall wet the soil within the tree protection zone to a depth of 12 inches.

9. Erosion control devices such as silt fencing, debris basins, and water diversion structures shall be installed to prevent siltation and/or erosion within the tree protection zone.
10. Before grading, pad preparation, or excavation for foundations, footings, walls, or trenching, trees shall be root pruned 1 foot outside the tree protection zone by cutting all roots cleanly to a depth of 24 inches. Roots shall be cut by manually digging a trench and cutting exposed 1" roots with a saw, vibrating knife, rock saw, narrow trencher with sharp blades or other approved root-pruning equipment.
11. Any roots damaged during grading or construction shall be exposed to sound tissue and cut cleanly with a saw.
12. If temporary haul or access roads must pass over the root area of trees to be retained, a roadbed of 6 inches of mulch with ½ plywood over the mulch shall be created to protect the soil. The roadbed material shall be replenished as necessary to maintain a 6-inch depth.
13. Spoil from trenches, basements, or other excavations shall not be placed within the tree protection zone, either temporarily or permanently.
14. No burn piles or debris pits shall be placed within the tree protection zone. No ashes, debris, or garbage may be dumped or buried within the tree protection zone.
15. Maintain fire-safe areas around fenced areas. Also, no heat sources, flames, ignition sources, or smoking is allowed near mulch or trees.

END OF SECTION

SAMPLE AGREEMENT

THIS AGREEMENT, dated this ____ day of _____, 20__ is between the Town of Leesburg (hereinafter called "TOWN" or "Owner") and _____ (hereinafter called "CONTRACTOR"). TOWN AND CONTRACTOR, in consideration of the mutual covenants hereinafter set forth, agree as follows:

1. **WORK**

1.1 The project's name is _____, project # _____.

1.2 CONTRACTOR shall complete all Work as specified or indicated in the Contract Documents. The Work is generally described as follows:

The project includes _____
_____.

2. **OWNER'S REPRESENTATIVES**

2.1 All references to the Owner's Chief Procurement Officer shall mean: _____.

2.2 All references to the Owner's Project Manager or ENGINEER shall mean: _____, who shall have the sole responsibility for clarifying any ambiguities.

3. **CONTRACT TIME AND LIQUIDATED DAMAGES**

3.1 Time of the Essence

A. All time limits for Interim Completion, Milestones, Substantial Completion, and Final Completion as stated in the Contract Documents are of the essence of the Contract.

B. Contract Time:

a. The Work to be performed under this Contract shall be commenced after issuance of the Notice to Proceed and Substantial Completion shall be achieved within _____ calendar days.

b. Final Completion shall be achieved within _____ calendar days.

c. [Insert Interim or Milestone dates as appropriate.]

3.2 Liquidated Damages

A. TOWN and CONTRACTOR recognize that time is of the essence of this Agreement and the TOWN will suffer financial loss if the Work is not completed within the time specified in Paragraph 3.1 above, plus any extensions thereof allowed in accordance with the General Conditions, Article 8, "TIME." Contractor recognizes the delays, expense, and difficulties involved in proving in a legal or other dispute resolution proceeding the actual loss suffered by TOWN if the Work is not completed on time. Accordingly, instead of requiring any such proof, TOWN and CONTRACTOR agree that as liquidated damages for delay, but not as a penalty, CONTRACTOR shall pay the TOWN as follows:

- a. For each day that expires after the time established to achieve Substantial Completion as specified above, CONTRACTOR shall pay TOWN liquidated damages in the amount of \$_____.
- b. For each day that expires after the time established to achieve Final Completion as specified above, CONTRACTOR shall pay TOWN liquidated damages in the amount of \$_____.
- c. [Insert liquidated damage rate for and Interim or Milestone dates.]

B. CONTRACTOR hereby waives any defense as to the validity of any liquidated damages stated in this Agreement as they may appear on the ground that such liquidated damages are void as penalties or are not reasonably related to actual damages.

C. TOWN may recover liquidated damages by deducting the amount owed from progress payments, final payment or retainage.

4. **CONTRACT PRICE**

4.1. ***[If Fixed Price]*** In consideration of the Performance of the Contract, the Owner agrees to pay the Contractor as compensation for his services the firm, fixed price of: _____ Dollars and _____ Cents (\$_____).

4.2. ***[If Unit Price]*** In consideration of the Performance of the Contract, the Owner agrees to pay the Contractor as compensation for his services in accordance with the Bid Form and Contract Documents, which are included as Exhibits to this Agreement, an amount equal to the sum of the itemized prices as shown for each item of work multiplied by the actual quantity of each item completed:

A. Total Computed Price used for Comparison and Award:

(Words)

\$ _____
(Figures)

All specific cash allowances are included in the above price and have been computed to include the Contractors profit, overhead, all furnishing and installation charges.

This is a unit price contract and the estimated quantities are not guaranteed and are given only as a basis of calculation for comparing and awarding the project. The determinations of actual quantities and classifications are to be made by Project Manager, as provided in the General Conditions, Article 9. The Total Computed Price used for Comparison and Award will be deemed to include for all Unit Price Work an amount equal to the sum of the unit price for each separately defined item times the estimated quantity for each item as indicated on the bid form. Notwithstanding the language of this paragraph, the contract price shall not exceed \$ _____ without further authorization.

5. **INTEREST**

- 5.1 The TOWN will pay on all amounts owed to the CONTRACTOR accordance with Sections 2.2-4354 and 2.2-4355 of the Virginia Public Procurement Act.
- 5.2 The rate of interest charged shall be the base rate on corporate loans (prime rate) at large United States money center commercial banks as reported daily in the publication entitled The Wall Street Journal. Whenever a split prime rate is published, the lower of the two rates shall be used.

6. **CONTRACT DOCUMENTS**

- 6.1 The Contract Documents which comprise the entire Agreement between TOWN and CONTRACTOR concerning the Work are defined as follows:
 - A. The body of this Agreement;
 - B. Payment Bond (attached);
 - C. Performance Bond (attached);
 - D. Insurance Certificate (attached);
 - E. CONTRACTOR'S Bid (attached);
 - F. Bidding Documents (by reference) including:
 - 1. Advertisement for Bids;

2. Instructions to Bidders;
3. General Conditions;
4. Specifications;
5. Supplemental Specifications;
6. Construction Drawings prepared by _____ bearing the following title:
 - _____(Sheets ___ through ___) approved

7. Addenda

G. Deliverables issued on or after the effective date of the Agreement and are not attached hereto:

1. Notice to Proceed
2. Written Amendments
3. Work Change Directives
4. Change Orders

7. **NOTICE**

The term "Notice" as used herein shall mean and include written notice. Any legal notice by any party shall be deemed to have been duly given if either delivered personally or enclosed in a certified mail, postage paid envelope addressed to:

The Owner:

The Owner's Project Manager:

The Contractor:

IN WITNESS WHEREOF, TOWN and CONTRACTOR have signed two copies of this Agreement. All portions of the Contract Documents have been signed or identified by TOWN and CONTRACTOR.

OWNER
TOWN OF LEESBURG
25 West Market Street
Leesburg, VA 20176

CONTRACTOR

By _____
Town Manager

By _____
President

Date _____

Date _____

License No: _____

[CORPORATE SEAL]

Approved as to Form:

Town Attorney

Resolution authorizing execution of Agreement is attached hereto.

Agent for service of process:

(If CONTRACTOR is a corporation attach evidence of authority to sign.)

VIRGINIA PAYMENT BOND

BOND NO. _____

AMOUNT: \$ _____

KNOW ALL MEN BY THESE PRESENTS, that _____
of _____ hereinafter called the CONTRACTOR
(Principal), and _____

a corporation duly organized and existing under and by virtue of the laws of the State
of _____, hereinafter called the SURETY, and authorized to
transact business within the Commonwealth of Virginia, as SURETY, are held and firmly bound
unto The Town of Leesburg as OWNER (Obligee), in the sum of:

_____ DOLLARS (\$ _____), lawful money
of the United States of America, for the payment of which, well and truly be made to the
OWNER. The CONTRACTOR and the SURETY bind themselves and each of their heirs,
executors, administrators, successors, and assigns, jointly and severally, firmly by these presents
as follows:

THE CONDITION OF THE ABOVE OBLIGATION IS SUCH THAT:

WHEREAS, the CONTRACTOR has executed and entered into a certain Contract hereto
attached with _____, naming the OWNER as beneficiary, dated this
_____ day of _____, 20 _____,
for: _____

NOW, THEREFORE, the CONTRACTOR shall promptly make payment to all persons, firms,
subcontractors, and corporations furnishing materials for or performing labor in the prosecution
of the work provided for in the Contract, and any authorized extension or modification thereof,
including all amounts due for materials, lubricants, oil, gasoline, coal and coke, repairs on
machinery, equipment, and tools consumed or used in connection with the construction of the
work, and all insurance premiums on the work, and for all labor performed in the work, whether
by subcontractor or otherwise, then this obligation shall be void; otherwise to remain in full force
and effect.

Furthermore, the SURETY, for value received, hereby stipulates and agrees that no change,
extension of time, alteration, or addition to the terms of the Contract Documents or to the work to
be performed there under, or the Specifications accompanying the same, shall in any way affect
its obligation on this bond, and it does hereby waive notice of any such change, extension of
time, alteration, or addition to the terms of the Contract Documents.

PROVIDED, FURTHER that no final settlement between the OWNER and the CONTRACTOR shall abridge the right of any beneficiary hereunder, whose claim may be unsatisfied.

IN WITNESS WHEREOF, the above parties bounded together have executed this instrument this _____ day of _____, 20____, the name and corporate seal of each corporate party being hereto affixed and those presents duly signed by its undersigned representative, pursuant to authority of its governing body.

CONTRACTOR

By _____(Seal)

Attest

SURETY

By _____(Seal)

Attest

NOTE: Date of bond must not be prior to date of Contract. If CONTRACTOR is a partnership, all partners should execute bond.

IMPORTANT: The SURETY named on this bond shall be one who is licensed to conduct business in the Commonwealth of Virginia, and named in the current list of Companies Holding Certificates of Authority as Acceptable Sureties on Federal Bonds and as Acceptable Reinsuring Companies, as published in Circular 570 (amended) by the Audit Staff Bureau of Accounts, U.S. Treasury Department. All bonds signed by an agent must be accompanied by a certified copy of the authority to act for the SURETY at the time of the signing of this bond.

VIRGINIA PERFORMANCE BOND

BOND NO. _____

AMOUNT: \$_____

KNOW ALL MEN BY THESE PRESENTS, that _____

of _____

hereinafter called the CONTRACTOR (Principal), and _____

_____ a corporation duly organized and existing under and by virtue of the laws of the State of _____, hereinafter called the SURETY, and authorized to transact business within the Commonwealth of Virginia, as SURETY, are held and firmly bound unto The Town of Leesburg as OWNER (Obligee), in the sum of:

_____ DOLLARS (\$ _____), lawful money of the United States of America, for the payment of which, well and truly be made to the OWNER. The CONTRACTOR and the SURETY bind themselves and each of their heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents as follows:

THE CONDITION OF THE ABOVE OBLIGATION IS SUCH THAT:

WHEREAS, the CONTRACTOR has executed and entered into a certain Contract hereto attached with _____, naming the OWNER as beneficiary, dated this _____ day of _____, 20 _____,

for: _____

NOW, THEREFORE, the CONTRACTOR shall at all times duly, promptly, and faithfully perform the Contract and any alteration in or addition to the obligations of the CONTRACTOR arising there under, including the matter of infringement, if any, of patents or other proprietary rights, and shall assure all guarantees against defective workmanship and materials, including the guarantee period following final completion by the CONTRACTOR and final acceptance by the OWNER and comply with all covenants therein contained in the Specifications, Drawings, and other Documents constituting a part of the Contract required to be performed by the CONTRACTOR, in the manner and within the times provided in the Contract, and shall fully indemnify and save harmless the OWNER from all cost and damage which it may suffer by reason or failure so to do, and shall fully reimburse and repay it all outlay and expenses which it may incur in making good any default, and reasonable counsel fees incurred in the prosecution of

or defense of any action arising out of or in connection with any such default, then this obligation shall be void; otherwise to remain in full force and effect.

Furthermore, the SURETY, for value received, hereby stipulates and agrees that no change, extension of time, alteration, or addition to the terms of the Contract Documents or to the work to be performed there under, shall in any way affect its obligation on this bond, and it does hereby waive notice of any such change, extension of time, alteration, or addition to the terms of the Contract Documents.

PROVIDED, FURTHER that no final settlement between the OWNER and the CONTRACTOR shall abridge the right of any beneficiary hereunder, whose claim may be unsatisfied.

IN WITNESS WHEREOF, the above parties bounded together have executed this instrument this _____ day of _____, 20____, the name and corporate seal of each corporate party being hereto affixed and those presents duly signed by its undersigned representative, pursuant to authority of its governing body.

CONTRACTOR

Attest

By _____(Seal)

SURETY

Attest

By _____(Seal)

NOTE: Date of bond must not be prior to date of Contract. If CONTRACTOR is a partnership, all partners should execute bond.

IMPORTANT: The SURETY named on this bond shall be one who is licensed to conduct business in the Commonwealth of Virginia, and named in the current list of Companies Holding Certificates of Authority as Acceptable Sureties on Federal Bonds and as Acceptable Reinsuring Companies, as published in Circular 570 (amended) by the Audit Staff Bureau of Accounts, U.S. Treasury Department. All bonds signed by an agent must be accompanied by a certified copy of the authority to act for the SURETY at the time of the signing of this bond.

THE TOWN OF LEESBURG

GENERAL CONDITIONS

Project Name:

MARKET STREET AND KING STREET
INTERSECTION IMPROVEMENTS

IFB No. : 17016-FY22-11

GENERAL CONDITIONS

THE TOWN OF LEESBURG

GENERAL CONDITIONS

ARTICLE 1: CONTRACT DOCUMENTS

1.1 DEFINITIONS

1.1.1 The Contract Documents

The Contract Documents consist of the Advertisement or Invitation for Bids, Request for Proposals, Information for Bidders, Insurance Certificates, Official Bid Form, Offeror's Bid or Proposal, Bonds, the Notice of Award, the Project Manual, the Owner/Contractor Agreement, the General and Special Conditions, the Drawings, the Specifications, all Addenda issued prior to and all Modifications issued after execution of the Agreement. A Modification is either a written Change Order issued pursuant to the provisions of Article 12.5, or a Field Order issued pursuant to Article 12.2.

1.1.2 The Contract

The Contract is the sum of all the Contract Documents. This Contract represents the entire and integrated agreement between the Owner and the Contractor and supersedes all prior negotiations, representations, or agreements, either written or oral. The Contract may be changed only by a Modification as defined in Article 1.1.1.

1.1.3 The Work

The Work comprises the completed construction required by the Contract Documents and includes all labor, material, equipment, supplies and other facilities or things necessary to produce such construction, and all materials, equipment and supplies incorporated or to be incorporated in such construction.

1.1.4 The Project

The Project is the total construction of which the Work performed under the Contract Documents may be the whole or a part.

1.1.5 Furnish, Install, Provide

The terms "Furnish", "Install" or "Provide," unless specifically limited in context, mean: furnishing and incorporating a specified item, product or material in the Work, including all labor, materials, and equipment necessary to perform the Work required, ready for intended use.

1.1.6 Firm, Fixed Price or Lump Sum

The terms "Firm, Fixed Price" or "Lump Sum" mean that the Contract Work shall be performed for the price stated in the Contract without any adjustment based on

GENERAL CONDITIONS

the Contractor's actual costs unless such adjustment is made by a properly executed Contract Change or Modification.

1.1.7 Schedule of Values

The term "Schedule of Values" means the unit prices for portions of the Work submitted by the Contractor and approved by the Owner's Project Manager for use in preparing Applications for Payment and pricing Contract Changes in accordance with Article 9.2. The Schedule of Values shall not alter the Firm, Fixed Price or Lump Sum value of the Contract.

1.1.8 Miscellaneous Words or Terms

Whenever they refer to the Work or its performance, "Directed," "Required," "Permitted," "Ordered," "Designated," "Prescribed," and words of like import shall imply the direction, requirements, permission, order, designation or prescription of the Owner and/or the Owner's Project Manager, and "Approved," "Acceptable," "Satisfactory," "in the judgment of," and words of like import shall mean approved by or acceptable to or satisfactory to or in the judgment of the Owner and/or the Owner's Project Manager. "Approved" means approved in writing, including subsequent written confirmation of prior oral approval and "Approval" means approval in writing, including all aforesaid.

1.2 EXECUTION, CORRELATION AND INTENT

1.2.1 The Contract Documents may be signed in duplicate originals by the Owner and the Contractor and each set shall be deemed an original, but all sets shall constitute one and the same instrument.

1.2.2 By executing the Contract, the Contractor represents that he has familiarized himself with, and assumes full responsibility for having familiarized himself with, the nature and extent of the Contract Documents, Work, locality, and with all local conditions and federal, state and local laws, ordinances, rules and regulations that may in any manner affect performance of the Work, and represents that his study and observations have been correlated with the requirements of the Contract Documents. The Contractor also represents that he has studied all surveys and investigation reports of subsurface and latent physical conditions referred to in the Contract Documents and made such additional surveys and investigations as he deems necessary for the performance of the Work at the Contract Price in accordance with the requirements of the Contract Documents and that he has correlated the results of all such data with the requirements of the Contract Documents. Failure to make an examination necessary for this determination shall not release the Contractor from the obligations of this Contract nor be grounds for any claim based upon unforeseen conditions.

GENERAL CONDITIONS

The Owner assumes no responsibility for any conclusions or interpretations made by the Contractor based on the information made available by the Owner. The Owner assumes no responsibility for any understanding reached or representation made concerning conditions that can affect the Work by any of its officers or agents before the execution of this contract, unless that understanding or representation is expressly stated in this contract.

- 1.2.3** The intent of the Contract Documents is to include all items necessary for the proper execution and completion of the Work. The Contract Documents are complementary, and what is required by any one shall be as binding as if required by all. Should any work or material be required which is not denoted in the drawings and specifications either directly or indirectly, but which is nevertheless necessary for the proper carrying out of the intent thereof, it is understood and agreed that the same is implied and required and that the Contractor shall perform such work and furnish such materials as fully as if they were completely delineated and prescribed.

Words and abbreviations which have well-known technical or trade meanings are used in the Contract Documents in accordance with such recognized meanings unless otherwise specifically defined herein. The Table of Articles, titles, headings, and running headlines are solely to facilitate reference to various provisions of the Contract Documents and in no way affect, limit or cast light upon the interpretation of the provisions to which they refer.

- 1.2.4** The organization of the specifications into divisions, sections and articles, and the arrangement of drawings are for clarity only, and shall not control the Contractor in dividing the Work among Subcontractors or in establishing the extent of Work to be performed by any trade. The Contractor may subcontract the Work in such divisions as he sees fit and he is ultimately responsible for furnishing all work shown on the drawings and/or in the specifications.

- 1.2.5** Unless otherwise provided for or amended herein, work shall be performed in accordance with the VDOT Road and Bridge Specifications, current edition; the Town of Leesburg Design and Construction Standards Manual (DCSM), current edition; the Virginia Erosion and Sediment Control Handbook; and the Special Provisions, Special Conditions, and Special Designs as may be described on the plans for the project or in this solicitation. Where there is a conflict between the VDOT Road and Bridge Specifications and the DCSM, the most stringent shall take precedence. A copy of the DCSM may be purchased from the Department of Plan Review at the current standard rate.

Anything shown on the drawings and not mentioned in the specifications or mentioned in the specifications and not shown on the drawings shall have the same effect as if shown or mentioned respectively in both. Technical specifications take priority over general specifications and detail drawings take

GENERAL CONDITIONS

precedence over general drawings. Any work shown on one drawing shall be construed to be shown in all drawings and the Contractor will coordinate the Work and the drawings. If any portion of the Contract Documents shall be in conflict with any other portion, the various documents comprising the Contract Documents shall govern in the following order of precedence: The Owner/Contractor Agreement; Modifications; Changes; Addenda; the Supplementary Conditions; the General Conditions; the Specifications; the drawings; the Town DCSM; other published construction standards and specifications; the bonds; the advertisement for bids or invitation or request for proposal; information for bidders; bids; the notice of award. As between schedules and information given on drawings and the scaled measurements, the figures shall govern. As between large-scale drawings and small-scale drawings, the larger scale shall govern. Any such conflict or inconsistency between or in the drawings shall be submitted to the Project Manager whose decision thereon shall be final and conclusive.

1.2.6 This Contract is not intended to create, nor shall any provision be interpreted as creating, any contractual relationship between the Owner and any third parties including all Subcontractors.

1.2.7 The Provisions of this Contract cannot be changed, varied or waived in any respect except by a written Modification or Change Order. No person has authority to orally waive, or to release the Contractor from any of the Contractor's duties or obligations under or arising out of this Contract. Any waiver, approval or consent granted by Changes to the Contractor shall be limited to those matters specifically and expressly stated thereby to be waived, approved or consented to and shall not relieve the Contractor of the obligation to obtain any future waiver, approval or consent.

1.3 OWNERSHIP AND USE OF DOCUMENTS

1.3.1 All drawings, specifications, and copies thereof furnished by or to the Owner under this Contract are and shall remain the property of the Owner. They are to be used only with respect to this Project and are not to be used in whole or in part for any other purpose.

1.3.2 The Contractor shall be provided five sets of the Contract Documents by the Owner's Project Manager. Additional sets of Drawings and Specifications may be obtained from the Owner's Project Manager by paying the then current and regular printing, mailing and handling charges.

END OF ARTICLE 1

GENERAL CONDITIONS

ARTICLE 2: OWNER'S PROJECT MANAGER

2.1 DEFINITIONS

2.1.1 The term "Project Manager" as used in the Contract Documents, shall mean the entity so identified in the Owner/Contractor Agreement or its duly authorized representatives.

2.1.2 The Project Manager is referred to throughout the Contract Documents as if singular in number and masculine in gender.

2.2 SERVICES OF THE OWNER'S PROJECT MANAGER

2.2.1 The Owner's Project Manager will serve during construction and until the end of the warranty period. The Owner's Project Manager will advise and consult with the Owner and will have the authority to act on behalf of the Owner only to the extent provided in the Contract Documents. The Owner may identify a substitute Owner's Project Manager at any time by providing written notice to the Contractor.

2.2.2 The Owner's Project Manager will inform the Owner and the Contractor whenever in his reasonable opinion any of the Work is proceeding contrary to the requirements of the Contract Documents and will be unacceptable. Failure of the Contractor to take corrective action to make the Work conform to the Contract Documents will subject the Contractor to any and all remedies available to the Owner, including, without limitation, termination pursuant to Article 14. Such notification by the Owner's Project Manager will not be a cause for the Contractor to claim either delay of the Work or any increase in the Contract Price.

2.2.3 The Owner, the Owner's Project Manager and other government representatives shall at all times have access to the Work wherever it is in preparation or progress, to include off-site facilities of Subcontractors and suppliers at any tier. The Contractor shall provide safe facilities for such access so the Owner's Project Manager may perform his functions under the Contract Documents.

2.2.4 All communications, correspondence, submittals and documents exchanged between the Owner's Project Manager and the Contractor in connection with the Project shall be through or in the manner prescribed by the Owner and consistent with the Owner/Contractor Agreement.

2.2.5 The Owner's Project Manager shall make decisions on all matters relating to aesthetic effect, which decision shall be final.

END OF ARTICLE 2

GENERAL CONDITIONS

ARTICLE 3: OWNER

3.1 DEFINITIONS

- 3.1.1** "Owner" means the Town of Leesburg, Virginia, unless the Owner/Contractor Agreement provides otherwise. The Owner shall be referred to as the "Town," or as the "Owner."
- 3.1.2** The term "Owner" or "Owner's Project Manager" specifically excludes any and all inspectors having building code or Town ordinance responsibilities or jurisdiction under the requirements of the Building Permit, unless the Owner designates such person to serve as the Owner's Representative.
- 3.1.3** "Contractor" means the person or persons, firm or company whose bid or proposal has been accepted by the Owner and includes the Contractor's representatives, successors and assigns as permitted by the Owner.

3.2 INFORMATION, SERVICES AND RIGHTS OF THE OWNER

- 3.2.1** The Project Manager will provide administration of the Contract as described below.
- 3.2.2** The Owner or, at the Owner's sole discretion, the Owner's Project Manager or Project Manager, will review and process all Progress Payments, including the Final Payment.
- 3.2.3** The Project/Manager shall have the authority to reject the Work when, in his opinion, the Work does not conform to the Contract Documents.
- 3.2.4** Whenever in the Project Manager's reasonable opinion it is necessary or advisable for the implementation of the Contract Documents, the Project Manager will have authority to require special inspection or testing of the Work in accordance with the provisions of the Contract Documents, whether or not such Work is then fabricated, installed or completed.
- 3.2.5** The Owner or the Owner's Project Manager shall at all times have access to the Work wherever it is in preparation or progress. The Contractor shall provide safe facilities for such access.
- 3.2.6** The Owner, the Owner's Project Manager and the Engineer shall not be responsible for or have control or charge of the construction means, methods, techniques, sequences, or procedures, or for the safety precautions and programs in connection with the Work, and will not be responsible for the Contractor's failure to carry out the Work in accordance with the Contract Documents.

GENERAL CONDITIONS

- 3.2.7** The Owner or the Owner's Project Manager shall not be responsible or liable to the Contractor for the acts, errors or omissions of the Contractor, any separate Subcontractor, any separate Contractor or any Contractor's or Subcontractor's agents or employees, or any other persons performing any of the Work.
- 3.2.8** The Owner assumes no responsibility for any conclusions or interpretations made by the Contractor based on the information made available by the Owner. The Owner assumes no responsibility for any understanding reached or representation made concerning conditions that can affect the Work by any of its officers or agents before the execution of this Contract, unless that understanding or representation is expressly set forth in this Contract.
- 3.2.9** The Owner shall not be held responsible for failure to perform the duties and responsibilities imposed by the Contract if such failure is due to strikes, fires, riots, rebellions, or Force Majeure, beyond the control of the Owner, that make performance impossible or illegal, unless otherwise specified in the Contract.
- 3.2.10** The Owner will, throughout the Contract Time and any extension thereof have the right of reasonable rejection and approval of staff assigned to the project by the Contractor. If the Owner reasonably rejects staff or Subcontractors, the Contractor must provide replacement staff or Subcontractors satisfactory to the Owner in a timely manner and at no additional cost to the Owner.
- 3.2.11** The foregoing rights are in addition to other rights of the Owner enumerated herein and those provided by law.

3.3 OWNER'S RIGHT TO STOP OR TO SUSPEND WORK

- 3.3.1** If the Contractor fails to correct defective Work as required by Article 13.2 "CORRECTION OF WORK," or fails to carry out the Work or supply labor and materials in accordance with the Contract Documents, the Owner by written order may order the Contractor to stop the Work, or any portion thereof, without monetary compensation to the Contractor until the cause for such order has been eliminated.
- 3.3.2** The Owner may order the Contractor in writing to suspend, delay, or interrupt all or any part of the Work for such period of time as he may determine to be appropriate for the convenience of the Owner.
- 3.3.3** If the performance of all or any part of the Work is suspended, delayed, or interrupted by the Owner or the Owner's Project Manager for an unreasonable period of time, or by failure of either of them to act within the time specified (or if no time is specified, within a reasonable time), an adjustment increasing the time of performance of the Work shall be made. Such adjustments will be made solely for unreasonable suspension, delay, or interruption. The Contract shall be

GENERAL CONDITIONS

modified in writing accordingly. However, no claim for an extension of time shall be made under this Article 3.3.3 for any suspension, delay, or interruption pursuant to Article 3.4.1, or for which claim is provided or excluded under any other provision of this Contract.

No claim under this Article 3.3.3 shall be allowed for any claim for an extension of time required for performance, unless within twenty days after the act or failure to act involved, the Contractor submits to the Owner's Project Manager a written statement setting forth, as then practicable, the extent of such claimed time extension and unless the claim for an extension of time is submitted with supporting data within thirty days after the termination of such suspension, delay, or interruption.

3.3.4 In the event of a suspension of work or delay or interruption of work, the Contractor will and will cause his Subcontractors to protect carefully his, and their, materials and work against damage from the weather and maintain completed and uncompleted portions of the work as required by the Contract Documents. If, in the opinion of the Owner's Project Manager, any work or material shall have been damaged by reason of failure on the part of the Contractor or any of his Subcontractors to protect same, such work and materials shall be removed and replaced at the expense of the Contractor.

3.3.5 No claim by the Contractor under Article 3.3.3 shall be allowed if asserted after Final Payment under this Contract.

3.4 OWNER'S RIGHT TO CARRY OUT THE WORK

3.4.1 If the Contractor defaults or neglects to carry out the Work in accordance with the Contract Documents and fails within a seven day period after receipt of written notice from the Owner to commence and continue correction of such default or neglect with diligence and promptness, the Owner may after the seven day period give the Contractor a second written notice to correct the deficiencies within a three day period. If the Contractor fails to commence and continue to correct any deficiencies within the second notice's three day period, the Owner may, without prejudice to other remedies the Owner may have, correct such deficiencies. In such a case an appropriate Change Order shall be issued pursuant to Article 12 deducting from the payments then or thereafter due the Contractor the cost of correcting such deficiencies, including compensation for services of the Owner's Project Manager, the Engineer and any other additional services made necessary by such default, neglect or failure. If the payments then or thereafter due the Contractor are not sufficient to cover such amount, the Contractor shall pay on demand the difference to the Owner.

3.4.2 The Owner will not be liable or accountable to the Contractor for the method by which the Work, or any portion thereof, performed by the Owner or by separate

GENERAL CONDITIONS

contractors pursuant to Article 3.4 is accomplished or for the price paid therefor. Notwithstanding the Owner's right to carry out a portion of the Work, maintenance and protection of the Work remains the Contractor's responsibility.

3.5 EXAMINATION OF RECORDS

3.5.1 The Owner, or any duly authorized representative, shall, until the expiration of five years after final payment hereunder, have access to and the right to examine, audit and copy any directly pertinent books, documents, as-builts, papers and records of the Contractor involving transactions related to this Contract. Any audit or examination shall occur during regular business hours and not exceed a reasonable period of time under the circumstances.

3.5.2 The Contractor further agrees to include in any subcontract for more than \$10,000 entered into as a result of this Contract, a provision to the effect that the Subcontractor agrees that the Owner or any duly authorized representative shall, until the expiration of three years after final payment under the Contract, have access to and the right to examine, audit and copy, without charge, any directly pertinent books, documents, papers and records of such contractor involved in transactions related to such subcontract, or this Contract. The term subcontract shall exclude subcontracts or purchase orders for public utility services at rates established for uniform applicability to the general public.

3.5.3 The period of access provided in Subparagraphs 3.5.1 and 3.5.2 above shall continue for all contracts and subcontracts until any appeals, litigation, or claims have been finally concluded.

3.5.4 Nothing in these General Conditions shall be deemed to modify in any manner any applicable statute of limitations.

END OF ARTICLE 3

GENERAL CONDITIONS

ARTICLE 4: CONTRACTOR

4.1 DEFINITION

4.1.1 The Contractor is the person or organization identified as such in the Owner/Contractor Agreement. The term Contractor means the Contractor or his authorized representative, who shall have authority to bind the Contractor in all matters pertinent to this Contract.

4.1.2 The Contractor is not an agent for the Owner but is an independent contractor engaged in the business of providing the services and performing the Work described in the Contract Documents.

4.2 REVIEW OF CONTRACT DOCUMENTS

4.2.1 Before submitting his bid or proposal to the Owner, and continuously after execution of the Contract, the Contractor shall carefully study and compare the Contract Documents and shall at once report to the Owner any error, inconsistency or omission he may discover, including any requirement that may be contrary to any law, ordinance, rule, regulation or order of any public authority bearing on the performance of the Work. By submitting his bid or proposal for the Contract and the Work under it, the Contractor agrees that the Contract Documents are accurate, consistent and complete. The Contractor shall perform no portion of the Work at any time without Contract Documents and, where required, approved Shop Drawings, product data, samples, mock ups or other submittals for such portion of the Work

4.3 SUPERVISION AND CONSTRUCTION PROCEDURES

4.3.1 The Contractor shall supervise and direct the Work, using his best skill and attention. He shall be solely responsible for and have control over all construction means, uses, sequences, procedures, safety precautions and programs, and coordination of all portions of the Work under the Contract.

4.3.2 The Contractor shall be responsible to the Owner for the acts and omissions of his employees, Subcontractors, Suppliers, their agents and employees, and other persons performing any of the Work and for their compliance with each and every requirement of the Contract Documents, in the same manner as if they were fully employed by the Contractor.

4.3.3 The Contractor shall not be relieved from his obligations to perform the Work in accordance with the Contract Documents either by acts, failures to act or duties of the Owner or the Owner's Project Manager in their administration of the Contract, or by inspections, tests, or approvals (or the lack thereof) required or

GENERAL CONDITIONS

performed under Article 4.4 "INSPECTION OF CONSTRUCTION" or Article 7.5 "TESTS" by persons other than the Contractor.

4.3.4 The Contractor shall employ no plant, equipment, materials, methods or persons to which the Owner or Owner's Project Manager reasonably objects.

4.3.5 The Contractor shall not remove any portion of the Work or stored materials from the site of the Work, if payment for such was requested or received from the Owner.

4.3.6 The Contractor shall at all times so conduct its work as to ensure the least possible obstruction to traffic and inconvenience to the general public and the residents in the vicinity of the Work. No road or street shall be closed to the public except with the permission of the Town Traffic Engineer and proper governmental authority. Fire hydrants on or adjacent to the Work shall be kept accessible to fire fighting equipment at all times. Temporary provisions shall be made by the Contractor to ensure the use of sidewalks and the proper functioning of all gutters, drainage inlets, drainage ditches, and irrigation ditches, which shall not be obstructed except as approved by the Owner's Project Manager.

4.3.7 When construction crosses highways, railroads, streets, or utilities under the jurisdiction of State, County, Town, or other public agency, public utility, or private entity, the Contractor shall secure written permission where necessary from the proper authority before executing such new construction. A copy of such written permission must be filed with the Owner before any work is started. The Contractor shall be required to furnish a release from the proper authority before final acceptance of the Work.

4.3.8 The Contractor shall provide and maintain such sanitary accommodations for the use of the Contractor's employees and those of its Subcontractors as may be necessary to comply with the requirements and regulations of the local and State departments of health and where additional accommodations are necessary for a reasonably sanitary activity, then such additional accommodations shall be made by the Contractor.

4.4 INSPECTION OF CONSTRUCTION

4.4.1 The Contractor shall maintain an adequate inspection system and perform such inspections as will ensure that the Work called for by this Contract conforms to Contract requirements. The Contractor shall maintain complete inspection records and make them available to the Owner and Owner's Project Manager. All work is subject to inspection and testing at all places and at all reasonable times before acceptance to ensure strict compliance with the terms of the Contract.

GENERAL CONDITIONS

4.5 CONTRACTOR'S REPRESENTATIONS

4.5.1 By entering into this Contract with the Owner, the Contractor represents and warrants the following, together with all other representations and warranties in the Contract Documents:

- .1 That he is experienced in and competent to perform the type of work required and to furnish the plant, materials, supplies or equipment to be so performed or furnished by him;
- .2 That he is financially solvent, able to pay his debts as they mature, and possessed of sufficient working capital to initiate and complete the Work and Changes required under the Contract;
- .3 That he is familiar with all laws, ordinances, permits, regulations and resolutions that may in any way affect the Work or those employed therein, including but not limited to any special laws or regulations related to contractor licenses and/or registrations for the Work or any part thereof;
- .4 That such temporary and permanent work required by the Contract Documents that is to be done by him will be satisfactorily constructed and fit for use for its intended purpose and that such construction will not injure any person, or damage any property;
- .5 That he will fully comply with all requirements of the Contract Documents;
- .6 That he will perform the Work in a skillful manner consistent with good workmanship, sound business practice, and in the most expeditious and economical manner consistent with the best interests of the Owner;
- .7 That he will furnish efficient business administration and experienced superintendence and an adequate supply of workers, equipment, tools, and materials at all times;
- .8 That he has carefully reviewed the Work required and that the Work can be planned and executed in a normal and orderly sequence and be reasonably scheduled so as to insure completion of the Work in accordance with the Contract Documents, allowing for normal and reasonably foreseeable weather, labor

GENERAL CONDITIONS

and other delays, interruptions and disruptions of the Work at the site designated;

- .9 That he will complete the Work within the Contract Time and all portions thereof within any required Contract milestones;
- .10 That his Contract Price is based upon the labor, materials, systems and equipment required by the Contract Documents, without exception;
- .11 That he does not and will not during the performance of the Contract violate the provisions of the Federal Immigration Reform and Control Act of 1986, as amended, which prohibits the employment of illegal aliens, and Federal and State employment and wage hour laws;
- .12 That he has taken steps reasonably necessary to ascertain the nature and locations of the Work of the Contract, has investigated and satisfied himself as to the general and local conditions which can affect the Work or its cost, including but not limited to: conditions bearing upon transportation, disposal, handling, and storage of materials; the availability of labor, water, electric power, and roads; uncertainties of weather, river stages, tides, or similar physical conditions at the site; the conformation and conditions of the ground; and the character of equipment and facilities needed before and during work performance;
- .13 That no employee of the Owner shall be admitted to any share or part of this Contract or to any benefit that may arise therefrom which is not available to the general public; and
- .14 That Contractor's bid or offer was made without collusion or fraud and that it has not offered or received any kickbacks or inducements from any other offeror, supplier, manufacturer, or Subcontractor and that it has not conferred on any public employee having official responsibility for this purchase any payment, loan, subscription, advance, deposit of money, services, or anything of more than nominal value, present or promised unless consideration of substantially equal or greater value was exchanged. Contractor acknowledges that this Contract incorporates by reference the Virginia Public Procurement Act, VA Code Sect. 2.2-4300 *et seq.* (VPPA), as well as any state or federal law related to ethics, conflicts of interest, or bribery, including by way of illustration and not limitation, the Virginia State and Local Government Conflict of Interests Act, the

GENERAL CONDITIONS

Virginia Governmental Frauds Act, and Articles 2 and 3 of Chapter 10 of Title 18.2 of the Virginia Code, as amended.

4.6 LABOR AND MATERIALS

4.6.1 Unless otherwise provided in the Contract Documents, the Contractor shall provide and pay for all labor, materials, equipment, supplies, tools, construction equipment and machinery, heat, utilities, transportation, and other facilities and services necessary or proper for or incidental to the execution and completion of the Work required by and in accordance with the Contract Documents and any applicable code or statute, whether specifically required by the Contract Documents, or whether their provision may reasonably be inferred as necessary to produce the intended results, whether temporary or permanent and whether or not incorporated or to be incorporated in the Work. Unless otherwise specified, all materials and equipment incorporated in the Work under the Contract shall be new. All work performed, shall be accomplished by persons qualified in the respective trades. Final Payment will not be made until the Work is so completed.

4.6.2 Whenever materials or equipment are specified or described in the Drawings or Specifications by using the name of a proprietary item or the name of a particular manufacturer, fabricator, supplier, or distributor, the naming of the item is intended to establish the type, function, and quality required. Unless the name is followed by words indicating that no substitution is permitted, materials or equipment of other manufacturers, fabricators, suppliers or distributors may be accepted by the Owner's Project Manager if sufficient information is submitted by the Contractor to allow the Owner's Project Manager to determine that the material or equipment proposed is equivalent to that name.

4.6.3 Requests for review of substitute items of material and equipment will not be accepted by the Owner's Project Manager from anyone other than the Contractor. If the Contractor wishes to furnish or use a substitute item of material or equipment, the Contractor shall make written application to the Owner's Project Manager for acceptance thereof, certifying that the proposed substitute will perform adequately the functions called for by the general design, be similar and of equal or better substance to that specified, and be suited to the same use and capable of performing the same or better function as that specified. The application shall state whether or not acceptance of the substitute for use in the Work will require a change in the drawings or specifications to adapt the design to the substitute and whether or not incorporation or use of the substitute in connection with the Work is subject to payment of a license fee or royalty. All variations of the proposed substitute from that specified shall be identified in the application and available maintenance, repair, and replacement service shall be indicated.

GENERAL CONDITIONS

4.6.4 The Contractor shall submit complete data substantiating compliance of the proposed substitution with the Contract Documents, including:

- .1 Product identification including manufacturer's name, address and phone number;
- .2 Manufacturer's literature showing complete product description, performance and test data, and all reference standards;
- .3 Samples and colors in the case of articles or products;
- .4 Name and address of similar projects on which the product was used and date of installation;
- .5 For construction methods, include a detailed description for the proposed method and drawings illustrating same;
- .6 Itemized comparison of proposed substitution with product or method specified and any cost reduction which shall benefit the Owner;
- .7 Accurate cost data on proposed substitution with product or method specified and any cost reduction which shall benefit the Owner;
- .8 All directions, specifications and recommendations by manufacturers for installation, handling, storing, adjustment and operation; and
- .9 A mock up if determined necessary by the Project Manager.

4.6.5 The Contractor shall also submit with his request for approval a sworn and notarized statement that shall include the following representations:

- .1 That he has investigated the proposed product or method and determined that it is equal or better in all respects to that specified and that it fully complies with all requirements of the Contract Documents;
- .2 That he will meet all Contract obligations with regard to the substitution;
- .3 That he will coordinate installation of accepted substitutions into the Work, making all such changes and any required schedule

GENERAL CONDITIONS

adjustment, at no additional cost to the Owner, as may be required for the Work to be complete in all respects;

- .4 He waives all claims for additional costs and additional time related to substitutions which consequently become apparent. He also agrees to hold the Owner harmless from claims for extra costs and time incurred by other Subcontractors and suppliers, or additional services which may have to be performed by the Owner's Project Manager, for changes or extra work that may, at some later date, be determined to be necessary in order for Work to function in the manner intended in the Contract Documents;
- .5 He will provide the same warranty and guarantee, and perform any work required in accordance therewith, for the substitution that is applicable to the specified item for which the substitution is requested;
- .6 Material will be installed, handled, stored, adjusted, tested, and operated in accordance with the manufacturers' recommendations and as specified in the Contract Documents;
- .7 In all cases new materials will be used unless this provision is waived by notice from the Owner or the Owner's Project Manager or unless otherwise specified in the Contract Documents;
- .8 All material and workmanship will be in every respect in accordance with that which, in the opinion of the Owner or the Owner's Project Manager, is in conformity with approved current practice;
- .9 He has provided accurate cost data on the proposed substitution in comparison with the product or method specified; and
- .10 He has taken into consideration the necessary adjustment, relocation and/or installation of public utilities in areas within the limits of this Contract. No additional compensation will be paid to the Contractor for delays to the project schedule, work interruptions, changes in construction sequences, changes in handling excavation, drainage or paving, or for changes in types of equipment used, etc., caused by complying with the provisions of this statement. The Contractor shall include activities in its initial schedule indicating the utility relocation necessary to complete the Work. Delays to the project schedule caused by untimely relocations of utilities will not be considered a compensable delay, but if supported in accordance with the

GENERAL CONDITIONS

provisions of Article 8.3, may entitle the Contractor to a non-compensable time extension. The Contractor shall assume all responsibility for coordinating with the various utility companies to verify their relocation schedules, determine the anticipated duration to complete the respective utility relocations, and to facilitate utility relocations to minimize the impact to the project schedule upon notification of being named the apparent low bidder.

- 4.6.6** The application shall also contain an itemized estimate of all costs that will result directly or indirectly from acceptance of such substitute, including costs of redesign and claims of other contractors affected by the resulting change. All of the foregoing shall be considered by the Owner's Project Manager in evaluating the proposed substitute. The Owner's Project Manager may require the Contractor to furnish at the Contractor's expense additional data about the proposed substitute. The Owner shall be the sole judge of acceptability, and no substitute shall be ordered or installed without the Owner's prior written acceptance. The Owner may require the Contractor to furnish at the Contractor's expense a special performance guarantee or other surety with respect to any substitute.
- 4.6.7** If a substitution is approved, no additional change in brand or make will be permitted unless satisfactory written evidence is presented to and approved by the Owner showing that the manufacturer cannot make scheduled delivery of the approved substituted item. Substitutions will not be considered by the Owner if:
- .1 The proposed substitution is indicated or implied on the Contractor's shop drawing or product data submittals and has not been formally submitted for approval by the Contractor in accordance with the above-stated requirement; or
 - .2 Acceptance of the proposed substitution will require substantial revisions to the Contract Document or is otherwise not acceptable to the Owner or his authorized representative.
- 4.6.8** The Contractor shall not have any right of appeal from the decision of the Project Manager rejecting any materials submittal.
- 4.6.9** Manufactured articles, material and equipment shall be applied, installed, connected, erected, used, cleaned, and conditioned as directed by the manufacturer unless herein specified to the contrary.
- 4.6.10** Any material specified by reference to the number, symbol or title of a specific standard, such as a Commercial Standard, a Federal Specification, a Trade Association Standard, or other similar standard, shall comply with the

GENERAL CONDITIONS

requirements in the latest revision of the standards or specification and any amendment or supplement, except as limited to type, class or grade, or as modified in such reference. The standard referred to, except as modified in the Specifications, shall have full force and effect as though printed in the Specifications.

- .1 Reference in the Specifications or on the Drawings to any article, device, product, material, fixture, form or type of construction by name, make or catalog number shall be interpreted as establishing a standard of quality and shall not be construed as eliminating from competition other products of equal or better quality by other manufacturers where fully suitable, as approved by the Owner's Project Manager. Applications for approval of substitutions for the specified items will be considered only upon request of the Contractor, not of individuals, trades or suppliers, and only for a specific purpose; no blanket approvals will be granted. No approval of a substitution shall be valid unless it is in written form and signed by the Owner's Project Manager.
- .2 If any proposed substitution will affect a correlated function, adjacent construction or the work of other contractors, then the necessary changes and modifications to the affected work shall be considered as an essential part of the proposed substitution, to be accomplished by the Contractor without additional expense to the Owner, if and when approved. Detail drawings and other information necessary to show and explain the proposed modifications shall be submitted with the request for approval of the substitution.

4.6.11 All equipment, apparatus, or devices of any kind to be incorporated into the Work that are shown or indicated on the drawings or called for in the specifications or required for the completion of the Work shall be entirely satisfactory to the Owner's Project Manager as regards operations, capacity, or performance. No approval, either written or oral, of any drawings, descriptive data, or samples of such equipment, apparatus, or device shall relieve the Contractor of his responsibility to turn over the same in good working order for its intended purpose at the completion of the Work in complete accordance with the Contract Documents. Any equipment, apparatus and/or device not fulfilling these requirements shall be removed and replaced by proper and acceptable equipment, or put in good working order satisfactory to the Owner's Project Manager without additional cost to the Owner.

4.6.12 The Contractor shall at all times enforce strict discipline and good order among his employees and shall not employ on the Work any unfit person or anyone not skilled in the task assigned to him. The Owner may, by written notice, require

GENERAL CONDITIONS

the Contractor to remove from the Work any employee the Owner deems incompetent, careless or otherwise objectionable.

4.7 WARRANTY

4.7.1 The Contractor guarantees and warrants to the Owner all work as follows:

- .1 That all materials and equipment furnished under this Contract will be new and the best of its respective kind unless otherwise specified;
- .2 That all Work will comply with or exceed industry standards and be free of omissions and faulty, poor quality, imperfect or defective materials or workmanship;
- .3 That where no standard is specified for such workmanship or materials, they shall be the best of their respective kinds;
- .4 That all applicable Work shall be entirely watertight and leakproof in accordance with all applicable industry customs and practices, and shall be free of shrinkage and settlement;
- .5 That the Work, including but not limited to, mechanical and electrical machines, devices and equipment shall be fit and fully usable for its intended and specified purpose and shall operate satisfactorily with ordinary care;
- .6 That consistent with requirements of the Contract Documents, the Work shall be installed and oriented in such a manner as to facilitate unrestricted access for the operation and maintenance of fixed equipment; and
- .7 That the Work will be free of abnormal or unusual deterioration that occurs because of poor quality materials, workmanship or unsuitable storage.

4.7.2 All work not conforming to guarantees and warranties specified in the Contract Documents, including substitutions not properly approved and authorized, may be considered defective. If required by the Owner's Project Manager, the Contractor shall furnish satisfactory evidence as to the kind and quality of materials and equipment. This warranty is not limited by the provisions of Article 13 "UNCOVERING AND CORRECTION OF WORK."

GENERAL CONDITIONS

- 4.7.3** The warranties set forth in this Article 4.7 and elsewhere in the Contract Documents shall survive Final Completion of the Work under Article 9.8 "FINAL COMPLETION AND FINAL PAYMENT."
- 4.7.4** If, within one year after the Date of Final Acceptance of the Work or designated portion thereof or within one year after acceptance by the Owner of designated equipment or within such longer period as may be prescribed by law or by the terms of the applicable special warranty required by the Contract Documents, any of the Work is found to be defective, not in accordance with the Contract Documents, or not in accordance with the guarantees and warranties specified in the Contract Documents, the Contractor shall correct it within five working days, or such other period as agreed, after receipt of written notice from the Owner or Owner's Project Manager to do so.
- 4.7.5** If at any time deficiencies in the Work are discovered that are found to have resulted from latent defects, gross mistakes, fraud or misrepresentation by the Contractor, any Subcontractor or Supplier, the Contractor will be liable for replacement or correction of such Work or any damage that the Owner has incurred, or will incur, related thereto, regardless of the time limit of any guarantees or warranty.
- 4.7.6** Any materials or other portions of the Work, installed, furnished, or stored on site that are not of the character or quality required by the specifications, or are otherwise not acceptable to the Owner's Project Manager shall be immediately removed and replaced by the Contractor to the satisfaction of the Owner's Project Manager when notified to do so by the Owner's Project Manager.
- 4.7.7** If the Contractor fails to correct defective or nonconforming Work as required by Article 4.7.4 or Article 4.7.5 or, if the Contractor fails to remove defective or nonconforming Work from the site, as required by Article 4.7.6, the Owner may elect to either correct such Work in accordance with Article 3.4 "OWNER'S RIGHT TO CARRY OUT THE WORK" or remove and store materials and equipment at the expense of the Contractor.
- 4.7.8** The Contractor shall bear the cost of making good all work of the Owner, separate contractors or others, destroyed or damaged by such correction or removal required under this Article, Article 13 "UNCOVERING AND CORRECTION OF WORK" or elsewhere in the Contract Documents.

4.8 TAXES

- 4.8.1** The Contractor shall pay all applicable Federal, State, and local taxes and duties for the Work or portions thereof provided by the Contractor that are legally enacted at the time the Contract is awarded, whether or not yet effective.

GENERAL CONDITIONS

Increases in the rates of such taxes and duties during performance of the Contract shall be the responsibility of the Contractor.

4.9 PERMITS, FEES AND NOTICES

4.9.1 The Contractor shall secure and pay for all permits, fees, licenses and inspections necessary for the proper execution and completion of the Work that are legally required at the time the proposals are received.

4.9.2 The Contractor shall give all notices and comply with all laws, ordinances, rules, regulations and lawful orders of any public authority bearing on the performance of the Work.

4.9.3 The Contractor shall have personnel on site that are qualified and have the proper certifications for Erosion and Sedimentation Control, Best Management Practice (BMP), and Storm Water Management (SWM), or any other Department of Environmental Quality (DEQ) certifications as required for any and all permits issued and/or required by the Work.

4.10 SUPERINTENDENT

4.10.1 The Contractor shall employ a competent Superintendent and necessary assistants who shall be in attendance at the Project site during the progress of the Work. The Superintendent shall be an authorized representative of the Contractor and all communications given to the Superintendent shall be as binding as if given to the Contractor.

4.10.2 The Superintendent shall be in attendance at the Project site not less than eight hours per day, five days per week, unless the job is closed down due to a general strike or conditions beyond the control of the Contractor or until termination of the Contract in accordance with the Contract Documents. It is understood that such Superintendent shall be approved in writing by the Owner and shall be the one who will continue in that capacity for the duration of the Project, unless the Superintendent ceases to be on the Contractor's payroll or his withdrawal is required or approved by the Owner. The Superintendent shall not be employed on any other project for or by the Contractor or any other entity during the course of the Work.

4.10.3 Such Superintendent shall be fluent in English and in such other languages as may be necessary to communicate effectively with all owner's representatives, employees and Subcontractors of the Contractor. This requirement may be satisfied by the on-site presence of a competent foreign language interpreter to English interpreter. Any costs associated with foreign language interpretation shall be borne by the Contractor.

GENERAL CONDITIONS

4.10.4 Any and all project documents, including but not limited to daily reports and logs, maintained by the Superintendent or the Contractor's employees or Subcontractors shall be in English. Any costs of foreign language translation shall be borne solely by the Contractor and shall not be a basis for any additional compensation or time extension from the Owner.

4.11 PROJECT SCHEDULES

4.11.1 The Schedule of Completion shall consist of the Contractor planning, scheduling, and constructing this project by using a Critical Path Method Project Schedule (CPM). The CPM shall be used for coordinating and monitoring all the Work specified in the Contract Documents including all activities of subcontractors, vendors, suppliers, utilities, and all other parties associated with the construction of the project. The CPM shall be based upon the entirety of the Contract Documents. All physical work and major procurement activities shall be included. The CPM shall be the Activity-On-Arrow type. The Contractor shall use either Primavera or SureTrak scheduling software.

The CPM utilized float: Float is defined as the amount of time between when an activity "can start" (the early start) and when an activity "must start" (the late start). Float is a shared commodity for the Owner and the Contractor and is not for the exclusive use or financial benefit of either party. Either party has the full use of the float until it is depleted.

4.11.2 Initial Critical Path Method Project Schedule (ICPM) shall consist of the following:

- a. Activity-On-Arrow Time Scale Diagram
- b. Total Float Computer sort
- c. Written Narrative (WN)
- d. Printed calendars. The printed calendars shall include a listing, description, and calendar form tabulation of all calendars used in the ICPM. The calendars shall contain the total number of anticipated work days required to complete all the Work required in the Contract. The calendars shall delineate the holidays, anticipated nonwork days, and bad weather days. An explanation of the Contractor's basis for determining nonwork and bad weather days shall be included with the calendars.
- e. Data disc containing all of the information for (a) thru (d). The format shall be compatible with the Owner's computer software.

The ICPM diagram shall be drafted to a scale that allows the I node and J node numbers of each activity to be printed adjacent to that activity. The activities shall be clearly defined. All restraints between activities shall be shown.

GENERAL CONDITIONS

The Contractor shall expend the entire Contract time specified in this Invitation for Bids. On Contracts with calendar date completions or calendar day durations, all planned activities shall have durations not exceeding 14 calendar days, except the activities required for the Owner's review and approval of the working drawings and material sources which shall be given a duration of not less than 30 calendar days. On Contracts with working day durations, these time periods shall be 10 working days and 25 working days.

All activities in the Contract Documents along with a written narrative explanation shall be identified in the ICPM. The Project Manager reserves the right to specify the number of activities, and to require at any time additional breakdown of the activities.

The Contractor shall provide a written narrative as part of the ICPM describing the original critical path, the sequence of work, number of shifts per day, number of hours per shift, composition and number of crews, and the equipment to be utilized on each activity. Subcontracting activities shall be listed and identified by activity number. Each activity shall be identified by physical location and phase of work. Abbreviations used in preparing the ICPM shall be explained in the written narrative.

The Contractor shall complete the proposed ICPM within 14 calendar days after receiving the Notice of Award and submit 5 sets to the Project Manager for review and approval. The Project Manager will review the Contractor's ICPM within 5 calendar days after the submittal. If required, the Project Manager will convene a Joint Review Conference at which time the Project Manager and Contractor may make corrections and adjustments to the proposed ICPM. If a revision is necessary due to the Project Manager's review or the Joint Review Conference, the proposed revisions shall be submitted, by the Contractor, within 7 calendar days after the initial review date to the Project Manager for another review. Revisions shall conform to the format used in the ICPM. The Project Manager will respond to the revised ICPM within seven calendar days after its receipt.

No construction work shall begin until the Project Manager has accepted the ICPM. Time charges shall begin no later than the on or before date of the Notice to Proceed. Any delay in starting work caused by the acceptance of the ICPM by the Project Manager will not be a basis for any monetary claim.

- 4.11.3** When the Project Manager notifies the Contractor that the ICPM has been accepted, that document will become the CPM of Record (CPMR). The Contractor shall be responsible for implementing and executing the Work specified in the Contract in strict conformance with the CPMR. The CPMR shall be the Contractor's work plan for completing the entire Contract as specified in the Contract Documents.

GENERAL CONDITIONS

Failure of the Contractor to adhere to the latest approved CPMR will be cause for the Owner to deny any and all requests for additional compensation or extensions of the Contract duration.

4.11.4 Revisions to the CPMR shall consist of one or more of the following:

- a. A change in duration of an activity.
- b. A change in the logic of the schedule.
- c. A change in the calendars.
- d. The deletion or addition of one or more activities.

The Contractor may submit a proposed revision to the CPMR at any time during the life of the Contract.

The Contractor shall submit a proposed revision to the CPMR whenever the activities differ from the accepted CPMR. Proposed revisions shall be submitted by the Contractor within 30-calendar days from the date on which the Contractor's activities deviated from the accepted CPMR. The revisions shall be submitted to the Project Manager in the same format used for the ICPM. The revisions shall include data from all CPMR Updates, which have been accepted by the Administration. The Written Narrative accompanying the revision shall describe the reason for the revisions, the critical path, and all logic and duration modifications to the CPMR. These shall include, but not be limited to, changes in the method or manner of the Work, changes in Specifications, extra work, addition or deletion of work, increased or decreased quantities, defective work and acceleration of the Work.

The Project Manager will review the CPMR and respond to the Contractor's proposed revision within 5 calendar days after its receipt. The Project Manager reserves the right to deny any proposed revision which adversely impacts the Owner, utilities, or other interested parties.

4.11.5 Any written request for an extension of time or change in incentive/disincentive date (if applicable) shall be accompanied by a revised CPMR, which documents the actual delay to the Contract completion date or incentive/disincentive date. The request shall include a written narrative of the events which would require an extension of the Contract time or incentive/disincentive date.

Only delays to activities, which affect the Contract completion date or incentive/disincentive date will be considered for a time extension. The extension of the specified Contract completion date or incentive/disincentive date will be based upon the actual number of calendar days the Contract completion date or incentive/disincentive date is adjusted. No extensions of the specified Contract completion date will be issued for work performed on activities with float.

GENERAL CONDITIONS

- 4.11.6 Monthly updates of the CPMR are required.** CPMR update submissions shall contain the activity data as specified in (a) thru (e) of the ICPM. The update shall describe the progress of the project to date. It shall include a description of the current critical path, the amount of float on the critical path, any delays or disruptions experienced by the Contractor during the period of the update, any change in manpower or equipment, the inclusion of any schedule revisions, and any potential delays or disruptions.

When a delay or a disruption to the Work is identified in the Written Narrative, which the Contractor believes to be the responsibility of the Owner, the Contractor shall submit a revision to the CPMR within 30 calendar days after the submittal of the updates.

- 4.11.7** The Owner and the Contractor will hold monthly job site progress meetings to discuss the progress of the project and update the CPMR. The Contractor shall arrange to have a representative of each subcontractor currently working on the project in attendance. The Contractor shall submit to the Project Manager the CPMR updates within 14 calendar days from the date of the monthly meeting. The Project Manager will review the update and advise the Contractor of its acceptability prior to the next monthly meeting.

4.12 RESPONSIBILITY FOR COMPLETION

- 4.12.1** The Contractor shall furnish such labor, materials, tools, equipment, and professional services and shall work such hours, including night shifts, overtime operations and Sundays and holidays, as may be necessary to ensure the performance of the Work within Milestone and Completion dates specified in the Owner/Contractor Agreement. If it becomes apparent to the Owner's Project Manager that the Work will not be completed within required Milestone or Completion dates, the Contractor agrees to undertake some or all of the following actions, at no additional cost to the Owner, in order to ensure, in the opinion of the Owner's Project Manager, that the Contractor will comply with all Milestone and Completion date requirements:

- .1 Increase labor, materials, tools, equipment and professional services;
- .2 Increase the number of working hours per shift, shifts per working day, working days per week, or any combination of the foregoing; and
- .3 Reschedule activities to achieve maximum practical concurrency of accomplishment of activities.

- 4.12.2** If the actions taken by the Contractor are not satisfactory, the Owner or the Owner's Project Manager may direct the Contractor to take any and all actions

GENERAL CONDITIONS

necessary to ensure completion within the required completion dates, without additional cost to the Owner. In such event, the Contractor shall continue to assume responsibility for his performance and for completion within the required dates.

4.12.3 If, in the opinion of the Project Manager, the actions taken by the Contractor pursuant to this Agreement or the progress or sequence of work are not accurately reflected on the Construction schedule, the Contractor shall revise such schedule to accurately reflect the actual progress and sequence of work.

4.12.4 This provision does not eliminate the Contractor's responsibility to comply with the Town noise ordinances, all Town permit requirements and all other applicable laws, regulations, rules, ordinances, resolutions, and permit requirements.

4.13 DOCUMENTS, OTHER SUBMITTALS AT THE SITE; AS-BUILT DRAWINGS

4.13.1 The Contractor and his Subcontractors shall maintain at the site, and at all times make available to the Owner and the Owner's Project Manager one record copy of all Drawings, Specifications, Addenda, Change Orders, and other Modifications, in good order and marked currently to record all changes made during construction, and approved Shop Drawings, Product Data, Samples, Mock Ups and other Submittals ("as-built drawings").

4.13.2 The Contractor shall prepare the as-built drawings by marking up two sets of prints and one electronic copy of the applicable Contract Drawings to portray as-built construction, in conformance with the DCSM. The prints shall be neatly and clearly marked to show all variations between the Work actually provided and that indicated on the Contract Drawings, and all utilities encountered in the Work. All drafting shall conform to good drafting practice and shall include such supplementary notes, legends and details as may be necessary for legibility and clear portrayal of the as-built construction. These drawings shall be marked promptly at the completion of the project and shall be turned over the Owner prior to Final Payment.

4.14 SHOP DRAWINGS, PRODUCT DATA, SAMPLES AND OTHER SUBMITTALS

4.14.1 The term "Shop Drawings" shall mean all drawings, diagrams, illustrations, brochures, schedules and other data which are prepared by Contractor, a Subcontractor, manufacturer, supplier or distributor and which illustrate the equipment, material or some portion of the Work.

4.14.2 The Contractor shall submit with reasonable promptness and in such sequence as to cause no delay in the Work or in the work of the Owner or any separate

GENERAL CONDITIONS

Contractor, all Shop Drawings, Product Data, Manuals, Samples, and Submittals required by the Contract Documents. All such submissions shall be made so as to cause no delay in the project, allowing the Owner or his designated representative fourteen (14) working days for review and checking.

- 4.14.3** By approving and submitting Shop Drawings, Product Data, Manuals, Samples and Submittals, the Contractor represents that he has determined and verified all materials, field measurements, and field construction criteria related thereto, and that he has checked and coordinated the information contained within such submittals with the requirements of the Work and of the Contract Documents. The Contractor shall adhere to any supplementary processing and scheduling instructions pertaining to any submittals that may be issued by the Owner's Project Manager.
- 4.14.4** Parts and details not fully indicated on the Contract Drawings shall be detailed by the Contractor in accordance with standard engineering practice. Dimensions on the Contract Drawings, as well as detailed drawings themselves, are subject in every case to measurements of existing, adjacent, incorporated and completed work that shall be taken by the Contractor before undertaking any work dependent on such data.
- 4.14.5** Where the Contract Documents call for the submittal of manufacturer's data to the Owner or the Owner's Project Manager for information only, such submittals shall be made before the commencement of any portion of the Work requiring such submission.
- 4.14.6** The Contractor shall not be relieved of responsibility for any deviation from the requirements of the Contract Documents by virtue of the review by the Owner or the Owner's Project Manager of Shop Drawings, Product Data, Samples or Manuals unless the Contractor has specifically informed the Owner's Project Manager in writing of such deviation at the time of submission and the Owner's Project Manager has given written approval to the specific deviation. The Contractor shall not be relieved from responsibility for errors or omissions in the Shop Drawings, Product Data, Samples or Manuals by the Owner or Owner's Project Manager's review thereof.
- 4.14.7** Shop drawings shall be submitted in such number of copies that three copies may be retained by the Project Manager or his designee after approval. Each submission shall be accompanied by a letter of transmittal in duplicate, listing the contents of the submission and identifying each item by reference to specification section or drawing. All Shop Drawings shall be clearly labeled with the name of the project and such information as may be necessary to enable their complete review by the Project Manager or his designee. Catalog plates and other similar material that cannot be so labeled conveniently shall be bound in suitable covers bearing the identifying data.

GENERAL CONDITIONS

- 4.14.8** Shop drawings shall be accompanied by all required certifications and other such supporting material, and shall be submitted in such sequence or in such groups that all related items may be checked together. When Shop Drawings cannot be checked because a submission is not complete, or because Shop Drawings on related items have not been received by the Project Manager or his designee, such Shop Drawings will be returned without action, and marked 'rejected' with the reason for rejection clearly stated. Incomplete or defective submittals shall also be returned without action, and marked 'rejected' with the reason for rejection clearly stated.
- 4.14.9** Shop Drawings shall have been reviewed by the Contractor and coordinated with all other related or affected work before they are submitted for approval and shall bear the Contractor's certification that the Contractor has checked and approved them as complying with all relevant information in the Contract Documents. Shop Drawings submitted without such certification and coordination will be returned to the Contractor without action and will be considered not a formal submission.
- 4.14.10** SAMPLES required by the specifications or requested by the Project Manager or his designee shall be submitted for approval. Samples shall be submitted in single units only, unless the Contractor desires additional units for the Contractor's own use. Each sample shall bear a label indicating the material represented, the name of the producer and the title of the Project. Approval of a sample shall be only for conformance with the design concept of the Project and compliance with the information given in the Contract Documents, and only for the characteristics or use named in such approval. Such approval shall not be construed to change or modify any Contract requirements or the Contract Price. Materials and equipment incorporated in the Work shall match the approved samples.
- 4.14.11** All TESTS of materials and finished articles shall be made by bureaus, laboratories or agencies approved by the Project Manager or his designee, and the certified reports of such tests shall be submitted to the Project Manager. All costs in connection with the testing shall be borne by the Contractor. Failure of any material to pass the specified tests or any test performed by the Project Manager or his designee will be sufficient cause for refusal to consider, under this Contract, any further materials of the same brand or make of that material. Samples of various materials delivered on the site or in place may be taken by the Project Manager or his designee for testing. Samples failing to meet the requirements of the Contract Documents will automatically void previous approvals of the items tested. See Article 7.5 for additional test requirements.

Unless otherwise specified, testing for soil compaction, soil suitability, concrete testing, etc. will be performed by or on behalf of the Contractor at the

GENERAL CONDITIONS

Contractor's expense. The Contractor shall furnish copies of all test results or related reports or documents to the Project Manager.

4.15 CUTTING AND PATCHING OF WORK

4.15.1 The Contractor shall be responsible for all cutting, fitting or patching that may be required to complete the Work and to make its several parts fit properly and in accordance with the Contract Documents.

4.15.2 The Contractor shall not damage or endanger any portion of the Work or the work of the Owner or any separate Contractors by cutting, patching or otherwise altering any work, or by excavation. The Contractor shall not cut or otherwise alter the work of the Owner or any separate Contractor except with the written consent of the Owner and of such separate Contractor. The Contractor shall not unreasonably withhold from the Owner or any separate Contractor his consent to cutting or otherwise altering the Work. The Owner shall not be required to accept work with a cut, a splice, or patch when such cut, splice or patch is not generally accepted practice for the particular work involved or is otherwise unworkmanlike in the opinion of the Owner or the Owner's Project Manager.

4.16 DRUG-FREE WORKPLACE

During the performance of this contract, the Contractor agrees as follows:

- .1 The Contractor will provide a drug-free workplace for the Contractor's employees. The Contractor agrees to post in conspicuous places, available to employees and applicants for employment, a statement notifying employees that the unlawful manufacture, sale, distribution, dispensation, possession, or use of a controlled substance or marijuana is prohibited in the Contractor's workplace and specifying the actions that will be taken against employees for violations of such prohibition.
- .2 The Contractor shall state in all solicitations or advertisements for employees placed by or on behalf of the Contractor that the Contractor maintains a drug-free workplace.
- .3 The Contractor will include the provisions of the foregoing clauses in every subcontract or purchase order of over \$10,000, so that the provisions will be binding upon each Subcontractor or vendor.

For the purposes of this section, "drug-free workplace" means a site for the performance of work done in connection with a specific contract awarded to a Contractor in accordance with the VPPA Section 2.2-4312, the employees of

GENERAL CONDITIONS

whom are prohibited from engaging in the unlawful manufacture, sale, distribution, dispensation, possession or use of any controlled substance or marijuana during the performance of the contract.

4.17 NON-DISCRIMINATION IN EMPLOYMENT

During the performance of this Contract, the Contractor agrees to comply fully with VPPA § 2.2-4201 and § 2.2-4343.1 as follows:

- .1 The Contractor will not discriminate against any employee or applicant for employment because of race, religion, disability, color, sex or national origin, except where religion, sex or national origin is a bona fide occupational qualification reasonably necessary to the normal operation of the Contractor and the Contractor agrees to post in conspicuous places, available to employees and applicants for employment, notices setting forth the provisions of this nondiscrimination clause;
- .2 The Contractor, in all solicitations or advertisements for employees placed by or on behalf of the Contractor, will state that such Contractor is an equal opportunity employer;
- .3 Notices, advertisements and solicitations placed in accordance with Federal law, rule or regulation, shall be deemed sufficient for the purpose of meeting the requirements of this provision; and
- .4 The Contractor will include the provisions of paragraphs .1, .2, .3 above in every subcontract or purchase order of over \$10,000 so that the provisions will be binding upon every Subcontractor or vendor.
- .5 The Contractor will comply with the requirements VPPA Section 2.2-4343.1, Permitted Contracts with Certain Religious Organizations, as applicable.

4.18 SIGNS

The Contractor may at his option and without cost to the Owner, erect signs acceptable to the Owner on the site of the Contract for the purpose of identifying and giving directions to the job. No signs shall be erected without prior approval of the Owner as to design and location.

GENERAL CONDITIONS

4.19 CLEANING UP

4.19.1 The Contractor at all times shall keep the project site and all surrounding public streets and neighboring property free from accumulation of waste materials or rubbish caused by his operations. At the completion of the Work and before Final Payment is made, he shall remove all his waste materials and rubbish from and about the Project as well as all his tools, equipment and surplus materials. The Contractor shall also thoroughly clean and leave reasonably dust free all interior of all buildings included in the Contract, and thoroughly clean all glass installed under the Contract including the removal of all paint and mortar splatters and other defacements.

4.19.2 If the Contractor fails to clean up during or at the completion of the Work, the Owner may do so as provided in Article 6.3 "OWNER'S RIGHT TO PERFORM DISPUTED WORK" and the cost thereof shall be charged to the Contractor.

4.19.3 The Contractor shall take all reasonable steps, including but not limited to providing a wash down area, to prevent mud, dirt, and other material from accumulating upon the public streets.

4.19.4 During and at the completion of the Work, the Contractor shall prevent site soil erosion, the runoff of silt or debris carrying water from the site, and the blowing of debris off the site in accordance with the applicable requirements and standards of the Virginia Erosion and Sediment Control Handbook, latest edition, and the Contract Documents.

4.20 ROYALTIES AND PATENTS

4.20.1 Contractor shall pay all license fees and royalties and assume all costs incident to the use in the performance of the Work of any invention, design, process, product or device which is the subject of patent rights or copyrights held by others. If a particular invention, design, process, product or device is specified in the Contract Documents for use in the performance of the Work and if to the actual knowledge of the Owner or Owner's Project Manager its use is subject to patent rights or copyrights calling for the payment of any license fee or royalty to others, the existence of such rights shall be disclosed by Owner in the Contract Documents. Contractor shall indemnify, defend and hold harmless Owner and Owner's Project Manager and anyone directly or indirectly employed by either of them from and against all claims, damages, losses and expenses (including attorneys' fees) arising out of any infringement of patent rights or copyrights incident to the use in the performance of the Work of any invention, design, process, product or device not specified in the Contract Documents, and shall defend all such claims in connection with any alleged infringement of such rights.

GENERAL CONDITIONS

4.21 ANTITRUST

By entering into a contract Contractor conveys sells assigns and transfers to the Owner all rights, title and interest in and to all causes of the action it now may have or hereafter acquire under the antitrust laws of the United States and the Commonwealth of Virginia, relating to the particular good(s) or service(s) purchased or acquired by the Owner under this contract.

4.22 INDEMNIFICATION

4.22.1 To the fullest extent permitted by law, the Contractor shall, at his sole cost and expense, indemnify, defend, and hold harmless the Owner, the Owner's Project Manager, their agents, representatives, employees, successors and assigns from and against all claims, actions, judgments, costs, liabilities, penalties, damages, losses and expenses, including but not limited to, attorneys' fees, arising out of or resulting from the performance of the Work, provided that any such claim, action, judgment, cost, liability, penalty, damage, loss or expense:

- .1 Is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property (other than the Work itself) including loss of use resulting therefrom; and
- .2 Is caused in whole or in part by any negligent act or omission of the Contractor, any Subcontractor or supplier, anyone directly or indirectly employed by any of them or anyone for whose acts any of them may be liable, regardless of whether or not it is caused in part by a party indemnified hereunder.

The Contractor shall not be obligated to indemnify the Owner or the Owner's Project Manager hereunder for any damages or injuries, including death, the proximate cause of which is the sole negligence of the Owner or the Owner's Project Manager, consistent with Va. Code § 11-4.1.

Such obligation shall not be construed to negate, abridge, or otherwise reduce any other right or obligation of indemnity that would otherwise exist as to any party or person described in this Article 4.22

4.22.2 In any and all claims against the Owner and the Owner's Project Manager or any of their agents, representatives, or employees by any employee of the Contractor, any Subcontractor, anyone directly or indirectly employed by any of them, or anyone for whose acts any of them may be liable, the indemnification obligation under this Article 4.22 shall not be limited in any way by any limitation on the amount or type of damages, compensation or benefits payable by or for the Contractor or any Subcontractor under workers' compensation acts, disability benefit acts or other employee benefit acts.

GENERAL CONDITIONS

4.22.3 No provision of Article 4.22 shall give rise to any duties on the part of the Owner or the Owner's Project Manager, or any of their agents, representatives or employees.

4.22.4 The obligations of the Contractor under Article 4.22 shall not extend to the liability of the Owner's Project Manager, or the Owner's design architect or engineers, their agents or employees arising out of (a) the preparation or approval of maps, drawings, opinions, reports, surveys, Change Orders, designs or specifications, or (b) the giving of or the failure to give directions or instructions by Owner's Project Manager, his agents or employees provided such giving or failure to give is the primary cause of injury or damage.

4.23 PERSONS AUTHORIZED TO SIGN DOCUMENTS

The Contractor, within five days after the earlier of the date of a Notice to Proceed or the date of the Owner/Contractor Agreement shall file with the Owner's Project Manager a list of all persons who are authorized to sign documents such as contracts, certificates and affidavits on behalf of the Contractor and to fully bind the Contractor to all the conditions and provisions of such documents.

4.24 ASBESTOS AND OTHER HAZARDOUS SUBSTANCES

4.24.1 Whenever and wherever during the course of performing any work under this contract, the Contractor discovers the presence of asbestos or other hazardous substances or suspects the presence of any hazardous substances, he shall stop the work immediately, secure the area, notify the Owner and await positive identification of the suspect material. During the downtime in such a case, the Contractor shall not disturb any surrounding surfaces but shall protect the area with suitable dust covers. In the event the Contractor is delayed due to the discovery of asbestos, suspected asbestos or any other hazardous or suspected hazardous substances, then a mutually agreed extension of time to perform the Work shall be allowed the Contractor.

4.24.2 Any claims for extension of time shall be subject to the provisions of Article 8.

4.24.3 If the items/products to be purchased are "Hazardous Substances" as defined by 15 U.S.C. § 1261, then the Contractor certifies and warrants that the items or products to be delivered under the Contract shall be properly labeled as required by the foregoing sections and that by delivering the items/products, the Bidder does not violate any of the prohibitions of 15 U.S.C. § 1263.

GENERAL CONDITIONS

4.24.4 Material Safety Data Sheets (MSDS) and descriptive literature shall be provided with the submittal or delivery of each chemical and/or compound subject to Article 4.24.3. Failure on the part of the Contractor to submit such data may be cause for termination in accordance with Article 14.3.

4.25 RIGHT TO PUBLISH

The Contractor otherwise agrees that he will not publish, cause to be published, or otherwise disseminate any information of any nature relating to the Work performed under this Contract, except as may be approved by the Owner in writing.

4.26 MATERIALS AND EQUIPMENT LIST

4.26.1 At least ten (10) working days before the start of construction the Contractor shall submit to the Project Manager for approval a complete list of materials and equipment proposed for use in connection with the project. Partial lists submitted from time to time will not be considered.

4.26.2 After any material or piece of equipment has been approved, no change in brand or make will be permitted unless satisfactory written evidence is presented to prove that the manufacturer cannot make scheduled delivery of the approved material, or that material delivered has been rejected and the substitution of a suitable material is an urgent necessity, or that other conditions have become apparent which indicate that approval of such other material is in the best interest of the Owner.

END OF ARTICLE 4

GENERAL CONDITIONS

ARTICLE 5: SUBCONTRACTORS

5.1 DEFINITIONS

5.1.1 A Subcontractor is any firm, supplier, distributor or vendor that performs work for or furnishes services, equipment or supplies to or for the Contractor or another Subcontractor in conjunction with the Contract. The term Subcontractor is referred to throughout the Contract Documents as if singular in number and masculine in gender and means a Subcontractor or his authorized representative. Although the term Sub-subcontractor may appear within the Contract Documents, the term Subcontractor includes any person or entity that has a direct or indirect contract with the Contractor to perform any of the Work.

5.1.2 The Contractor shall be fully responsible to the Owner for all acts and omissions of his Subcontractors, and of persons and organizations directly or indirectly employed by them, and of persons and organizations for whose acts any of them may be liable, to the same extent that he is responsible for the acts and omissions of persons directly employed by him.

5.1.3 Nothing contained in the Contract Documents is intended to, nor shall it create, any contractual relationship between the Owner, the Owner's Project Manager, or any of their agents, consultants, employees, independent contractors, or representatives and any Subcontractor, but the Owner shall be entitled to performance of all obligations intended for its benefit, and to enforcement thereof.

5.1.4 The Owner's Project Manager will not deal directly with any Subcontractor. Communication will be made only through the Contractor. Subcontractors shall route requests for information or clarification through the Contractor to the Owner's Project Manager.

5.2 AWARD OF SUBCONTRACTS AND OTHER CONTRACTS FOR PORTIONS OF THE WORK

5.2.1 The Contractor shall within fourteen days after award of the Contract furnish to the Owner's Project Manager in writing the names of the persons or entities (including those who are to furnish materials or equipment fabricated to a special design) proposed for each of the principal portions of the Work. The Owner's Project Manager will promptly reply to the Contractor in writing stating whether the Owner has objection to any such proposed person or entity.

5.2.2 The Contractor shall not contract with any such proposed Subcontractor to whom the Owner has made objection under the provisions of Article 5.2.1. The Contractor shall not be required to contract with anyone to whom he has an objection.

GENERAL CONDITIONS

5.2.3 If the Owner objects to any proposed Subcontractor under Article 5.2.1, the Contractor shall name a substitute to whom the Owner has no objection within fifteen days.

5.2.4 The Contractor shall make no substitution for any Subcontractor previously proposed by the Contractor and not objected to by the Owner's Project Manager if the Owner makes objection to such substitution.

5.3 SUBCONTRACTUAL RELATIONS

5.3.1 By an appropriate agreement, written where legally required for validity, the Contractor shall require each Subcontractor, to the extent of the Work to be performed by the Subcontractor, to be bound to the Contractor by the terms of the Contract Documents, and to assume toward the Contractor all the obligations and responsibilities that the Contractor, by these Documents, assumes toward the Owner.

This agreement shall preserve and protect the rights of the Owner under the Contract Documents with respect to the Work to be performed by the Subcontractor. The subcontracting will not prejudice such rights, and shall allow to the Subcontractor, unless specifically provided otherwise in the Contractor-Subcontractor Agreements, the benefit of all rights, remedies and redress against the Contractor that the Contractor, by these Contract Documents, has against the Owner. Where appropriate, the Contractor shall require each Subcontractor to enter into similar agreements with his Subcontractors.

The Contractor shall make available to each proposed Subcontractor, prior to the execution of the Subcontract, copies of the Contract Documents to which the Subcontractor will be bound by this Article 5.3, and identify to the Subcontractor any terms and conditions of the proposed Subcontract that may be at variance with the Contract Documents. Each Subcontractor shall similarly make copies of such Contract Documents available to his Sub-subcontractors or Suppliers.

5.3.2 The Contractor shall be liable to and indemnify, defend and hold the Owner harmless from all costs, expenses, fees, attorney's fees, accountant's fees, damages and claims arising because of the Contractor's failure to comply with the provisions of this Article 5.3.

5.4 QUALIFICATION SUBMITTALS

5.4.1 Specific qualification submittals may be required of Subcontractors for certain critical items of the Work. Required qualification submittals are set forth in detail in the Contract Documents and shall be collected and submitted by the Contractor to the Owner's Project Manager for review and approval by the

GENERAL CONDITIONS

Owner and Owner's Project Manager. All information required of a single Subcontractor shall be contained in a single, complete submittal. The Contractor shall submit the required qualification information within ten days after receipt of the Owner's Project Manager's request.

5.4.2 The Owner may reject any proposed Subcontractor, or any qualification submittals related thereto, for the following reasons:

- .1 The Contractor's failure to submit requested information within the specified time; or
- .2 The Contractor's failure to provide all of the requested information; or
- .3 The Contractor's submission of a Subcontractor, or its qualifications, that are unacceptable to the Owner.

5.4.3 Should the Owner have objection to any proposed Subcontractor, the Contractor shall submit another firm for approval within fifteen days.

END OF ARTICLE 5

GENERAL CONDITIONS

ARTICLE 6: WORK BY OWNER OR BY SEPARATE CONTRACTORS

6.1 OWNER'S RIGHT TO PERFORM WORK AND TO AWARD SEPARATE CONTRACTS

6.1.1 The Owner reserves the right to perform work related to the Project with its own forces, and to award separate contracts in connection with other portions of the Project or other work on the site.

6.1.2 When separate contracts are awarded for different portions of the Project or other work on the site, the term Contractor in the Contract Documents in each case shall mean the Contractor who executes each separate Owner/Contractor Agreement.

6.2 MUTUAL RESPONSIBILITY

6.2.1 The Contractor shall afford other Contractors and the Owner reasonable opportunity for the introduction and storage of their materials and equipment and the execution of their work and shall properly connect and coordinate the Work with that of the Owner and other Contractors, to store his tools, materials and equipment in such orderly fashion at the site of the Work as will not unduly or unreasonably interfere with the progress of the Work or the work of any other Contractors.

6.2.2 If the execution or result of any part of the Work depends upon any work of the Owner or of any separate Contractor, the Contractor shall, prior to proceeding with the Work, inspect and promptly report in writing to the Owner's Project Manager any apparent discrepancies or defects in such work of the Owner or of any separate Contractor that render it unsuitable for such proper execution or result of any part of the Work under this Contract.

6.2.3 Failure of the Contractor to so inspect and report shall constitute an acceptance of the Owner or separate Contractor's work as fit and proper to receive the Work, except as to defects that may develop in the Owner's or separate Contractor's work after completion of the Work, and that the Contractor could not have discovered by its inspection prior to completion of the Work under this Contract.

6.2.4 Should the Contractor cause damage to the Work or property of the Owner or of any separate Contractor on the Project, or to other work on the site, or delay or interfere with the Owner's work on ongoing operations or facilities or adjacent facilities of the Contractor's work, the Contractor shall be liable for the same and, in the case of another Contractor, the Contractor shall attempt to settle such claim with such Contractor prior to such other Contractor's institution of litigation.

GENERAL CONDITIONS

6.3 OWNER'S RIGHT TO PERFORM DISPUTED WORK

6.3.1 If a dispute arises between the Contractor and separate Contractors as to their responsibility for cleaning up as required by Article 4.19 "CLEANING UP" or for accomplishing coordination as required by Article 6.4 "COORDINATION OF THE WORK," the Owner may carry out such Work and charge the cost thereof to the Contractors responsible therefor as the Owner's Project Manager shall determine.

6.4 COORDINATION OF THE WORK

6.4.1 By entering into this Contract, Contractor acknowledges that there may be separate Contractors on the Site whose work will be coordinated with that of his own. Contractor warrants and guarantees that he will cooperate with separate Contractors, and will do nothing to delay, hinder or interfere with the Work of other separate Contractors, the Owner or the Owner's Project Manager.

END OF ARTICLE 6

GENERAL CONDITIONS

ARTICLE 7: MISCELLANEOUS PROVISIONS

7.1 GOVERNING LAW

7.1.1 The Contract shall be governed by the law of the Commonwealth of Virginia, and shall be performed in accordance with the laws, ordinances, regulations, permits and resolutions of the Town of Leesburg. The sole venue for any litigation under this Contract shall be the Circuit Court of Loudoun County, Virginia. The conflicts of law provisions shall not be employed to apply the laws of any state other than those of the Commonwealth of Virginia to this Contract.

7.1.2 Each provision of law required to be inserted in this Contract shall be deemed inserted. If through mistake or otherwise, any provision is not properly inserted, the Contract shall be modified to include such provision upon the application of either party.

7.1.3 Where applicable, the Contractor shall meet or exceed all requirements of the Town of Leesburg Design and Construction Standards Manual and all other local, state and federal building codes.

7.2 SUCCESSORS AND ASSIGNS

7.2.1 The Contractor binds himself, his partners, successors, assigns and legal representatives to the Owner, its partners, successors, assigns and legal representatives in respect to all covenants, agreements and obligations contained in the Contract Documents. The Contractor shall not assign the Contract or sublet it as a whole without the written consent of the Owner, nor shall the Contractor assign any monies due or to become due to him under the Contract, without the previous written consent of the Owner and the Contractor's Surety. Nor shall any contract be entered into or assigned to any party that is debarred from doing business with or in the Commonwealth of Virginia.

7.2.2 In the event the Contractor desires to make an assignment of all or part of the contract or any monies due or to become due under this Contract, the Contractor shall file a written consent of Surety, together with a copy of the proposed Assignment with the Owner or the Owner's Project Manager. In the event the Contractor assigns all or any part of the monies due or to become due under this Contract, the instrument or assignment shall state that the right of assignees in and to any monies due to or to become due to the Contractor shall be subject to prior liens and claims of all persons, firms and corporations that provided labor, services, or furnished material and equipment during the performance of the Work. The rights of assignees shall further be subject to the payment of any liens, claims or amounts due to Federal or State governments, and to all rights of retention and set-off granted to the Owner by the Contract Documents.

GENERAL CONDITIONS

7.3 CLAIMS FOR DAMAGES

7.3.1 Should the Contractor suffer injury or damage to person or property because of any act or omission of the Owner or of any of its employees, agents or others for whose acts either is legally liable, claim shall be made in writing to the Owner within thirty days after the first observance of such injury or damage; otherwise, the Contractor shall have waived any and all rights he may have against the Owner, or its employees, representatives and agents.

7.4 DISPUTES

7.4.1 A claim, if any, shall be made in writing and submitted by the Contractor to the Owner, the Project Manager and the Leesburg Town Attorney within ten calendar days after the occurrence of events giving rise to the claim. A claim is limited to events rising out of or relating to the Contract. Failure to file a written claim as required herein shall constitute an absolute waiver of any claim of any sort.

7.4.2 The parties shall first endeavor to resolve any disputes, claims or other matters in question between them through direct negotiations, and if such direct negotiations fail, by non-binding mediation, with the site of the mediation being the Town of Leesburg, Virginia.

7.4.3 If the procedures of subparagraph 7.4.2 have been followed, but more than 90 days have passed since a party has requested mediation, and the dispute, claim or matter in question remains unresolved, then either party may institute a lawsuit in the Circuit Court of Loudoun County, Virginia, which is agreed to be the sole and exclusive venue, and may pursue all available appeals in Virginia state courts, to the extent they have jurisdiction.

7.4.4 Nothing in paragraphs 7.4.1 or 7.4.2 shall prevent a party from seeking temporary injunctive or other temporary equitable relief in the Loudoun County Circuit Court if circumstances so warrant.

7.4.5 In the event of any dispute, claim, or other matter in question arising, Contractor shall continue its performance diligently during its pendency as if no dispute, claim or other matter in question had arisen. During the pendency of any dispute in connection with the payment of moneys, Contractor shall be entitled to receive payments for non-disputed items.

7.4.6 Notwithstanding any other provision hereof, the Contractor expressly waives all claims against the Owner for consequential damages arising out of or relating to this Contract. This waiver includes losses of financing, business and reputation, bonding capacity, and loss of profit other than profit arising directly from the Work where otherwise permitted in the Contract.

GENERAL CONDITIONS

7.5 TESTS

7.5.1 If the Contract Documents, laws, ordinances, rules, regulations or orders of any public authority having jurisdiction require any portion of the Work to be inspected, tested, or approved, the Contractor shall give the Owner's Project Manager five days notice of its readiness so the Owner's Project Manager may observe such inspection, testing, or approval. The Contractor shall bear all costs of such inspections, tests or approvals conducted by public authorities.

7.5.2 If the Owner's Project Manager determines that any Work requires special inspection, testing, or approval that Article 7.5.1 does not include, the Owner's Project Manager will order the Contractor to make arrangements for such special inspection, testing or approval, and the Contractor shall give the Owner's Project Manager five days notice of such inspection. If such special inspection or testing reveals a failure of the Work to comply with:

- .1 The requirements of the Contract Documents, or
- .2 The conformance of the Work with laws, ordinances, rules, regulations, or orders of any public authority having jurisdiction.

The Contractor shall bear all costs of the Work, including compensation for the Owner's Project Manager and any additional services made necessary by such failure.

7.5.3 Inspections and tests required under Article 7.5.2 to establish compliance with the Contract Documents will be made by a testing agency employed by the Owner. If the initial tests indicate non-compliance with the Contract Documents, the Contractor shall bear the costs thereof and any subsequent testing occasioned by non-compliance shall be performed by the same agency and the cost thereof shall be borne by the Contractor. Representatives of the testing agency shall have access to the Work at all times. The Contractor shall provide facilities for such access in order that the agency may properly perform its functions.

7.5.4 Certificates of inspection, testing or approval required by public authorities shall be secured by the Contractor and promptly delivered by him to the Owner's Project Manager, in adequate time to avoid delays in the Work or Final Payment.

7.5.5 The Contractor shall pay for and have sole responsibility for inspection or testing performed exclusively for his own convenience and for tests necessary because of Contractor's or Subcontractor's errors, omission, or noncompliance with Contract Documents.

GENERAL CONDITIONS

7.5.6 All materials and workmanship (if not otherwise designated by the specifications) shall be subject to inspection, examination and test by the Owner or the Owner's Project Manager, at any time during the manufacture or construction and at any place where such manufacture or construction are carried on. Special, full-sized and performance tests shall be described in the specifications. Without additional charge, the Contractor shall furnish promptly all reasonable facilities, labor and materials necessary to make tests safe and convenient.

7.5.7 It is specifically understood and agreed that an inspection and approval of the materials or work by the Owner or the Owner's Project Manager shall not in any way subject the Owner to pay for the said materials or work or any portion thereof, even though incorporated in the Work, if said materials or work shall in fact turn out to be not in compliance with the Contract Documents or otherwise defective.

7.6 UNENFORCEABILITY OF ANY PROVISION

7.6.1 If any provision of this Contract is held as a matter of law to be unenforceable or unconscionable, the remainder of the Contract shall be enforceable without such provision.

7.7 AVAILABILITY OF LANDS

7.7.1 Owner shall furnish, as indicated in the Contract Documents, the lands upon which the Work is to be done, rights-of-way or easements for access thereto. The Owner reserves the right to delay the notice to proceed with the Contract Work in order to secure rights of way, easements or to relocate utilities, such as sewer, water, gas, electricity, cable television and other services.

7.7.2 If the Contractor requires additional land for temporary construction facilities and for storage of materials and equipment other than the areas available on the site or right-of-way, or as otherwise furnished by the Owner, the Contractor shall provide such other lands and access thereto entirely at the Contractor's own expense and without liability to the Owner. The Contractor shall not enter upon private property for any purpose without written permission. The contractor shall provide to the Owner evidence of written permission for entry onto private property for the purpose of temporary construction facilities and/or storage of materials and equipment.

7.8 NONEXCLUSIVITY OF REMEDIES

All remedies available to the Owner under the Contract are cumulative and no such remedy shall be exclusive of any other remedy available to the Owner.

END OF ARTICLE 7

GENERAL CONDITIONS

ARTICLE 8: TIME

8.1 DEFINITIONS

8.1.1 The Contract Time is the period set forth in the Owner/Contractor Agreement for Final Completion of the Work as defined in Article 8.1.4, including authorized extensions thereto.

8.1.2 The date of commencement of the Work is the date established in the Notice to Proceed issued by the Owner.

Submission by the Contractor of all Certificates of Insurance, Performance and Payment Bonds and their approval by the Owner are conditions precedent to the issuance of the Notice to Proceed. Availability of lands under Article 7.7 is also a condition precedent to the issuance of the Notice to Proceed. The Contractor shall not commence the Work or store materials or equipment on site until written Notice to Proceed is issued or until the Contractor otherwise receives the written consent of the Owner.

8.1.3 The date of Substantial Completion of the Work or designated portion thereof is the date certified by the Owner's Project Manager that the Work or a designated portion thereof is sufficiently complete, in accordance with the Contract Documents, so the Owner can fully occupy or utilize the Work or designated portion thereof for the use for which it is intended, with all of the Project's parts and systems operable as required by the Contract Documents. Only punch list work and any final cleaning beyond that needed for the Owner's full use may remain for Final Completion.

8.1.4 The date of Final Completion of the Work is the date certified by the Owner's Project Manager when the Work is complete, to include punch list work and final clean up, in accordance with the Contract Documents and the Owner may fully occupy or fully utilize the Work for the use for which it is intended.

8.1.5 If the date or time of completion is included in the Contract, it shall be the Date of Final Completion as defined in Article 8.1.4, including authorized extensions thereto, unless otherwise provided.

8.1.6 The term Day as used in the Contract Documents shall mean calendar day unless otherwise specifically designated. All dates shall mean midnight of the indicated day unless otherwise stipulated.

GENERAL CONDITIONS

8.2 PROGRESS AND COMPLETION

8.2.1 All time limits stated in the Contract Documents are of the essence of this Contract.

8.2.2 The Contractor shall prosecute the Work diligently to Final Completion.

8.3 DELAYS AND EXTENSIONS OF TIME

8.3.1 The time during which the Contractor is delayed in the performance of the Work, by the acts or omissions of the Owner, the Owner's Project Manager or their employees or agents, acts of God, unusually severe and abnormal climatic conditions, fires, floods, epidemics, quarantine restrictions, strikes (not to exceed the actual duration of the strike), riots, terrorism, civil commotions, war or freight embargoes, or other conditions beyond the Contractor's control and that the Contractor could not reasonably have foreseen and provided against, shall be added to the Contract Time; provided, however, that no claim by the Contractor for an extension of time for delays will be considered unless made in compliance with the requirements of this Article and other provisions of the Contract Documents.

8.3.2 The Contract Time shall be adjusted only for Change Orders pursuant to Article 12, "CHANGES IN THE WORK," Article 3.3, "OWNER'S RIGHT TO STOP OR SUSPEND THE WORK," and Article 8.3, "DELAYS AND EXTENSIONS OF TIME." If the Contractor requests an extension of the Contract Time, he shall furnish such justification and supporting evidence as the Owner's Project Manager may deem necessary for a determination of whether the Contractor is entitled to an extension of time under the provisions of the Contract.

8.3.3 The burden of proof to substantiate a claim for an extension of the Contract Time shall rest with the Contractor, including evidence that the cause was beyond his control. The Owner's Project Manager shall base his findings of fact and decision on such justification and supporting evidence and shall advise the Contractor in writing thereof.

8.3.4 The Contractor shall not be entitled to and hereby expressly waives any extension of time resulting from any condition or cause unless the request for an extension of time is made in writing to the Owner's Project Manager within seven days of the first instance of delay.

8.3.5 Any claim for an extension of time for a delay for any cause shall be made by filing a written notice of claim with the Owner and the Owner's Project Manager at the beginning of the occurrence or within seven days thereafter if the resulting delay was not reasonably foreseeable. If the asserted cause of delay is weather,

GENERAL CONDITIONS

such notice shall be given within seven days after asserted commencement of the claim delayed. The notice of claim shall state the circumstances of the occurrence, the justification for the delay and for the extension of time, and the estimated duration of the delay and of the extension requested. The claim for an extension of time for weather delays shall be further substantiated by weather data collected during the period of delay at the construction site. Said data must demonstrate that an actual departure from normal weather occurred at the work site during the dates in question. Within seven days after the cause of delay has been remedied, the Contractor shall give written notice to the Owner and the Owner's Project Manager of the actual time extension requested as a result of the claimed delay. Failure to file either of the notices as required herein shall constitute an absolute waiver of any claims resulting from a delay or any sort.

The anticipated adverse weather days per month are shown in the chart below.

<u>Jan</u>	<u>Feb</u>	<u>Mar</u>	<u>Apr</u>	<u>May</u>	<u>June</u>	<u>July</u>	<u>Aug</u>	<u>Sept</u>	<u>Oct</u>	<u>Nov</u>	<u>Dec</u>
8	7	7	8	8	7	5	6	4	6	5	5

The above chart will constitute the base line for monthly weather time evaluations. Actual adverse weather days will be recorded on a calendar day basis (including holidays and weekends), and compared to the anticipated monthly adverse monthly days based on the above chart. The number of actual adverse weather days shall be calculated chronologically from the first day to the last day in each month.

- 8.3.6** Any extension of time beyond the date of completion fixed by the Contract shall not be effective unless granted in writing, signed by the Owner.
- 8.3.7** The Contractor shall be entitled to an extension of time for delay which in the opinion of the Owner is entirely beyond the expectation and control of the Contractor by suspension of work pursuant to Article 3, or by strikes, lockouts, fire, insurrection, war, lightning, hurricane, and tornado. The Contractor shall be entitled to an extension of time for such causes only for the number of days of delay that the Owner may determine to be due solely to such causes and only to the extent that such occurrences actually delay the completion of the Project. Any request for extension of time shall be accompanied by detailed documentation of which specific schedule activities were affected, when they were affected and for what duration.
- 8.3.8** No extension of time will be granted to the Contractor for delays occurring to parts of the Work that have no measurable impact on the competition of the total Work under this Contract; nor will extension of time be granted for delays to

GENERAL CONDITIONS

parts of the Work that are not located on the Critical Path as reflected on the approved construction schedule at the time of such delay.

- 8.3.9** Delays in the delivery of equipment or material purchased by the Contractor or his Subcontractors (including Owner-selected equipment), or in the submission of required drawings or specifications by the Contractor's or its Subcontractor's materialmen, manufacturers or dealers, or in the performance of any of the Contractor's Subcontractors or caused by the performance of any of the Contractor's Subcontractors, shall not be considered as a just cause for delay. The Contractor shall be fully responsible for the timely submission, ordering, scheduling, expediting, delivery and installation of all equipment, materials and drawings.
- 8.3.10** Within sixty days after the Contractor files the notice of the actual duration of the extension of time as required herein, the Owner's Project Manager shall present his written opinion to the Owner as to whether an extension of time is justified, and, if so, his recommendation as to the number of days for time extension. The Owner will make the final decision on all requests for extension of time. The Owner's written decision shall be presented to the Contractor within thirty days from receipt of the Owner's Project Manager's recommendation. All such decisions made by the Owner shall be binding and conclusive upon the Contractor.
- 8.3.11** With respect to suspensions of work under Article 3, the Contractor may be entitled to an extension of time if the claim for such extension is submitted in accordance with the requirements of this Article, and if the suspension is not due to any act or omission of the Contractor, any Subcontractor or Sub-subcontractor or any other person or organization for whose acts or omission the Contractor may be liable.
- 8.3.12** An extension of time shall be the sole remedy under this Contract for any reasonable delay caused by any reason or occurrence. The Contractor acknowledges such extension of time to be its sole remedy hereunder, and agrees to make no claim for monetary damages of any sort for delay in the performance of this Contract occasioned by or in any way related to or arising from any act or omission to act of the Owner or the Owner's Project Manager or any representatives of the Owner or any representatives of the Owner's Project Manager, or because of any injunction which may be brought against the Owner or the Owner's Project Manager.
- 8.3.13** As a condition precedent to such additional compensation for unreasonable delay, the Contractor shall satisfy all notice and submission requirements set forth in the Contract Documents for approval of any extension of Contract Time or any change in the Contract Price.

GENERAL CONDITIONS

8.3.14 If the Contractor asserts an unwarranted claim for additional compensation for unreasonable delay, the Contractor shall be liable to the Owner and shall pay the Owner all costs incurred by the Owner in investigating, analyzing, negotiating, and litigating the claim.

8.3.15 This Article shall be construed to be included where applicable in every portion of the Contract Documents regardless of whether or not it is specifically referenced therein.

END OF ARTICLE 8

GENERAL CONDITIONS

ARTICLE 9: PAYMENTS AND COMPLETION

9.1 CONTRACT PRICE

9.1.1 Unless all or a part of the Contract is based on unit prices, the Contract Price is stated in the Contract and, including authorized adjustments thereto, is the firm, fixed price amount payable by the Owner to the Contractor for the performance of the Work under the Contract Documents. The Contract Price includes, but is not limited to, the Contractor's profits and general overhead and all costs and expenses of any nature whatsoever (including without limitation taxes, labor and materials), foreseen or unforeseen, and any increases in said costs and expenses, foreseen and unforeseen, incurred by the Contractor on this project. The Contractor agrees to assume all increases in costs of any nature whatsoever that may develop during the performance of the Work. The Contract Price includes all applicable Federal, State and local taxes and duties.

9.2 SCHEDULE OF VALUES

9.2.1 Within ten days after the Notice to Proceed is issued, the Contractor shall submit to the Owner's Project Manager a Schedule of Values, allocated to the various portions of the Work including mobilization and demobilization. This schedule, supported by data from the approved Progress Schedule, shall be used as a basis for the Contractor's Applications for Payment upon approval by the Owner's Project Manager. The Schedule of Values shall not alter in any way the firm, fixed price or lump sum contract price. The Contractor shall not front-end load or otherwise assign disproportionate amounts to the Schedule of Values.

9.2.2 If at any time the Contractor expects to receive an amount for a monthly progress payment larger than that indicated by the Schedule of Values and the approved Construction Schedule, the Contractor shall notify the Owner at least thirty days in advance of that payment so that the necessary allocation of funds can be processed. If the Contractor fails to give such notice, the Owner may defer such excess payment to the following progress payment.

9.2.3 With respect to any portion of the Contract subject to unit prices, the schedule of unit prices in the accepted bid shall be used as the basis for preparing Applications for Payment, and each partial payment shall represent the total value of all units of work completed, computed at the unit prices stated in the Contract, less the aggregate of previous payments and retainage. Final payment will be based on the actual quantities performed and justified on as-built drawings.

GENERAL CONDITIONS

9.3 APPLICATIONS FOR PAYMENT

9.3.1 The Owner shall make progress payments monthly as the Work proceeds on Applications for Payment approved by the Owner's Project Manager.

9.3.2 Prior to the date for each progress payment established in the Contract, the Contractor, in accordance with any Supplementary Conditions concerning schedules or payments, shall submit to the Owner's Project Manager an itemized Application for Payment, supported by such data substantiating the Contractor's right to payment as the Owner's Project Manager may require, including but not limited to the Contractor's certification that all work for which payment is requested has been completed in full accordance with the Contract Documents, copies of requisitions from Subcontractors and reflecting retainage, if any, as provided elsewhere in the Contract Documents. The Contractor shall certify that he has paid all due and payable amounts for which previous Certificates for Payment were issued and payments received from the Owner.

9.3.3 The Owner will retain five percent of the amount of all progress payments until the Work is substantially completed and accepted, whether or not the Owner has occupied any or all of the Project before such time.

9.3.4 The Contractor warrants that title to all Work, materials and equipment covered by an Application for Payment will pass to the Owner either by incorporation in the construction or upon the receipt of payment by the Contractor, whichever occurs first, free and clear of all liens, claims, security interests or encumbrances, hereinafter referred to in this Article 9 as "LIENS". The Contractor further warrants that no Work, materials or equipment covered by an Application for Payment will have been acquired by the Contractor, or by any other person performing Work at the site or furnishing materials and equipment for the Project, subject to an agreement under which an interest therein or an encumbrance thereon is retained by the seller or otherwise imposed by the Contractor or such other person.

9.3.5 Unless otherwise provided in the specifications the Owner will make partial payments to the Contractor on the basis of a duly certified and approved estimate of the Work performed during the preceding calendar month as certified by the Owner's Project Manager.

9.3.6 The Contractor may, in preparing estimates, take into consideration the material delivered on site and preparatory work done, if properly documented as required by this Contract, or as may be required by the Owner or the Owner's Project Manager so that the quantities may be verified.

9.3.7 The Contractor may, in preparing estimates, take into consideration material such as large pieces of equipment and items purchased specifically for the project, but

GENERAL CONDITIONS

stored off the site within the Commonwealth of Virginia, and these items may be considered for payment at the sole discretion of the Owner, provided that all of the following are accomplished prior to the submission of the monthly payment request in which payment for such materials is requested:

- .1 The Contractor must notify the Owner in writing at least ten days prior to the submission of the payment request, through the Owner's Project Manager, that specific items will be stored off site in a designated secure place within the Commonwealth of Virginia. The Schedule of Values must be detailed to separately indicate both the value of the material and of the labor/installation for trades requesting payment for stored materials. The Contractor warrants by giving such notification and by requesting payment for material stored off-site that the storage location is safe and suitable for the type of material stored and agrees that loss of such material shall not relieve him of the obligation to furnish these types and quantities of materials for the project and on a schedule to meet the time completion requirements of the Contract, subject to Article 8.
- .2 Such notification, as well as the payment request, shall:
 - a. itemize the quantity of such materials, and document with invoices the cost of said materials;
 - b. indicate the identification markings used on the materials. Such markings shall clearly reference the materials to the Project;
 - c. State the specific location of the materials. The location must be within reasonable proximity to the job site within the Commonwealth of Virginia;
 - d. State that the Surety on the Performance Bond and the Labor and Material Payment Bond has been notified of the request for payment of materials stored off the site and is agreeable to such payment;
 - e. Certify that adequate all-risk insurance has been obtained by the Contractor on the materials. Such insurance shall be in the name of the Owner and the Contractor.
- .3 The Owner's Project Manager shall indicate, in writing, to the Owner that submittals for such materials have been reviewed and meet the requirements of the drawings and specifications of the

GENERAL CONDITIONS

Contract documents, that the stored materials meet the requirement of the drawings and specifications, and that such material conforms to the approved submittals.

- .4 The Owner, through the Owner's Project Manager, shall notify the Contractor in writing of his agreement to prepayment for materials.
- .5 The Contractor shall notify the Owner in writing, through the Owner's Project Manager, when the materials are to be transferred to the site and when the materials are received at the site.
- .6 No partial payment shall be made until the appropriate Certificates of Insurance have been provided.
- .7 All material and Work for which partial payments are made shall thereupon become the sole property of the Owner, but this provision shall not relieve the Contractor from the sole responsibility for all materials and Work, including those for which payment has been made, or the restoration of any damaged Work or as a waiver of the right of the Owner to require the fulfillment of all the terms of the Contract.

9.4 CERTIFICATES FOR PAYMENT

9.4.1 The Owner's Project Manager will within ten days after receipt of the Contractor's Application for Payment, either approve the Application for Payment for such amount as he determines is properly due, or notify the Contractor in writing of his reasons for not approving the Application for Payment as provided in Article 9.6 "PAYMENTS WITHHELD."

9.4.2 The submission and approval of the Progress Schedule and monthly updates thereof, as required by any Supplementary Conditions concerning Schedules, shall be part of the application upon which progress payment shall be made. The Contractor shall be entitled to progress payments only as determined from the currently Approved and Updated Progress Schedule.

9.5 PROGRESS PAYMENTS

9.5.1 After an Application for Payment has been approved by the Owner's Project Manager, the Owner shall make payment in the manner and within the time provided in the Contract Documents.

GENERAL CONDITIONS

9.5.2 In accordance with Title 2.2-4354, Va. Code. Ann., Contractor is obligated to take one of the two following actions within seven (7) days after receipt of amounts paid to the Contractor by the Owner for work performed by any Subcontractor under this Contract:

- .1 Pay the subcontractor for the proportionate share of the total payment received from the Owner attributable to the Work performed by the Subcontractor under this Contract; or
- .2. Notify the Owner and the Subcontractor, in writing, of the Contractor's intention to withhold all or a part of the Subcontractor's payment with the reason for nonpayment.

The Contractor is obligated to provide its social security numbers and if a proprietorship, partnership, or corporation, they must provide its federal employer identification number.

The Contractor is obligated to pay interest to Subcontractors on all amounts owed by the Contractor that remain unpaid after seven (7) days following receipt by the Contractor of payment from the Owner for Work performed by the Subcontractor under this Contract, except for amounts withheld as allowed in Article 9.5.2.2, above. It is herewith provided that interest shall accrue at the base rate on corporate loans (prime rate) at large United States money center commercial banks as reported daily in the publication entitled The Wall Street Journal.

The Contractor shall include in each of its subcontracts a provision requiring each Subcontractor to include or otherwise be subject to the same payment and interest requirements with respect to each lower-tier Subcontractor.

The Contractor's obligation to pay an interest charge to a Subcontractor pursuant to the above provisions shall not be construed to be an obligation of the Owner. A Contract modification may not be made for the purpose of providing reimbursement for such interest charge. A cost reimbursement claim may not include any amount for reimbursement for such interest charge.

9.5.3 The Owner's Project Manager may, on request and at his discretion, furnish to any Subcontractor, if practicable, information regarding the percentages of completion or the amounts applied for by the Contractor, and the action taken thereon by the Owner's Project Manager on account of Work done by such Subcontractor.

9.5.4 The Owner has no obligation to pay or to see to the payment of any monies to any Subcontractor except as may otherwise be required by law.

GENERAL CONDITIONS

9.5.5 No Application for Payment, nor any progress payment, nor any partial or entire use or occupancy of the Project by the Owner, shall constitute an acceptance of any Work that is not in accordance with the Contract Documents.

9.5.6 In the event of disputes, payment shall be mailed on or before the Payment date for amounts and Work not in dispute, subject to any set-offs claimed by the Owner; except in instances where further appropriations are required by the Owner or where the issuance of further bonds is required, in which case, payment shall be made within thirty days after the effective date of such appropriation or within thirty days after receipt of bond proceeds by the Owner.

9.6 PAYMENTS WITHHELD

9.6.1 The Owner's Project Manager may decline to approve the Application for Payment or reduce payment or because of subsequently discovered evidence or subsequent observations, he may nullify the whole or any part of any Application for Payment previously approved to such extent as may be necessary in his opinion to protect the Owner from loss, because of:

- .1 Defective Work not remedied;
- .2 Third party claims filed, whether in court, in arbitration or otherwise, or reasonable evidence indicating probable filing of such claims;
- .3 Failure of the Contractor to make payments properly to Subcontractors;
- .4 Reasonable evidence that the Work cannot be completed for the unpaid balance of the Contract Price;
- .5 Damage to the Owner or to a separate contractor;
- .6 Reasonable evidence that the Work will not be completed within the Contract Time, or within any Contract Milestones as established in the Contract Documents;
- .7 Failure or refusal of the Contractor to carry out the Work in accordance with or to otherwise substantially or materially comply with the Contract Documents;
- .8 Failure or refusal of the Contractor to properly schedule and coordinate the Work, or to provide Progress Schedules, reports and updates; and

GENERAL CONDITIONS

.9 Failure or refusal of the Contractor to fully comply with the provisions of Article 4.13 "DOCUMENTS, OTHER SUBMITTALS AT THE SITE; AS-BUILT DRAWINGS."

9.6.2 When the above grounds in Article 9.6.1 are removed, payment shall be made for amounts withheld because of them.

9.7 SUBSTANTIAL COMPLETION

9.7.1 When the Contractor considers that the Work, or a designated portion thereof which is acceptable to the Owner's Project Manager, is substantially complete as defined in Article 8.1.3, the Contractor shall prepare for submission to the Owner's Project Manager a list of items that in his opinion are to be completed or corrected and shall request in writing that the Owner's Project Manager perform a Substantial Completion inspection. The Owner's Project Manager shall review the Contractor's list and will compile a punch list of items to be corrected and completed. The failure to include any items on such list does not alter the responsibility of the Contractor to complete all Work in accordance with the Contract Documents. When the Owner's Project Manager on the basis of an inspection determines that the Work or designated portion thereof is substantially complete, he will then prepare a Certificate of Substantial Completion that will establish the Date of Substantial Completion, state the responsibilities of the Owner and the Contractor for security, maintenance, heat, utilities, damage to the Work, and insurance, and shall fix the time within which the Contractor shall complete the items listed.

The Certificate of Substantial Completion shall be issued to the Contractor for his written acceptance of the responsibilities assigned to him in such Certificate and returned to the Owner's Project Manager within five days after issuance

9.7.2 The Contractor shall have thirty days from the Date of Substantial Completion to complete all items on the punch list to the satisfaction of the Owner's Project Manager. The Owner's Project Manager shall have the option to correct any and all punch list items not completed by the Contractor within thirty days from the Date of Substantial Completion by utilizing his own forces, those of the Owner, or by a separate Contractor. The cost of such correction of remaining punch list items by the Owner or others shall be deducted from the Final Payment to the Contractor.

9.7.3 The issuance of the Certificate of Substantial Completion does not indicate final acceptance of the Project by the Owner, and the Contractor is not relieved of any responsibility for the Project except as specifically stated in the Certificate of Substantial Completion.

GENERAL CONDITIONS

9.7.4 Should the Owner's Project Manager determine that the Work or a designated portion thereof is not substantially complete, he shall provide the Contractor a written notice stating why the project or designated portion is not substantially complete. The Contractor shall expeditiously complete the Work and shall request in writing that the Owner's Project Manager perform a Substantial Completion reinspection and the costs, if any, associated with such reinspection shall be assessed to the Contractor.

9.8 FINAL COMPLETION AND FINAL PAYMENT

9.8.1 Upon receipt of the documentation required by Article 9.8.3, and of written notice that the Work is ready for final inspection and acceptance, the Owner's Project Manager will promptly make such inspection and, when he finds the Work acceptable under the Contract Documents and the Contract fully performed, he will issue a Certificate of Final Completion to the Contractor. Upon his receipt of the Final Completion Certificate, the Contractor may submit his Application for Final Payment to the Owner's Project Manager for his approval. Final Payment shall be made in full to the Contractor within thirty calendar days after the approval by the Owner's Project Manager of the Application for Final Payment provided that the requirements of Article 9 have been fulfilled, except for an amount agreed upon for any Work remaining uncompleted for which the Owner is entitled a credit under the Contract Documents.

9.8.2 Should the Owner's Project Manager determine that the Work or a designated portion thereof is not complete, he shall provide the Contractor a written notice stating why the Project or designated portion is not complete. The Contractor shall expeditiously complete the Work and shall request in writing that the Owner's Project Manager perform a Final Completion reinspection and the costs, if any, associated with such reinspection shall be assessed to the Contractor.

9.8.3 Neither the Final Payment nor the remaining retained percentage shall become due until the Work is free and clear of any and all Liens and the Contractor submits to the Owner's Project Manager:

- .1 An affidavit that all payrolls, bills for materials and equipment, and other indebtedness connected with the Work for which the Owner or its property might in any way be responsible, have been paid or otherwise satisfied;
- .2 Consent of surety to Final Payment, if necessary;
- .3 As-built drawings, operation and maintenance manuals and other project closeout submittals, as required by the Contract Documents;

GENERAL CONDITIONS

- .4 A fully executed and notarized Release of claims in such form as may be designated by the Owner; and
- .5 A written certification that:
 - a. the Contractor has reviewed the requirements of the Contract Documents;
 - b. the Work has been inspected by the Contractor for compliance with all requirements of the Contract Documents;
 - c. pursuant to this inspection, the Contractor certifies and represents that the Work complies in all respects with the requirements of the Contract Documents;
 - d. the Contractor further certifies and represents that all equipment and systems have been installed and tested in accordance with the Contract Documents and the Owner personnel training in the proper operation and maintenance of equipment is complete; and
 - e. the Contractor provides construction releases as required by the Contract Documents from each property owner on whose property an easement for construction of this project has been obtained by the Owner, such release to be in the forms to be provided by the Owner. This release is for the purpose of releasing the Owner and the Contractor from liability, claims, and damages arising from construction operations on or adjacent to the easement and includes proper restoration of the property after construction. It shall be the Contractor's sole responsibility to obtain all such releases and furnish them to the Owner.

9.8.4 The making of Final Payment shall constitute a waiver of all claims by the Owner against the Contractor except those arising from:

- .1 Unsettled liens and claims against the Owner;
- .2 Faulty, defective or non-conforming Work discovered or appearing after Substantial or Final Completion;
- .3 Failure of Work to comply with the requirements of the Contract Documents; and

GENERAL CONDITIONS

.4 Terms of any warranties contained in or required by the Contract Documents.

9.8.5 The acceptance of Final Payment shall constitute a waiver of all claims by the Contractor except those previously made in writing and identified by the Contractor as unsettled at the time of the Application for Final Payment.

9.8.6 Warranties required by the Contract Documents shall commence on the Date of Final Acceptance of the Work or designated portion thereof unless otherwise provided in writing.

9.9 PARTIAL OCCUPANCY OR USE

9.9.1 The Owner may occupy or use any completed or partially completed portion of the Work at any stage when such portion is designated by separate agreement with the Contractor, provided such occupancy or use is consented to by the insurer as required under Article 11.2.8 and authorized by public authorities having jurisdiction over the Work. Such partial occupancy or use may commence whether or not the portion is substantially complete, provided the Owner and the Contractor have accepted in writing the responsibilities assigned to each of them for payments, retainage, if any, security, maintenance, heat, utilities, damage to the Work and insurance, and have agreed in writing concerning the period for correction of the Work and commencement of warranties required by the Contract Documents. When the Contractor considers a portion substantially complete, the Contractor shall prepare and submit a list to the Owner's Project Manager as provided under Article 9.7. Consent of the Contractor to partial occupancy or use shall not be unreasonably withheld. The stage of the progress of the Work shall be determined by written agreement between the Owner's Project Manager and the Contractor or, if no agreement is reached, by decision of the Owner's Project Manager.

9.9.2 Immediately prior to such partial occupancy or use, the Owner or the Owner's Project Manager, and the Contractor shall jointly inspect the area to be occupied or portion of the Work to be used in order to determine and record the condition of the Work.

9.9.3 Unless otherwise agreed upon, partial occupancy or use of a portion or portions of the Work shall not constitute acceptance of Work not complying with the requirements of the Contract Documents.

END OF ARTICLE 9

GENERAL CONDITIONS

ARTICLE 10: PROTECTION OF PERSONS AND PROPERTY

10.1 SAFETY PRECAUTIONS AND PROGRAMS

10.1.1 The Owner and the Owner's Project Manager are not responsible for the means, methods, techniques, sequences or procedures utilized by the Contractor, or for safety precautions and programs in connection with the Work. The Contractor shall be solely responsible for initiating, maintaining, and supervising all safety precautions and programs in connection with the Work. This requirement applies continuously throughout the Contract performance, until Final Payment is made, and is not limited to regular working hours.

10.2 SAFETY OF PERSONS AND PROPERTY

10.2.1 The Contractor shall take reasonable precautions for safety of, and shall provide reasonable protection to prevent damage, injury or loss, to:

- .1 All employees on the Work and other persons who may be affected thereby;
- .2 All the Work and materials and equipment to be incorporated therein whether in storage off the site, under the care, custody or control of the Contractor or any of his Subcontractors, machinery and equipment. The Contractor shall comply with, and ensure that the Contractor's personnel and subcontracted personnel comply with all current applicable local, state and federal policies, regulations and standards relating to safety and health, including, by way of illustration and not limitation, the standards of the Virginia Occupational Safety and Health Administration for the General Industry and for the Construction Industry, the Federal Environmental Protection Agency Standards, the Manual of Accident Prevention in Construction published by the Associated General Contractors of America and the applicable standards of the Virginia Department of Environmental Quality.
- .3 Other property at or adjacent to the Work, including trees, shrubs, lawns, walks, pavements, roadways, structures and utilities not designated for removal, relocation or replacement in the course of construction.

10.2.2 The Contractor shall give all notices and comply with applicable laws, ordinances, permits, rules, regulations and orders of any public authority bearing on the safety of persons or property or their protection from damage, injury or loss.

GENERAL CONDITIONS

- 10.2.3** The Contractor shall at all times safely guard the Owner's property from injury or losses in connection with this Contract. He shall at all times safely guard and protect his own work and adjacent property as provided by law and the Contract Documents from damage. All security personnel, passageways, guard fences, lights, and other facilities required for protection of the property and the Work described herein shall be provided and maintained at the Contractor's expense.
- 10.2.4** The Contractor shall erect and maintain, as required by existing conditions and progress of the Work, all reasonable safeguards for safety and protection, including danger signs and other warnings against hazards, promulgating safety regulations and notifying owners and users of adjacent utilities.
- 10.2.5** When the use or storage of explosives or other hazardous materials or equipment is necessary for the execution of the Work, the Contractor shall exercise the utmost care and shall carry on such activities under the supervision of properly qualified personnel.
- 10.2.6** The Contractor shall promptly remedy at his own cost and expense all damage or loss to any property referred to in Articles 10.2.1.2 and 10.2.1.3. The Contractor shall perform such restoration by underpinning, repainting, rebuilding, replanting, or otherwise restoring as may be required or directed by the Owner's Project Manager or shall make good such damage in a satisfactory and acceptable manner. In case of failure on the part of the Contractor to promptly restore such property or make good such damage, the Owner may, upon two days written notice, proceed to repair, rebuild or otherwise restore such property as may be necessary, and the cost thereof will be deducted from any monies due or to become due to the Contractor under the Contract.
- 10.2.7** The Contractor shall give notice in writing at least 48 hours before breaking ground, to the Owner, all persons, Public Utility Companies, superintendents, inspectors or those otherwise in charge of property, streets, water pipes, gas pipes, sewer pipes, telephone cables, electric cables, railroads or otherwise, who may be affected by the Contractor's operation, in order that they may remove any obstruction for which they are responsible and have a representative on site to see that their property is properly protected. The Contractor is responsible for any damages or claims resulting from any excavation and shall defend, fully indemnify, and hold harmless the Owner from all actions resulting from such work regardless of whether the Contractor gave proper notice under this clause.
- 10.2.8** The Contractor shall protect all utilities encountered while performing its work, whether indicated on the Contract Documents or not. The Contractor shall maintain utilities in service until moved or abandoned. The Contractor shall exercise due care when excavating around utilities and shall restore any damaged utilities to the same condition or better as existed prior to starting the Work, at no cost to the Owner. The Contractor shall maintain operating utilities or other

GENERAL CONDITIONS

services, even if they are shown to be abandoned on the Contract Drawings, in service until new facilities are provided, tested and ready for use.

- 10.2.9** The Contractor shall return all improvements on or about the site and adjacent property that are not shown to be altered, removed or otherwise changed to conditions that existed prior to starting work.
- 10.2.10** The Contractor shall protect the Work, including but not limited to, the site, stored materials and equipment, excavations, and excavated or stockpiled soil or other material, intended for use in the Work, and shall take all necessary precautions to prevent or minimize damage to same or detrimental effect upon his performance or that of his Subcontractors, caused by or due to rain, run-off, floods, temperature, wind, dust, sand, and flying debris. For example, but not by way of limitation, Contractor shall, when necessary, utilize temporary dikes, channels or pumping to carry-off, divert or drain water, and as necessary tie-down or otherwise secure the Work and employ appropriate covers and screens.
- 10.2.11** The Contractor shall be responsible for the prevention of accidents and the protection of material, equipment and property.
- 10.2.12** The Contractor shall not load or permit any part of the Work to be loaded so as to endanger the safety of the Work, persons or adjacent property.
- 10.2.13** The Contractor has sole and complete responsibility for the correction of any safety violation and sole liability for the consequences of the violation. The Contractor shall give prompt written notice of any safety violation to the Owner's Project Manager.
- 10.2.14** The Contractor shall provide, or cause to be provided, all technical expertise, qualified personnel, equipment, tools and material to safely accomplish the Work, specified to be performed by the Contractor and Subcontractor(s).
- 10.2.15** The Contractor shall be responsible for the preservation of all public and private property, trees, monuments, etc., along and adjacent to the street and/or right-of-way, and shall use every precaution to prevent damage to pipes, conduits and other underground structures, curbs, pavements, etc., except those to be removed or abandoned in place and shall protect carefully from disturbance or damage all monuments and property marks until an authorized agent has witnessed or otherwise referenced their location and shall not remove them until directed. Any damage which occurs by reason of the operations under this Contract shall be completely repaired by the Contractor at the Contractor's expense.
- 10.2.16** The Contractor shall shore, brace, underpin, secure, and protect, as may be necessary, all foundations and other parts of existing structures adjacent to,

GENERAL CONDITIONS

adjoining, and in the vicinity of the site that may be affected in any way by excavations or other operations connected with the Work contained in this Contract. The Contractor shall be responsible for the giving of any and all required notices to any adjoining or adjacent property owned or other party before commencement of any Work. The Contractor shall indemnify and save the Owner harmless from any damages on account of settlements or loss of all damages for which the Owner may become liable in consequence of such injury or damage to adjoining and adjacent structures and their premises.

10.2.17 The Contractor shall identify to the Owner's Project Manager at least one on-site person who is the Contractor's competent, qualified, and authorized person on the worksite and who is, by training or experience, familiar with policies, regulations and standards applicable to the Work being performed. The competent, qualified and authorized person must be capable of identifying existing and predictable hazards in the surroundings or working conditions which are unsanitary, hazardous or dangerous to employees, shall be capable of ensuring that applicable safety regulations are complied with, and shall have the authority and responsibility to take prompt corrective measures, which may include removal of the Contractor's personnel from the work site.

10.2.18 The Contractor shall provide to the Owner's Project Manager, a copy of the Contractor's written safety policies and safety procedures applicable to the Work within seven (7) days of the issuance of the Notice to Proceed.

10.3 EMERGENCIES

10.3.1 In any emergency affecting the safety of persons or property, the Contractor shall act to prevent threatened damage, injury, or loss to the Owner. The Contractor shall notify the Owner's Project Manager of the situation and all actions taken immediately thereafter. If, in the opinion of the Contractor, immediate action is not required, the Contractor shall notify the Owner's Project Manager of the emergency situation and take necessary steps. If any loss, damage, injury or death occurs that could have been prevented by the Contractor's prompt and immediate action or the emergency resulted from acts or omissions of the Contractor or his Subcontractors, or anyone directly or indirectly employed by any of them, or by anyone whose acts any of them may be liable, the Contractor shall defend, fully indemnify and hold harmless the Owner (including attorneys' fees) from all actions resulting from the emergency. Any additional compensation or extension of time claimed by the Contractor on account of emergency work shall be determined as provided in Article 12 "CHANGES IN THE WORK."

10.3.2 Prior to commencing his work and at all times during the performance of the Work, the Contractor shall provide the Owner with two, 24-hour emergency phone numbers where his representatives can be contacted.

END OF ARTICLE 10

GENERAL CONDITIONS

ARTICLE 11: BONDS AND INSURANCE

11.1 BONDS

- 11.1.1** The Contractor shall furnish to the Owner a performance bond in the sum of the contract price executed by a surety authorized to do business in Virginia, payable to the Town of Leesburg, Virginia, or such other entity as may be identified in the Contract, and conditioned upon the faithful performance of the contract in strict conformity with the plans, specifications, and conditions of the Contract Documents.
- 11.1.2** The Contractor shall furnish to the Owner a payment bond in the amount of the contract price payable to the Town of Leesburg or such other entity as may be identified in the Contract, and executed by a surety authorized to do business in Virginia. Such bond shall be conditioned on the prompt payment to all claimants who have and fulfill contracts to supply labor or materials to the Contractor for all material furnished or labor supplied or performed in the prosecution of the Work. "Labor and materials" shall include public utility services and reasonable rentals of equipment, but only for periods when the equipment rented is actually used at the project site.
- 11.1.3** If the amount of all Work subcontracted to any one Subcontractor is in excess of \$10,000, the Contractor may at his option require the Subcontractor to furnish a Labor and Material Payment Bond with surety thereon, in the amount of fifty percent of the amount of the Subcontract.
- 11.1.4** The Contractor shall ensure that all sureties providing bonds for the Project will give written notice to the Owner, at least thirty days prior to expiration or termination of the bond(s).
- 11.1.5** If the surety on any Bond furnished by the Contractor is declared bankrupt or becomes insolvent or its right to do business is terminated in any state where any part of the Project is located, the Contractor shall within five days thereafter substitute another Bond and surety, both of which shall be acceptable to the Owner.
- 11.1.6** If at any time, the Owner shall be or become dissatisfied with any surety or sureties then upon the Performance and Labor and Materials Payment Bonds, or if for any other reason, such bond shall cease to be adequate security to the Owner, the Contractor shall within five days after notice from the Owner to do so, substitute an acceptable bond(s) in such form and sum and signed by such other sureties as may be satisfactory to the Owner. The premium on such bond(s) shall be paid by the Contractor. No further payment shall be deemed due nor shall be made until the new sureties have been qualified and accepted by the Owner.
- 11.1.7** If more than one surety executes a bond, each shall be jointly and severally liable to the Owner for the entire amount of the bond.

GENERAL CONDITIONS

11.2 CONTRACTOR'S LIABILITY INSURANCE

11.2.1 The Contractor shall provide to the Owner, a Certificate of Insurance indicating that the Contractor has in force the coverage below prior to the start of any Work under this Contract. The Contractor agrees to maintain such insurance until the completion of this Contract. All required insurance coverages must be acquired from insurers authorized to do business in the Commonwealth of Virginia and acceptable to the Owner. The minimum insurance coverage shall be:

- .1 Workers Compensation Insurance – as required by federal, state, and municipal laws for the protection of all Contractors' employees working on or in connection with the project, shall be in accordance with Title, 2.2-4332, Va. Code Ann.
- .2 Comprehensive General Liability Bodily Injury and Property Damage: \$3,000,000 combined single limit/each occurrence in the primary policy or through the use of Umbrella or Excess Limits.

The General Liability Insurance shall include the following coverages; comprehensive form, premises-operations, explosion and collapse hazard, underground hazard, products/completed operations hazard, contractual liability insurance, broad form property damage including completed operations, contractors protective liability, personal injury (all insuring agreements) deleting the employee exclusion, and owners protective liability.

- .3 Contractor's Automobile Liability (Bodily Injury and Property Damage):

\$3,000,000 combined single limit per occurrence in the primary policy or through the use of Umbrella or Excess Limit

The Automobile Liability Insurance shall include the following coverages; comprehensive form, owned, hired, and non-owned.

- .4 Property insurance written on a builder's risk "all-risk" or equivalent policy form in the amount of the initial Contract Sum, plus value of subsequent Contract modifications and cost of materials supplied or installed by others, comprising total value for the entire Project at the site on a replacement cost basis without optional deductibles. Such property insurance shall be maintained, unless otherwise provided in the Contract Documents or otherwise agreed in writing by all persons and entities who are beneficiaries of such insurance, until final payment has been made as provided in Article 9.8 or until no person or entity other than the Owner has

GENERAL CONDITIONS

an insurable interest in the property required by this Article 11.5 to be covered, whichever is later. This insurance shall include interests of the Owner, the Contractor, Subcontractors and Sub-subcontractors in the Project. The property insurance shall be on an "all-risk" or equivalent policy form and shall include, without limitation, insurance against the perils of fire (with extended coverage) and physical loss or damage including, without duplication of coverage, theft, vandalism, malicious mischief, collapse, earthquake, flood, windstorm, falsework, testing and startup, temporary buildings and debris removal including demolition occasioned by enforcement of any applicable legal requirements.

If the liability insurance purchased by the Corporation has been issued on a "claims made" basis, the Corporation must comply with the following additional conditions. The limits of liability and the extensions to be included as described previously in these provisions, remain the same.

The Corporation must either:

1. Agree to provide certificates of insurance evidencing the above coverage for a period of two (2) years after final payment for the Agreement for General Liability policies. This certificate shall evidence a "retroactive date" no later than the beginning of the Corporation's work under this Agreement, or
2. Purchase the extended reporting period endorsement for the policy or policies in force during the term of this Agreement and evidence the purchase of this extended reporting period endorsement by means of a certificate of insurance or a copy of the endorsement itself.

11.2.2 Additional Insured – The Owner, its officers, elected and appointed officials, and employees shall be named as an additional insured in the Contractor's Commercial General Liability policy; evidence of the Additional Insured endorsement shall be typed on the certificate and a copy of the additional insured endorsement shall be forwarded to the Owner along with the copy of the insurance certificate.

11.2.3 Contract Identification – The insurance certificate shall state this Contract's number and title.

11.2.4 The Contractor shall secure and maintain until all work required under the Contract is accepted, such insurance as will protect the Contractor and the Owner from claims directly or indirectly arising or alleged to arise out of the performance of, or failure to perform the Work, or the condition of the Work or the jobsite, from claims by workers, suppliers, Subcontractors, and the general public; from claims made under safe place laws, or any law with respect to protection of adjacent landowners; and from any other claims for damages to property from operations by the Contractor or any Subcontractor,

GENERAL CONDITIONS

or anyone directly or indirectly employed by either of them.

The Contractor assumes all risks for direct and indirect damage or injury to the property or persons used or employed on or in connection with the Work contracted for, and of all damage or injury to any person or property wherever located, resulting from any action, omission, commission or operation under the Contract, or in connection in any way whatsoever with the contracted Work.

No acceptance or approval of any insurance by the Owner shall be construed as relieving or excusing the Contractor from any liability or obligation imposed upon the Contractor by the provisions of the Contract Documents.

- 11.2.5** These certificates and the insurance policies required by Article 11.2 shall contain a provision that coverages afforded under the policies will not be canceled or allowed to expire until at least thirty days prior written notice has been given to the Owner. If any of the foregoing insurance coverages are required to remain in force after final payment and are reasonably available, an additional certificate evidencing continuation of such coverage shall be submitted with the final Application for Payment as required by Article 9.8. Information concerning reduction of coverage on account of revised limits or claims paid under the General Aggregate, or both, shall be furnished by the Contractor with reasonable promptness in accordance with the Contractor's information and belief.
- 11.2.6** Neither the Owner nor the Owner's Project Manager shall have any obligation to review any Certificates of Insurance provided by the Contractor or to check or verify the Contractor's compliance with any and all requirements regarding insurance imposed by the Contract. The Contractor is fully liable for the amounts and types of insurance required herein and is not excused should any policy or Certificate of Insurance provided by the Contractor not comply with the Contract's insurance requirements.
- 11.2.7** If the Contractor fails to comply with the Contract's insurance requirements, the Owner shall be entitled to recover all amounts payable as a matter of law to the Owner or any other parties, including but not limited to the Owner's Project Manager, had the insurance coverage been in effect. Any recovery shall include but is not limited to interest for the loss of the use of such amounts of money, attorneys' fees, costs and expenses incurred in securing such determination and any other consequential damages.
- 11.2.8** Partial occupancy or use in accordance with Article 9.9 shall not commence until the insurance company or companies providing property insurance have consented to such partial occupancy or use by endorsement or otherwise. The Owner and the Contractor shall take reasonable steps to obtain consent of the insurance company or companies and shall, without mutual written consent, take no action with respect to partial occupancy or use that would cause cancellation, lapse or reduction of insurance.

GENERAL CONDITIONS

11.3 WAIVERS OF SUBROGATION

11.3.1 The Owner and Contractor waive all rights against (1) each other and any of the Subcontractors, Sub-subcontractors, agents and employees, each of the other, and (2) the Owner's Project Manager and Engineer or Architect or their consultants, separate contractors, if any, and any of their Subcontractors, Sub-subcontractors, agents and employees, for damages caused by fire or other causes of loss to the extent covered by property insurance obtained pursuant to this Article 11.5 or other property insurance applicable to the Work, except such rights as they have to proceeds of such insurance held by the Owner as fiduciary. The Owner or Contractor, as appropriate, shall require of his consultants, separate contractors, if any, and the Subcontractors, Sub-subcontractors, agents and employees of any of them, by appropriate agreements, written where legally required for validity, similar waivers each in favor of other parties enumerated herein. The policies shall provide such waivers of subrogation by endorsement or otherwise. A waiver of subrogation shall be effective as to a person or entity even though that person or entity would otherwise have a duty of indemnification, contractual or otherwise, did not pay the insurance premium directly or indirectly, and whether or not the person or entity had an insurable interest in the property damaged.

11.4 ADDITIONAL INSURANCE PROVISIONS

11.4.1 A loss insured under Owner's property insurance shall be adjusted by the Owner as fiduciary and made payable to the Owner as fiduciary for the insureds, as their interests may appear, subject to requirements of any applicable mortgagee clause and of Article 11.5.10. The Contractor shall pay Subcontractors their just shares of insurance proceeds received by the Contractor, and by appropriate agreements, written where legally required for validity, shall require Subcontractors to make payments to their Sub-subcontractors in similar manner.

11.4.2 If required in writing by a party in interest, the Owner as fiduciary shall, upon occurrence of an insured loss, give bond for proper performance of the Owner's duties. The cost of required bonds shall be charged against proceeds received as fiduciary. The Owner shall deposit in a separate account proceeds so received, which the Owner shall distribute in accordance with such agreement as the parties in interest may reach. If after such loss no other special agreement is made and unless the Owner terminates the Contract for convenience, replacement of damaged property shall be performed by the Contractor after notification of a Change in the Work in accordance with Article 12.

11.4.3 The Owner as fiduciary shall have power to adjust and settle a loss with insurers unless one of the parties in interest shall object in writing within five days after occurrence of loss to the Owner's exercise of this power; if such objection is made, the dispute shall be resolved as provided in Article 7.4. The Owner as fiduciary shall, in the case of disputes, make settlement with insurers in accordance with orders of the Court.

END OF ARTICLE 11

GENERAL CONDITIONS

ARTICLE 12: CHANGES IN THE WORK

12.1 CHANGES IN THE WORK

12.1.1 The Owner, without invalidating the Contract and without notice to the surety, may order a Change in the Work consisting of additions, deletions, modifications or other revisions to the general scope of the Contract, or changes in the sequence of the performance of the Work. The Contract Price and the Contract Time shall be adjusted accordingly. All such Changes in the Work shall be authorized by written Change Order, and all Work involved in a Change shall be performed in accordance with the terms and conditions of this Contract. If the Contractor should proceed with a Change in the Work upon an oral order, by whomever given, it shall constitute a waiver by the Contractor of any claim for an increase in the Contract Price or Contract Time, on account thereof.

12.1.2 When the Owner and the Contractor have agreed upon a Change in the Work, but a written Change Order Document has not yet been executed, the Owner may, at its sole discretion and option, direct in writing the Contractor to proceed with the Change in the Work pending the execution of the formal Change Order. Contractor shall proceed in accordance with such direction.

12.1.3 The Contractor shall not begin work on any alteration requiring a modification until such modification has been executed by the Owner and the Contractor. If a satisfactory agreement cannot be agreed to for any item requiring a modification, the Owner reserves the right to terminate the contract as it applies to the items in question and make such arrangements as may be deemed necessary to complete the Work.

12.2 FIELD ORDER

12.2.1 A Field Order is a written order to the Contractor signed by the Owner or the Owner's Project Manager interpreting or clarifying the Contract Documents or directing the Contractor to perform minor changes in the Work. Any work relating to the issuance of a Field Order shall be performed promptly and expeditiously and without additional cost to the Owner and within the Contract Time, unless the Contractor submits a Proposed Change Order, defined below, which is approved by the Owner. Field Orders shall be numbered consecutively by date of issuance by the Owner or the Owner's Project Manager.

12.3 REQUEST FOR PROPOSAL

12.3.1 A Request For Proposal (“RFP”) describes a proposed Change in the Work. In response to a Request for Proposal issued by the Owner or the Owner’s Project Manager, the Contractor is required to submit a complete Proposal for the total cost and additional time, if any, necessary to perform the proposed Change in the

GENERAL CONDITIONS

Work. Requests For Proposals shall be numbered consecutively by date of issuance by the Owner or the Owner's Project Manager.

12.3.2 The Contractor's Proposal in response to an RFP shall be in the form prescribed by the Owner's Project Manager, including all appropriate back-up material.

12.4 PROPOSED CHANGE ORDER

12.4.1 A Proposed Change Order is a written request from the Contractor to the Owner requesting a change in the Contract Price and/or Contract Time. A Proposed Change Order may be submitted as a proposal in response to a Request For Proposal issued by the Owner or as a claim for an increase in the Contract Price and/or Contract Time pursuant to the issuance of a Field Order. A Proposed Change Order must be submitted within twenty days of the issuance of a Request For Proposal or a Field Order. Proposed Change Orders shall be numbered consecutively by date of issuance by the Contractor. The Contractor shall also indicate on the Proposed Change Order the number of the Request For Proposal or the Field Order to which it responds.

12.4.2 If a Request for Proposal provides for an adjustment to the Contract Price, the adjustment shall be based on one of the following methods:

- .1 mutual acceptance of a lump sum properly itemized and supported by sufficient substantiating data to permit evaluation;
- .2 unit prices stated in the Contract Documents or subsequently agreed upon;
- .3 cost to be determined in a manner agreed upon by the parties and a mutually acceptable fixed or percentage fee; or
- .4 as provided in Articles 12.5.3 and 12.5.4.

12.4.3 If it is necessary in this subparagraph to increase the Contract Time to perform the Change in the Work, the Contractor shall provide an estimate of the increase in the Contract Time which shall be negotiated by the parties to the Contract. The Contractor's request for a time extension shall be evaluated in accordance with the criteria described in Article 8.

12.4.4 If the Contractor's Proposed Change Order is rejected by the Owner as being within the scope of the Work required by the Contract Documents the Owner may, at its sole option and discretion, direct the Contractor to perform the Work which is the subject of the Proposed Change Order; the Contractor shall then promptly proceed with the Work. Nothing shall excuse the timely performance by the Contractor of the Work because any Proposed Change Order is pending.

GENERAL CONDITIONS

12.5 CHANGE ORDER

12.5.1 A Change Order is a written order to the Contractor signed by the Contractor and the Owner's Project Manager, issued after execution of the Contract, authorizing a Change in the Work or an adjustment in the Contract Price and/or the Contract Time. The Contract Price and the Contract Time may be changed only by Change Order. A Change Order signed by the Contractor indicates his agreement therein, including the adjustment in the Contract Price and/or the Contract Time. Change Orders shall be numbered consecutively by date of issuance by the Owner or the Owner's Project Manager and shall, if applicable, indicate the number of the Field Order(s), Request For Proposal(s) and/or Proposed Change Order(s) to which it relates.

12.5.2 If the Owner and the Owner's Project Manager determine that the Contractor's Proposed Change Order, submitted pursuant to Article 12.4 for a change in the Contract Price or Contract Time, is acceptable, the Owner's Project Manager shall prepare and issue, or cause to be prepared and issued, a Change Order which will authorize the Contractor to proceed with the Change in the Work for the cost and time stated in the Proposed Change Order, or as otherwise may be agreed upon by the parties. The amounts stated in the Change Order for the cost and time to perform the Change in the Work shall be binding on the parties.

.1 The contractors markup for allowable profit and overhead shall be limited to 10%.

12.5.3 After issuance of the Change Order, the Contractor shall ensure that the amount of the Performance and Payment Bond coverage has been revised to reflect the increase in the Contract Price due to the Change Order.

12.5.4 If the Contractor's Proposed Change Order is not acceptable to the Owner and the Owner's Project Manager or if the parties are unable to otherwise agree as to the cost and time necessary to perform the Change in the Work, the Owner may, at its sole option and discretion, direct the Contractor to perform the Work on a time and material basis. The Contractor shall then promptly proceed with the Work.

12.5.5 If the Owner and the Owner's Project Manager elect to have the Change in the Work performed on a time and material basis, the same shall be performed, whether by the Contractor's forces or the forces of any of his Subcontractors or Sub-subcontractor's, at actual cost to the entity performing the Change in accordance with the time and material provisions included in the Road and Bridge Specifications of the Virginia Department of Transportation, current edition.

12.5.6 Prior to starting the work on a time and material basis, the Contractor shall notify the Owner's Project Manager in writing as to what labor, materials, equipment or

GENERAL CONDITIONS

rentals are to be used for the Change in the Work. During the performance of the Change, the Contractor shall submit to the Owner daily time and material tickets, which shall list the categories and amounts of labor and equipment for which Change Order compensation is to be charged for the previous work day. Such tickets shall be submitted in strict accordance with the time and material provisions included in the Road and Bridge Specifications of the Virginia Department of Transportation.

- 12.5.7** The Contractor shall commence submission of daily time and material tickets immediately upon commencement of the Change Order Work and continue to submit them until completion of the Change Order Work. The Owner may require authentication of all time and material tickets and invoices by persons designated by the Owner for such purpose.
- 12.5.8** The failure of the Contractor to provide any required authentication shall, if the Owner elects to treat it as such, constitute a waiver by the Contractor of any claim for the cost of that portion of the Change in the Work covered by a non-authenticated ticket or invoice; provided, however, that the authentication of any such ticket or invoice by the Owner shall not constitute an acknowledgment by the Owner that the items thereon were reasonably required for the Change in the Work.
- 12.5.9** The Contractor shall submit his complete submission of the reasonable actual cost and time to perform the Change in the Work within twenty days of the request of the Owner's Project Manager to do so. The Owner and the Owner's Project Manager shall review the costs and time submitted by the Contractor on the basis of reasonable expenditures and savings of those performing the Change in the Work. If such costs and time are acceptable to the Owner and the Owner's Project Manager, or if the parties otherwise agree to the actual reasonable cost to perform the Change in the Work, the Owner's Project Manager shall issue a Change Order for the cost and time agreed upon. The amounts stated in the Change Order for the cost and time to perform the Change in the Work shall be binding upon the parties.
- 12.5.10** The Contractor shall be entitled to costs as provided for in Article 12.4 which the Contractor, or his Subcontractors, may incur as a result of delays, interferences, suspensions, changes in sequence or the like, which are unreasonable, arising from the performance of any and all changes in the Work, caused by acts or omissions of the Owner, performed pursuant to this Article 12.
- 12.5.11** If any dispute should arise between the parties with respect to an increase or decrease in the Contract Price or an extension or reduction in the Contract Time or as a result of a Change in the Work, the Contractor shall not suspend performance of a Change in the Work or the Work itself unless otherwise so ordered by the Owner's Project Manager in writing. Disputes must be resolved

GENERAL CONDITIONS

pursuant to Article 7.4 of the Contract. The Owner will, however, pay the Contractor up to the Owner's Project Manager's estimated value of the Change in the Work, regardless of the dispute, if the Change in the Work results in an increase in the Contract Price; and the Owner will have the right to decrease the Contract Price up to the Owner's Project Manager's estimated value of the Change in the Work, regardless of the dispute, if the Change in the Work results in a decrease in the Contract Price.

12.6 UNILATERAL CHANGE ORDER

12.6.1 In the event that the parties are unable to agree as to the reasonable cost and time to perform the Change in the Work and the Owner does not elect to have the Change in the Work performed on a time and material basis, the Owner and the Owner's Project Manager shall make a unilateral determination of the reasonable cost and time to perform the Change in the Work, based upon their own estimates, the Contractor's submission or a combination thereof. A Change Order shall be issued for the amounts of cost and time determined by the Owner and the Owner's Project Manager and shall become binding upon the Contractor unless the Contractor submits his protest in writing to the Owner within ten days of the issuance of the Change Order. The procedure for the resolution of the Contractor's protest shall be as described in Article 12.10. The Owner has the right to direct in writing the Contractor to perform the Change in the Work, which is the subject of such Unilateral Change Order. Failure of the parties to reach an agreement regarding the cost and time of performing the Change in the Work, or any pending protest, shall not relieve the Contractor from performing the Change in the Work promptly and expeditiously.

12.7 DECREASES AND WORK NOT PERFORMED

12.7.1 Should it be deemed expedient by the Owner or the Owner's Project Manager at any time that the Contract Work is in progress to decrease the dimensions, quantity of material or work, or vary in any other way the Work herein contracted for, the Owner or the Owner's Project Manager shall have the full power to do so, and shall order, in writing, such decreases to be made or performed without affecting the enforcement of the Contract. The Contractor shall, in pursuance of such written orders and directions from the Owner or the Owner's Project Manager, execute the work ordered, and the difference in expense occasioned by such decrease so ordered shall be deducted from the amount payable under this Contract.

12.7.2 If Work is not performed, and such deletion of Work is not approved by the Owner, the Owner's Project Manager shall ascertain the amount of the credit due the Owner, based on the reasonable value of the labor and materials so deleted, for the lesser amount of materials and labor required.

GENERAL CONDITIONS

12.7.3 If Work is deleted from the Contract by Change Order, the amounts to be credited to the Owner shall reflect the same current pricing as if the Work were being added to the Contract at the time the deletion is ordered, and documentation will be required for a credit as specified in Article 12.4. If such deleted materials and equipment shall have already been purchased and stored on site and cannot be used in other projects or returned for credit or cannot be returned for credit at the price paid by the Contractor at the time of purchase, the Contractor shall be entitled, upon proper documentation and certification, to an adjustment in the pricing of the credit to avoid hardship to the Contractor. If necessary in order to establish such reasonable value, the Contractor may be required to submit a detailed breakdown of his original bid for the items or Work involved.

12.8 CHANGES IN LINE AND GRADE

12.8.1 The Owner reserves the right through the Owner's Project Manager to make such alterations in the line and grade of various structures or pipelines shown on the drawings, as may be necessitated by conditions found during construction or that in the judgment of the Owner's Project Manager appears advisable. The Contractor shall not claim forfeiture of Contract by reason of such changes by the Owner's Project Manager.

12.8.2 In case of a fixed price contract, the price of the Work shall be negotiated as herein provided. If such alterations or changes diminish the quantity of Work to be done, they shall not constitute a claim for damages or for loss of anticipated profits in the Work which may be dispensed with, and the Work as constructed shall be paid for in accordance with the Contract prices as established for such Work under this Contract. In the case of a unit price, or partial unit price, contract, the altered Work shall be performed at the appropriate unit price.

12.8.3 The Contractor shall employ a certified Land Surveyor to establish a base line and set bench marks for the Contractor's use as necessary to stake the basic layout of the Work. Where new construction connects to existing facilities, it shall be the responsibility of the Contractor to check and establish the location of all existing facilities prior to construction of the new facilities.

12.8.4 All stakes, bench marks, and other base line information provided by the Owner or the Owner's Project Manager shall be carefully preserved by the Contractor, and in case of their removal by any cause without prior written consent from the Owner, such stakes, bench marks, and other base line information will be replaced by the Contractor at the Contractor's sole expense.

12.8.5 The dimensions for lines and elevations for grades of the structures, appurtenances, and utilities are indicated on the Drawings, together with pertinent information required for laying out the Work. Utility locations are approximate and it shall be the Contractor's responsibility to determine the exact location of

GENERAL CONDITIONS

the utilities prior to commencing Work in all areas where conflicts with utility installations are possible. If site conditions vary from those indicated, the Contractor shall notify the Owner immediately, who will promptly direct any adjustment as required. The locations of existing utilities, including underground utilities, which may affect the Work, are indicated on the drawings or in the specifications insofar as their existence and location were known at the time of preparation of the drawings. However, nothing in these drawings or specifications shall be construed as a guarantee that such utilities are in the location indicated or that they actually exist, or that other utilities are not within the area of the operations. The Contractor shall make all necessary investigations to determine the existence and locations of such utilities. The Contractor will be held responsible for any damage to and maintenance and protection of existing utilities and structures, of both public and private ownership. Acceptability of restored utility installation shall be determined by the respective utility Owner. All utilities shall remain in service during the construction of this project unless written authorization of interruption of service is received from the respective utility Owner and the interruption is approved by the Project Manager.

- 12.8.6** Contractor shall notify the Owner immediately upon discovery of any apparent errors in the lines or grades. If Contractor proceeds with knowledge of such apparent error without first receiving written clarification from the Owner's Project Manager, the Contractor does so at his own risk.

12.9 DIFFERING SITE CONDITIONS

- 12.9.1** The Contractor shall promptly, and before the conditions are disturbed, give written notice to the Owner's Project Manager of (a) subsurface or latent physical conditions at the site which differ materially from those indicated in the Contract Documents, or (b) unknown physical conditions at the site, of an unusual nature, which differ materially from those ordinarily encountered and generally recognized as inhering in work of the character provided for in the Contract and which were not reasonably anticipated as a result of the investigation required by Article 1.2.2.
- 12.9.2** The Owner's Project Manager shall investigate the site conditions promptly after receiving the notice. If the conditions do materially so differ and cause an increase or decrease in the cost or time of performance, the provisions of Article 12 "Changes in the Work" shall apply.
- 12.9.3** No request by the Contractor for a Change Order under this Article shall be allowed, unless the Contractor has given the required written notice.
- 12.9.4** No request by the Contractor for a Change Order under this Article shall be allowed if made after final payment under the Contract.

GENERAL CONDITIONS

12.10 CLAIMS FOR ADDITIONAL COST AND/OR TIME

12.10.1 If the Contractor wishes to make a claim for an increase in the Contract Price and/or Contract Time, he shall give the Owner written notice thereof within seven calendar days after the occurrence of the event giving rise to such claim. This notice shall be given by the Contractor before proceeding to execute the Work, except in an emergency endangering life or property in which case the Contractor shall proceed as provided in Article 10. No claim shall be allowed and no amounts shall be paid for any costs incurred more than ten calendar days prior to the time notice is given to the Owner. Any change in the Contract Price or Contract Time resulting from such claim must be authorized by Change Order. The Contractor's complete claim submittal for an increase in the Contract Price shall be submitted no later than twenty calendar days after the Work for which the claim is made has been completed or after the request of the Owner or the Owner's Project Manager, whichever is earlier.

12.10.2 If the Contractor claims that additional cost or time is involved because of, but not limited to, any of the following circumstances, the Contractor shall make such claim as provided in Subparagraph 12.10.1: (1) any written interpretation pursuant to Article 2, (2) any order by the Owner to stop the Work pursuant to Article 3.3 where the Contractor was not at fault, (3) failure of payment by the Owner pursuant to Article 9, or (4) any written order for a minor change in the Work issued pursuant to Article 12.8.1.

12.11 ATTORNEYS' FEES AND OTHER EXPENSES

12.11.1 In recognition of the public monies being administered by the Owner to fund this Contract, the Contractor agrees that he will not submit, assert, litigate or otherwise pursue any frivolous or unsubstantiated delay claims. If the Contractor's delay claim, or any separate item of a delay claim, is determined through litigation or other dispute resolution process to be false or to have no basis in law or fact, the Contractor shall be liable to the Owner and shall pay it for all Investigation Costs incurred by the Owner. These costs include investigating, analyzing, negotiating, appealing, defending, and litigating the false or baseless delay claims, attorneys' fees, audit costs, accountants' fees, expert witness' fees, additional architect/engineer expenses and any other consultant costs. The amount to be paid hereunder to the Owner shall be the percentage of the Owner's total Investigation Costs in an amount equal to the percentage of the Contractor's total delay claim which is determined to be false or to have no basis in fact.

12.11.2 If the Contractor breaches any obligation under the Contract Documents, the Contractor shall reimburse the Owner for all costs and expenses incurred by the Owner relating to such breach, including but not limited to, attorneys' fees, audit

GENERAL CONDITIONS

costs, accountants' fees, expert witness' fees, additional architectural or engineering expenses, and any other consultant costs.

- 12.11.3** If the Owner prevails in a claim brought against the Contractor, including but not limited to, claims for fraud or misrepresentation, overpayment, defective work, delay damages, and recovery of termination expenses, the Contractor shall reimburse the Owner for all costs and expenses incurred by the Owner relating to such claim, including but not limited to, attorneys' fees, audit costs, accountants' fees, expert witness' fees, additional architect or engineering expenses, and any other consultant costs.

END OF ARTICLE 12

GENERAL CONDITIONS

ARTICLE 13: UNCOVERING AND CORRECTION OF WORK

13.1 UNCOVERING OF WORK

13.1.1 If any portion of the Work should be covered contrary to the request of the Owner's Project Manager or to requirements specifically expressed in the Contract Documents or to requirements of applicable Construction Permits, it must, if required in writing by the Owner's Project Manager, be uncovered for its observation and shall be replaced at the Contractor's expense.

13.1.2 If any portion of the Work has been covered that the Owner's Project Manager has not specifically requested to observe prior to being covered, the Owner's Project Manager may request to see such Work and it shall be uncovered by the Contractor. If such Work complies with the Contract Documents, the cost of uncovering and replacement shall, by appropriate Change Order, be charged to the Owner. If such Work does not comply with the Contract Documents, the Contractor shall pay such costs unless the Owner caused this condition, in which event the Owner shall pay such costs.

13.2 CORRECTION OF WORK

13.2.1 The Contractor shall promptly reconstruct, replace or correct all Work rejected by the Owner's Project Manager as defective or as failing to conform to the Contract Documents or as not in accordance with the guarantees and warranties specified in the Contract Documents whether observed before or after Substantial Completion and whether or not fabricated, installed or completed. The Contractor shall bear all costs of correcting such rejected Work, including compensation for the Owner's Project Manager and any other additional services made necessary thereby.

13.2.2 The Contractor, unless removal is waived by the Owner, shall remove from the site all portions of the Work that are defective or non-conforming, or if permitted or required, he shall correct such Work in place at his own expense promptly after receipt of notice, and such rejected Work shall not thereafter be tendered for acceptance unless the former rejection or requirement for correction is disclosed.

13.2.3 If the Contractor does not proceed with the correction of such defective or non-conforming Work within a reasonable time fixed by written notice from the Owner's Project Manager, the Owner may either:

- .1 By separate contract or otherwise replace or correct such Work and charge the Contractor the cost occasioned the Owner thereby and remove and store the materials or equipment at the expense of the Contractor; or

GENERAL CONDITIONS

.2 Terminate this Contract as provided in Article 14.3 "DEFAULT TERMINATION."

13.2.4 The Contractor shall bear the cost of making good all work of the Owner or separate Contractors destroyed or damaged by such correction or removal.

13.2.5 Nothing contained in this Article 13.2 shall be construed to establish a period of limitation with respect to any other obligation that the Contractor might have under the Contract Documents, including Article 4.7 "WARRANTY" hereof. The establishment of the period of one year after the Date of Final Completion or such longer period of time as may be prescribed by law or by the terms of any warranty required by the Contract Documents relates only to the specific obligation of the Contractor to correct the Work, and has no relationship to the time within which his obligation to comply with the Contract Documents may be sought to be enforced, or to the time within which proceedings may be commenced to establish the Contractor's liability with respect to his obligations other than specifically to correct the Work.

13.3 ACCEPTANCE OF DEFECTIVE OR NON-CONFORMING WORK

13.3.1 If the Owner or its Project Manager prefers to accept defective or non-conforming Work, it may do so instead of requiring its removal and correction. In this case, a Change Order will be issued to reflect a reduction in the Contract Price where appropriate and equitable, or the Owner may elect to accept payment in materials or services, in lieu of a reduction in the Contract Price. If the amount of a reduction is determined after Final Payment, it shall be paid on demand to the Owner by the Contractor.

END OF ARTICLE 13

GENERAL CONDITIONS

ARTICLE 14: TERMINATION OF THE CONTRACT

14.1 TERMINATION FOR THE CONVENIENCE OF THE OWNER

14.1.1 The Owner may, at any time upon ten days written notice to the Contractor, terminate, without prejudice to any right or remedy of the Owner, the whole or any portion of the Work for the convenience of the Owner. This Notice of Termination shall specify that portion of the Work to be terminated and the effective date of termination. The Contractor's sole remedy, in the event of such termination, will be the allowable termination costs permitted by Article 14.2 "ALLOWABLE CONVENIENCE TERMINATION COSTS."

14.1.2 The Contractor shall include termination clauses identical to Article 14 in all subcontracts and purchase orders related to the Work. Failure to include these termination clauses in any subcontracts or purchase orders shall preclude recovery of any termination costs related to that subcontract or purchase order.

14.1.3 Non-appropriation Clause

Notwithstanding anything contained herein to the contrary, this contract shall be terminated if all of the following events shall have occurred:

1. Funds are not appropriated for a subsequent fiscal period during the term of this contract for the acquisition of substantially the same functions as provided for herein, and written notice thereof is given to CONTRACTOR at least thirty (30) days prior to the first day of such subsequent fiscal periods or within five (5) days of the approval of the final budget for such fiscal year, whichever occurs later.

2. Town has exhausted all funds legally available for payment under this contract.

Upon such termination, Contractor's only remedy shall be to terminate the contract at the end of the fiscal period during which notice is given. Payment in compliance with the contract for materials, goods, and services rendered hereunder during the fiscal year at the end of which termination occurs, without penalty, termination, profit or overhead expenses of any kind shall constitute full performance on the part of the Town.

14.2 ALLOWABLE CONVENIENCE TERMINATION COSTS

14.2.1 After complying with the provisions of Article 14.4, the Contractor may submit a termination claim, not later than six months after the effective date of its

GENERAL CONDITIONS

termination, unless one or more extensions of three months each are granted by the Owner in response to the Contractor's written request.

14.2.2 The Owner shall pay the Contractor's reasonable costs of termination, plus a mark-up of ten percent for profit and overhead. This amount will not exceed the original contract price, reduced by any payments made prior to Notice of Termination, and further reduced by the price of the supplies not delivered, or the service not provided. This Contract shall be amended accordingly, and the Contractor shall be paid the agreed amount.

14.2.3 If the parties cannot agree on the amount to be paid to the Contractor by reason of termination under this clause, the Owner shall pay to the Contractor the amounts, as determined by the Owner's Project Manager as follows, without duplicating any amounts which may have already been paid under the preceding paragraph of this clause:

.1 With respect to all Contract performance prior to the effective date of Notice of Termination, the total of:

- a. cost of work performed or supplies delivered;
- b. the costs of settling and paying any reasonable claims as provided in Article 14.4; and
- c. a mark-up of ten percent for profit and overhead. Neither the Contractor nor any Subcontractor shall be entitled to profit or overhead associated with the portion of the work not performed, nor to profit associated with costs of demobilization.

.2 The total sum to be paid under .1 above shall not exceed the contract price, as reduced by the amount of payments otherwise made, and as further reduced by the contract price of work not done or supplies not delivered. The Owner may subtract from the amount claimed by the Contractor any claim the Owner has against the Contractor

14.2.4 If the Contractor is not satisfied with any payments that the Owner's Project Manager shall determine to be due under this clause, the Contractor may proceed in accordance with Article 7.4 "DISPUTES."

14.2.5 If the Contractor would have sustained a loss on the entire Contract had it been completed, no profit shall be included or allowed and an appropriate adjustment shall be made reducing the amount of the settlement to reflect the indicated rate of loss.

GENERAL CONDITIONS

14.3 DEFAULT TERMINATION

14.3.1 The Owner may, upon ten days written notice to the Contractor, terminate, without prejudice to any right or remedy of the Owner, the Contract for default, in whole or in part, and may take possession of the Work and complete the Work by contract or otherwise in any of the following circumstances:

- .1 The Contractor refuses or fails to prosecute the Work or any separable part thereof with such diligence as will ensure the Substantial Completion of the Work within the Contract Time, or fails to meet any milestones established in the Contract Documents or fails to substantially complete the Work within this period;
- .2 The Contractor is in default in carrying out any provision of the Contract for a cause within his or his Subcontractors' control;
- .3 The Contractor fails to supply a sufficient number of properly skilled workers or proper equipment or materials;
- .4 The Contractor fails to make prompt payment to Subcontractors or for materials or labor;
- .5 The Contractor disregards laws, permits, ordinances, rules, regulations, or orders of any public authority having jurisdiction;
- .6 The Contractor breaches any provision of the Contract Documents;
- .7 The Contractor voluntarily abandons the Project;
- .8 Upon at least thirty calendar days prior written notice by the Owner to the Contractor, at any time during the term of the Agreement, the Owner determines that maintaining the Agreement in force will harm, bring into disrepute, or affect the integrity of the Owner.

14.3.2 Upon termination of this Agreement under this Article, the Contractor shall remove all of his employees and property from the Project in a smooth, orderly, and cooperative manner.

14.3.3 The right of the Contractor to proceed shall not be terminated under Article 14.2 because of any delays in the completion of the Work due to unforeseeable causes beyond the control and without the fault or negligence of the Contractor or his Subcontractors as specifically set forth in Article 8, "DELAYS AND EXTENSIONS OF TIME."

GENERAL CONDITIONS

14.3.4 If, after the Contractor has been terminated for default pursuant to Article 14.3, it is determined that none of the circumstances set forth in Article 14.3.1 exist, then such termination shall be considered a termination for convenience pursuant to Article 14.1. In such case, the Contractor's sole remedy will be costs permitted by Article 14.2.

14.3.5 If the Owner terminates the Contract, the Contractor shall not be entitled to receive any further payment until the Work is finished. If the unpaid balance of the Contract Price exceeds the cost of completing the Work including compensation for additional managerial, administrative and inspection services and any damages for delay, such excess amount shall be paid to the Contractor. If such expenses exceed the unpaid balance, the Contractor and his sureties shall be liable to the Owner for such excess amount.

14.3.6 If the right of the Contractor to proceed with the Work is partially or fully terminated, the Owner may take possession of and utilize in completing the Work such materials, appliances, supplies, plant and equipment as may be on the site of the terminated portion of the Work and necessary for the completion of the Work. If the Owner does not fully terminate the right of the Contractor to proceed, the Contractor shall continue to perform the part of the Work that is not terminated.

14.4 GENERAL TERMINATION PROVISIONS

14.4.1 After receipt of a Notice of Termination from the Owner, pursuant to Article 14.1 or 14.3, and except as otherwise directed by the Owner, the Contractor shall:

- .1 Stop Work under the Contract on the date and to the extent specified in the Notice of Termination;
- .2 Place no further purchase orders or subcontracts for materials, services, or facilities, except as may be necessary for completion of such portion of the Work under the Contract that is not terminated;
- .3 Terminate all purchase orders and subcontracts to the extent that they relate to the performance of Work terminated by the Notice of Termination;
- .4 At the option of the Owner, assign to the Owner in the manner, at the times and to the extent directed by the Owner, all of the rights in the contracts so terminated, in which case, the Owner shall have the right, at his discretion, to settle or pay any or all claims arising out of the termination of such purchase orders and subcontracts;
- .5 Settle all outstanding liabilities and all claims arising out of such termination of purchase orders and subcontracts, with the approval

GENERAL CONDITIONS

or ratification of the Owner, to the extent he may require, which approval or ratification shall be final for all the purposes of this Article;

- .6 Transfer title and deliver to the entity or entities designated by the Owner, in the manner, at the times and to the extent directed by the Owner to the extent specifically produced or specifically acquired by the Contractor for the performance of such portion of the Work as has been terminated, the following:
 - a. The fabricated or unfabricated parts, Work in progress, partially completed supplies and equipment, materials, parts, tools, dies, jigs, and other fixtures, completed work, supplies and other material produced as part of, or acquired in connection with the performance of, the Work terminated by the Notice of Termination; and
 - b. The completed or partially completed plans, drawings, Shop Drawings, submittals, information, releases, manuals, and other property related to the Work and which, if the Contract had been completed, would have been required to be furnished to the Owner.
- .7 Use his best efforts to sell, in the manner, at the times, to the extent and at the price or prices directed or authorized by the Owner or Owner's Project Manager, any property of the types referred to in Article 14.4.1.6; provided, however, that the Contractor:
 - a. Shall not be required to extend credit to any buyer; and
 - b. May acquire such property under the conditions prescribed by and at a price or prices approved by the Owner; and provided further that the proceeds of any such transfer or disposition shall be applied in reduction of any payments to be made by the Owner to the Contractor under the Contract or shall otherwise be credited to the Contract Price covered by the Contract or paid in such other manner as the Owner may direct;
- .8 Complete performance of such part of the Work as shall not have been terminated by the Notice of Termination; and
- .9 Take such action as may be necessary, or as the Owner or Owner's Project Manager may direct for the protection and preservation of

GENERAL CONDITIONS


the property related to the Contract that is in the possession of the Contractor and in which the Owner has or may acquire an interest.




14.4.2 If the convenience termination, pursuant to Article 14.1, is partial, the Contractor may file with the Owner a claim for an equitable adjustment of the Contract Price relating to the continued portion of the Contract (the portion not terminated by the Notice of Termination) for costs increased because of such partial termination. Such equitable adjustment as may be agreed upon shall be made in the Contract Price. Any claim by the Contractor for an equitable adjustment under this Article must be submitted in writing to the Owner's Project Manager within sixty days from the Notice of Termination.

14.4.3 The Contractor shall refund to the Owner any amounts paid by the Owner to the Contractor in excess of costs reimbursed under Article 14.4 within sixty days of receipt of a written request from the Owner to do so.

END OF ARTICLE 14


****FOR INFORMATION ONLY****
Contractor MUST verify before any excavation work.



 RICE ASSOCIATES TEST HOLE FORM			
PROJECT INFORMATION			
TESTHOLE#	1	DATE	1/5/2015
PROJECT#	AA0902.01G	WEATHER	Below Freezing
PROJECT NAME	King/Market Street Leesburg Test Holes	REPORT BY	D. Lunghi
PROJECT DESCRIPTION	Test Holes	CREW	D.L, S.H, J.C
TARGET UTILITY INFORMATION			
UTILITY	Gas	O.D. UTILITY SIZE	Unknown
OWNER	Washington Gas	UTILITY TYPE	Gas
CONTACT NAME	Utilquest	COLOR	Unknown
PHONE NUMBER	703-754-2116	MATERIAL	Metallic
GENERAL LOCATION	Intersection of Market and King Street	CONDITION	Unknown
NOTES	Ground water level at approximately 5.7' in hole	SOIL	sand/clay mix
TEST HOLE COORDINATE INFORMATION			
NORTHING	7090649.659	TOP COVER	7.75'
EASTING	11748313.42	BOTTOM COVER	Unknown
ELEVATION GRADE	331.97	ELEV. UTILITY BOTTOM	Unknown
ELEV. UTILITY TOP	324.22	ALIGNMENT	N/A
INSTALLED	2 MAG Nails	STATION	N/A
B.M. #10001	Elev =332.33	OFFSET	N/A
SKETCH Not To Scale			

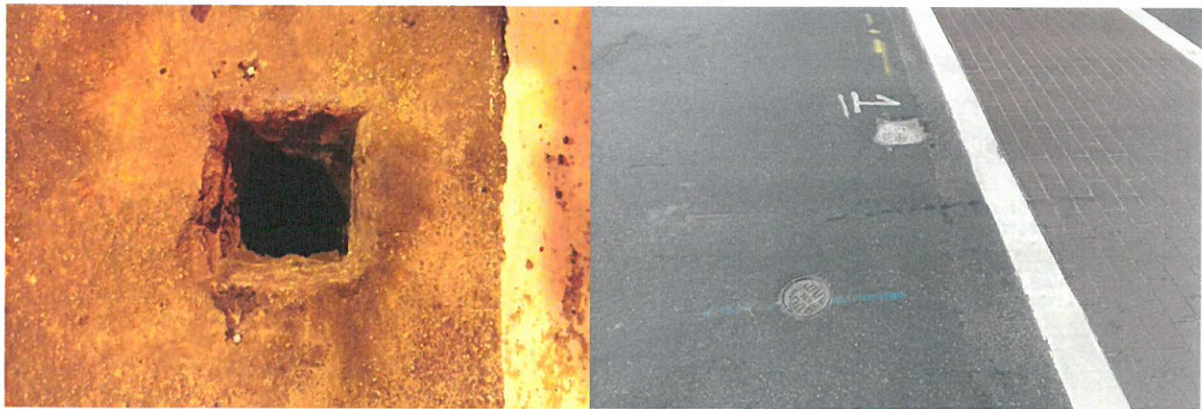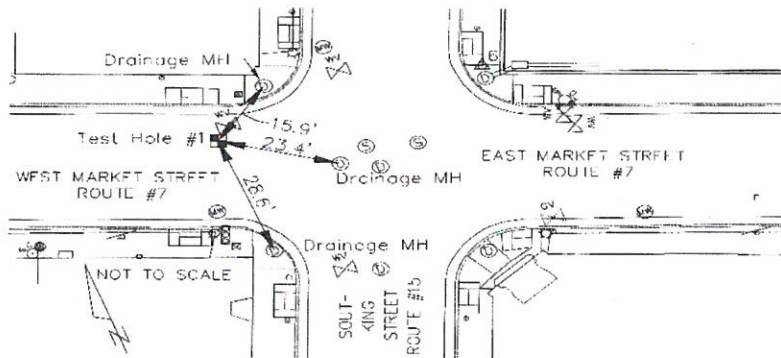

Surveying • Photogrammetry • 3-D Laser Scanning • Subsurface Utility Designation and Mapping


Corporate Office • 10625 Gaskins Way • Manassas, Virginia 20109 • Telephone 703.968.3200 • Fax 703.968.2705
Richmond Office • 308 Turner Road • Suite G • Richmond, Virginia 23225 • Telephone 804.674.9723 • Fax 804.674.9726
Virginia Beach Office • 3145 Virginia Beach Blvd. • Suite 103 • Virginia Beach, Virginia 23452 • Telephone 757.306.4260



		RICE ASSOCIATES TEST HOLE FORM	
		PROJECT INFORMATION	
TESTHOLE#	2	DATE	1/5/2015
PROJECT#	AA0902.01G	WEATHER	Below Freezing
PROJECT NAME	King/Market Street Leesburg Test Holes	REPORT BY	D. Lunghi
PROJECT DESCRIPTION	Test Holes	CREW	DL, SH, JC
		TARGET UTILITY INFORMATION	
UTILITY	Gas	O.D. UTILITY SIZE	3"
OWNER	Washington Gas	UTILITY TYPE	Gas Main
CONTACT NAME	Utiliquest	COLOR	Black
PHONE NUMBER	703-754-2116	MATERIAL	Wrapped Steel
GENERAL LOCATION	Intersection of Market and King Street	CONDITION	Excellent
NOTES	Test Hole Moved to Avoid Brick Crosswalk	SOIL	sand/clay mix
		TEST HOLE COORDINATE INFORMATION	
NORTHING	7090637.69	TOP COVER	3.45'
EASTING	11748298.34	BOTTOM COVER	3.7'
ELEVATION GRADE	331.68	ELEV. UTILITY BOTTOM	327.98
ELEV. UTILITY TOP	328.23	ALIGNMENT	N/A
INSTALLED	2 MAG Nails	STATION	N/A
B.M. #10001	Elev =332.33	OFFSET	N/A
SKETCH Not To Scale			

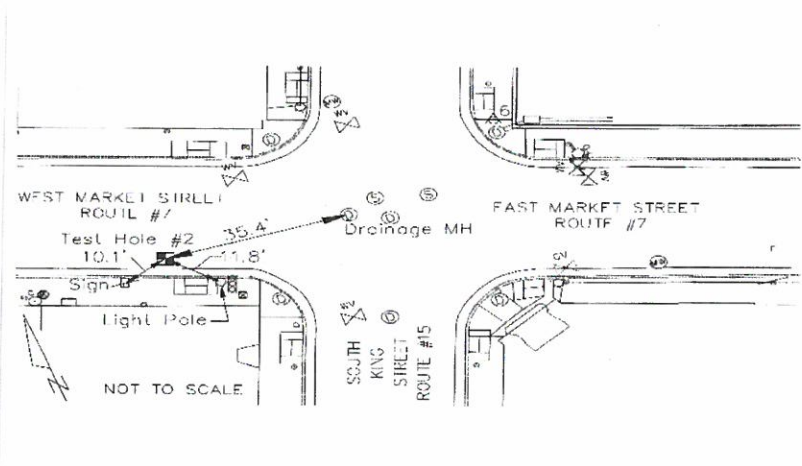

Surveying • Photogrammetry • 3-D Laser Scanning • Subsurface Utility Designation and Mapping

Corporate Office • 10625 Gaskins Way • Manassas, Virginia 20109 • Telephone 703.968.3200 • Fax 703.968.2705
 Richmond Office • 308 Turner Road • Suite G • Richmond, Virginia 23225 • Telephone 804.674.9723 • Fax 804.674.9726
 Virginia Beach Office • 3145 Virginia Beach Blvd. • Suite 103 • Virginia Beach, Virginia 23452 • Telephone 757.306.4260

		RICE ASSOCIATES TEST HOLE FORM	
PROJECT INFORMATION			
TESTHOLE#	3	DATE	1/6/2015
PROJECT#	AA0902.01G	WEATHER	Below freezing
PROJECT NAME	King/Market Street Leesburg Test Holes	REPORT BY	D. Lunghi
PROJECT DESCRIPTION	Test Holes	CREW	DL, SH, JC
TARGET UTILITY INFORMATION			
UTILITY	Water	O.D. UTILITY SIZE	Unknown
OWNER	Leesburg Water & Sewer	UTILITY TYPE	Water Main
CONTACT NAME	Leslie McClaughry	COLOR	Unknown
PHONE NUMBER	703-737-7075	MATERIAL	Metallic
GENERAL LOCATION	Intersection of Market and King Street	CONDITION	Unknkown
NOTES	Ground Water Level @ 6.88'	SOIL	sand/clay mix
No visual on pipe due to ground water, probed utility			
TEST HOLE COORDINATE INFORMATION			
NORTHING	7090645.17	TOP COVER	10.88'
EASTING	11748334.85	BOTTOM COVER	Unknown
ELEVATION GRADE	332.12	ELEV. UTILITY BOTTOM	Unknown
ELEV. UTILITY TOP	321.24	ALIGNMENT	N/A
INSTALLED	2 MAG Nails	STATION	N/A
B.M. #10001	Elev =332.33	OFFSET	N/A
SKETCH Not To Scale			

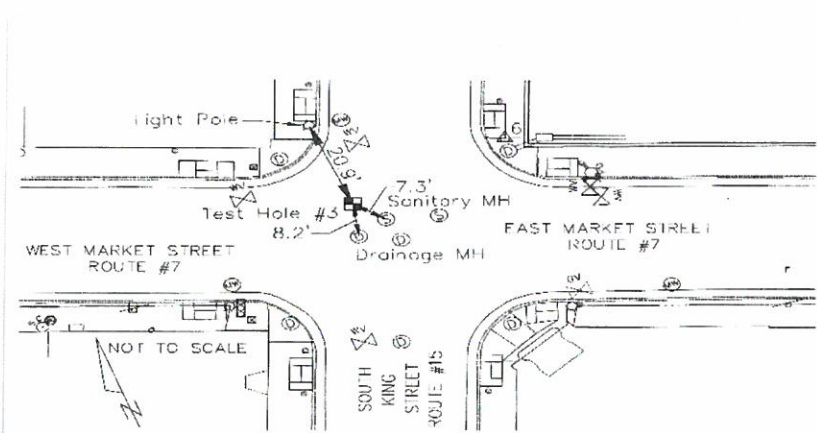

Surveying • Photogrammetry • 3-D Laser Scanning • Subsurface Utility Designation and Mapping

Corporate Office • 10625 Gaskins Way • Manassas, Virginia 20109 • Telephone 703.968.3200 • Fax 703.968.2705
 Richmond Office • 308 Turner Road • Suite G • Richmond, Virginia 23225 • Telephone 804.674.9723 • Fax 804.674.9726
 Virginia Beach Office • 3145 Virginia Beach Blvd. • Suite 103 • Virginia Beach, Virginia 23452 • Telephone 757.306.4260



RICE ASSOCIATES
TEST HOLE FORM

PROJECT INFORMATION



TESTHOLE#	4	DATE	1/6/2015
PROJECT#	AA0902.01G	WEATHER	Below freezing
PROJECT NAME	King/Market Street Leesburg Test Holes	REPORT BY	D. Lunghi
PROJECT DESCRIPTION	Test Holes	CREW	DL, SH, JC
TARGET UTILITY INFORMATION			
UTILITY	Water	O.D. UTILITY SIZE	Unknown
OWNER	Leesburg Water & Sewer	UTILITY TYPE	Water Main
CONTACT NAME	Leslie McClaughy	COLOR	Unknown
PHONE NUMBER	703-737-7075	MATERIAL	Metallic
GENERAL LOCATION	Intersection of Market and King Street	CONDITION	Unknkown
NOTES	Ground Water Level @ 6.85'	SOIL	sand/clay mix

No visual on pipe due to ground water, probed utility

TEST HOLE COORDINATE INFORMATION

NORTHING	7090649.52	TOP COVER	8.92'
EASTING	11748328.15	BOTTOM COVER	Unknown
ELEVATION GRADE	331.74	ELEV. UTILITY BOTTOM	Unknown
ELEV. UTILITY TOP	322.82	ALIGNMENT	N/A
INSTALLED	2 MAG Nails	STATION	N/A
B.M. #10001	Elev =332.33	OFFSET	N/A

SKETCH Not To Scale

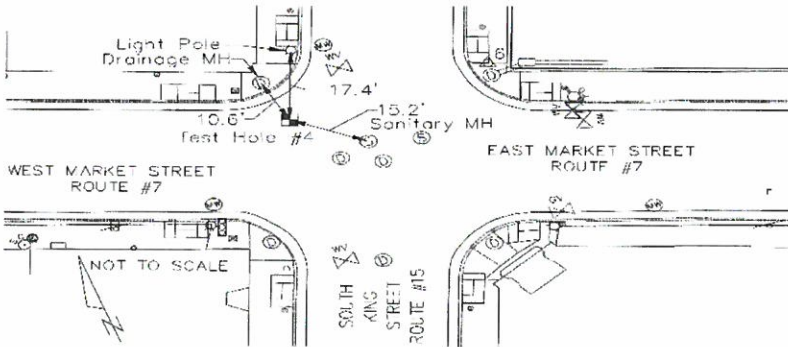

Surveying • Photogrammetry • 3-D Laser Scanning • Subsurface Utility Designation and Mapping



Corporate Office • 10625 Gaskins Way • Manassas, Virginia 20109 • Telephone 703.968.3200 • Fax 703.968.2705
 Richmond Office • 308 Turner Road • Suite G • Richmond, Virginia 23225 • Telephone 804.674.9723 • Fax 804.674.9726
 Virginia Beach Office • 3145 Virginia Beach Blvd. • Suite 103 • Virginia Beach, Virginia 23452 • Telephone 757.306.4260



**RICE ASSOCIATES
TEST HOLE FORM**

PROJECT INFORMATION			
TESTHOLE#	5	DATE	1/6/2015
PROJECT#	AA0902.01G	WEATHER	Below freezing
PROJECT NAME	King/Market Street Leesburg Test Holes	REPORT BY	D. Lunghi
PROJECT DESCRIPTION	Test Holes	CREW	DL, SH, JC
TARGET UTILITY INFORMATION			
UTILITY	Gas	O.D. UTILITY SIZE	Unknown
OWNER	Washington Gas	UTILITY TYPE	Gas Main
CONTACT NAME	Utiliquest	COLOR	Unknown
PHONE NUMBER	703-754-2116	MATERIAL	Unknown
GENERAL LOCATION	Intersection of Market and King Street	CONDITION	Unknown
NOTES	Met Layer of Solid Rock @ 3.26'	SOIL	sand/clay mix-Rock
unable to probe around or through. Test Hole Moved to Avoid Brick Sidewalk and Storm Drain Inlet			
TEST HOLE COORDINATE INFORMATION			
NORTHING	7090663.08	TOP COVER	Unknown
EASTING	11748337.11	BOTTOM COVER	Unknown
ELEVATION GRADE	331.78	ELEV. UTILITY BOTTOM	Unknown
ELEV. UTILITY TOP	Unknown	ALIGNMENT	N/A
INSTALLED	2 MAG Nails	STATION	N/A
B.M. #10001	Elev =332.33	OFFSET	N/A

SKETCH Not To Scale

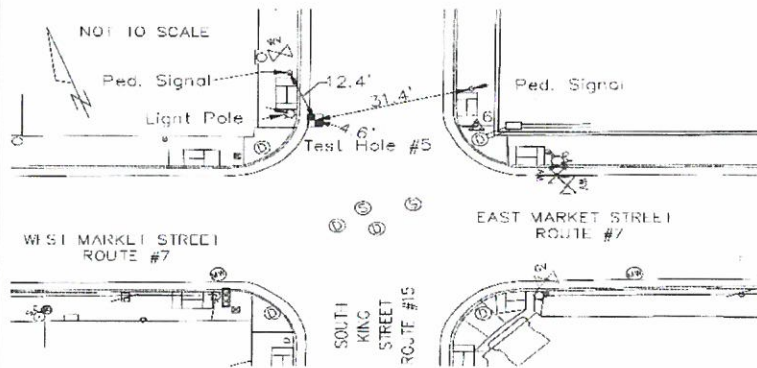

Surveying • Photogrammetry • 3-D Laser Scanning • Subsurface Utility Designation and Mapping



Corporate Office • 10625 Gaskins Way • Manassas, Virginia 20109 • Telephone 703.968.3200 • Fax 703.968.2705
 Richmond Office • 308 Turner Road • Suite G • Richmond, Virginia 23225 • Telephone 804.674.9723 • Fax 804.674.9726
 Virginia Beach Office • 3145 Virginia Beach Blvd. • Suite 103 • Virginia Beach, Virginia 23452 • Telephone 757.306.4260



RICE ASSOCIATES
TEST HOLE FORM

PROJECT INFORMATION			
TESTHOLE#	6	DATE	1/12/2015
PROJECT#	AA0902.01G	WEATHER	Below Freezing
PROJECT NAME	King/Market Street Leesburg Test Holes	REPORT BY	D. Lunghi
PROJECT DESCRIPTION	Test Holes	CREW	DL, JC
TARGET UTILITY INFORMATION			
UTILITY	Gas	O.D. UTILITY SIZE	8"
OWNER	Washington Gas	UTILITY TYPE	Gas Main
CONTACT NAME	Utiliquest	COLOR	Black
PHONE NUMBER	703-754-2116	MATERIAL	Wrapped Steel
GENERAL LOCATION	Intersection of Market and King Street	CONDITION	Excellent
NOTES	Test Hole Moved to Avoid Stop Bar	SOIL	sand/clay mix
TEST HOLE COORDINATE INFORMATION			
NORTHING	7090680.953	TOP COVER	3.64'
EASTING	11748343.47	BOTTOM COVER	4.31'
ELEVATION GRADE	332.08	ELEV. UTILITY BOTTOM	332.77
ELEV. UTILITY TOP	328.44	ALIGNMENT	N/A
INSTALLED	2 MAG Nails	STATION	N/A
B.M. #10001	Elev =332.33	OFFSET	N/A

SKETCH Not To Scale

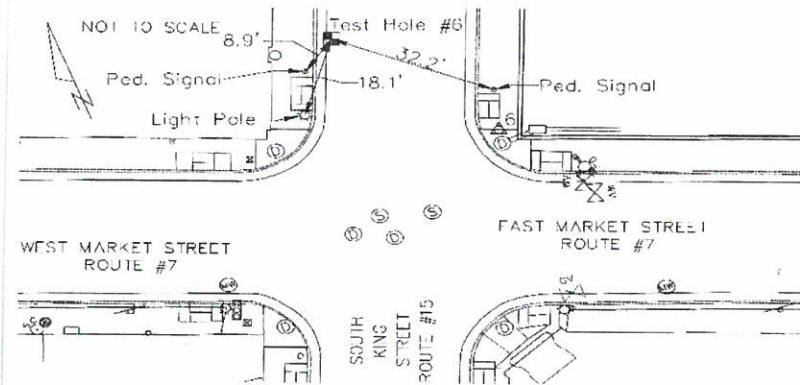

Surveying • Photogrammetry • 3-D Laser Scanning • Subsurface Utility Designation and Mapping



Corporate Office • 10625 Gaskins Way • Manassas, Virginia 20109 • Telephone 703.968.3200 • Fax 703.968.2705
 Richmond Office • 308 Turner Road • Suite G • Richmond, Virginia 23225 • Telephone 804.674.9723 • Fax 804.674.9726
 Virginia Beach Office • 3145 Virginia Beach Blvd. • Suite 103 • Virginia Beach, Virginia 23452 • Telephone 757.306.4260



RICE ASSOCIATES
TEST HOLE FORM

PROJECT INFORMATION			
TESTHOLE#	7	DATE	1/12/2015
PROJECT#	AA0902.01G	WEATHER	Below Freezing
PROJECT NAME	King/Market Street Leesburg Test Holes	REPORT BY	D. Lunghi
PROJECT DESCRIPTION	Test Holes	CREW	DL, JC
TARGET UTILITY INFORMATION			
UTILITY	Water	O.D. UTILITY SIZE	8"
OWNER	Leesburg Water & Sewer	UTILITY TYPE	Water Main
CONTACT NAME	Leslie McClaughry	COLOR	Black
PHONE NUMBER	703-737-7075	MATERIAL	Steel
GENERAL LOCATION	Intersection of Market and King Street	CONDITION	Excellent
NOTES	Test Hole Moved to Avoid Stop Bar	SOIL	sand/clay mix
TEST HOLE COORDINATE INFORMATION			
NORTHING	7090679.254	TOP COVER	3.24'
EASTING	11748348.37	BOTTOM COVER	3.91'
ELEVATION GRADE	332.29	ELEV. UTILITY BOTTOM	328.38
ELEV. UTILITY TOP	329.05	ALIGNMENT	N/A
INSTALLED	2 MAG Nails	STATION	N/A
B.M. #10001	Elev =332.33	OFFSET	N/A

SKETCH Not To Scale

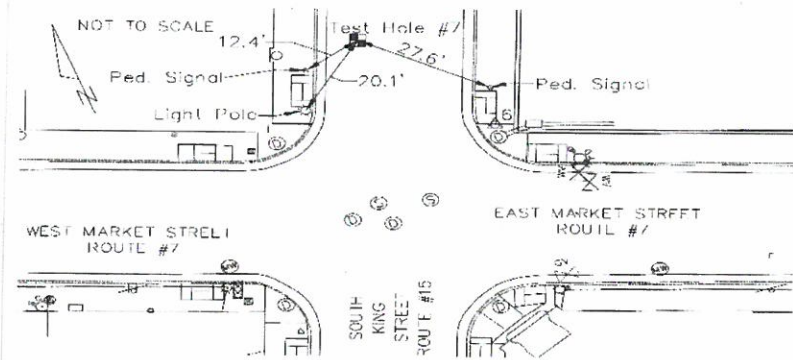

Surveying • Photogrammetry • 3-D Laser Scanning • Subsurface Utility Designation and Mapping

Corporate Office • 10625 Gaskins Way • Manassas, Virginia 20109 • Telephone 703.968.3200 • Fax 703.968.2705
 Richmond Office • 308 Turner Road • Suite G • Richmond, Virginia 23225 • Telephone 804.674.9723 • Fax 804.674.9726
 Virginia Beach Office • 3145 Virginia Beach Blvd. • Suite 103 • Virginia Beach, Virginia 23452 • Telephone 757.306.4260

****FOR INFORMATION ONLY****
Contractor MUST verify before any
excavation work.



TEST HOLE INVENTORY REPORT - QUALITY LEVEL "A"

Leesburg Downtown Improvements, Leesburg, Virginia

Rinker Design Associates

Date	TH #	Utility Requested	Utility Found		Existing Grade Depth	Material Type	Utility Elevation	Pavement Thickness	Utility Owner
08/23/20	1	Water 45° Bend	Water 45° Bend	A	3.12	Cast Iron	328.66	0.7' Asphalt	City of Leesburg
08/23/20	2	Water 45° Bend	Thrust Blocking	A	3.65	Concrete	328.57	0.8' Asphalt	Town of Leesburg
08/23/20	3	Water 45° Bend	Water 45° Bend	A	3.36	Cast Iron	328.19	0.8' Asphalt	Town of Leesburg
08/24/20	4	Telephone / Electric	4" Electric (3)	A	1.91	Plastic	329.50	0.7' Asphalt	VDOT
08/24/20	5	Water 45° Bend	Thrust Blocking	A	3.05	Concrete	328.89	0.7' Asphalt	Town of Leesburg
08/24/20	6	Gas	8" Gas	A	4.32	Steel	327.57	0.7' Asphalt	Washington Gas
06/08/21	7	Water (QLD)	8" Water	A	3.70	Plastic	329.18	0.7' Asphalt	Town of Leesburg

Rinker Design Associates - Point of Contact: Doug Mangin, PE (703) 334-0843


Accumark - Point of Contact: Aaron Blow (703) 635-3074

ACCUMARK

Subsurface Utility Services

Proud - Professional - Precise
Utility Test Hole Report - Quality Level "A"


Test Hole #:	1	Accumark Job#:	NV20-073
Project Name:	Leesburg Downtown Improvements	Client Reference#:	N/A
Requested By:	Rinker Design Associates	Test Hole Date:	08/23/20
	Manassas, Virginia	Project Location:	King Street
Point of Contact:	Doug Mangin, PE	Soil Conditions:	Dry Rocky Clay, Gravel
	(703) 334-0843	Pavement Condition:	Good 0.7' Asphalt
Utility Requested:	Water 45° Bend		

<p style="text-align: center;">Test Hole Cross Section</p>  <p>Existing Grade</p> <p style="text-align: center;">"A"</p> <p>Overall Utility Width: See Notes</p>	<p style="text-align: center;">Elevation / Survey Information:</p> <p>Located By: Accumark, Inc. Vertical Datum: NAVD88</p> <p>Benchmarks Used:</p> <p>BM#1 Elev: 332.33' Description: Pt. #6</p> <p>BM#2 Elev: 337.20' Description: Pt. #7</p> <p>Test Hole Reference Mark</p> <p>Northing: 7090651.92 Easting: 11748320.00 Elevation: 331.78</p>
Drawn Facing: West	

General Notes:

Target utility found. PK set over the top of the mechanical joint on the 45° vertical bend. Crew notes concrete covering utility - unable to obtain utility size. Crew found a pipe restraint between the valve and 45° bend.

Exposed Utility Information									
Utility	Utility Found	Utility Size	Material Type	Depth @ Top of Utility	Elevation @ Top	Duct Bank		Utility Owner	Condition
						Bottom Depth	Elevation		
A	Water 45° Bend	See Notes	Cast Iron	3.12	328.66	N/A	N/A	City of Leesburg	Good

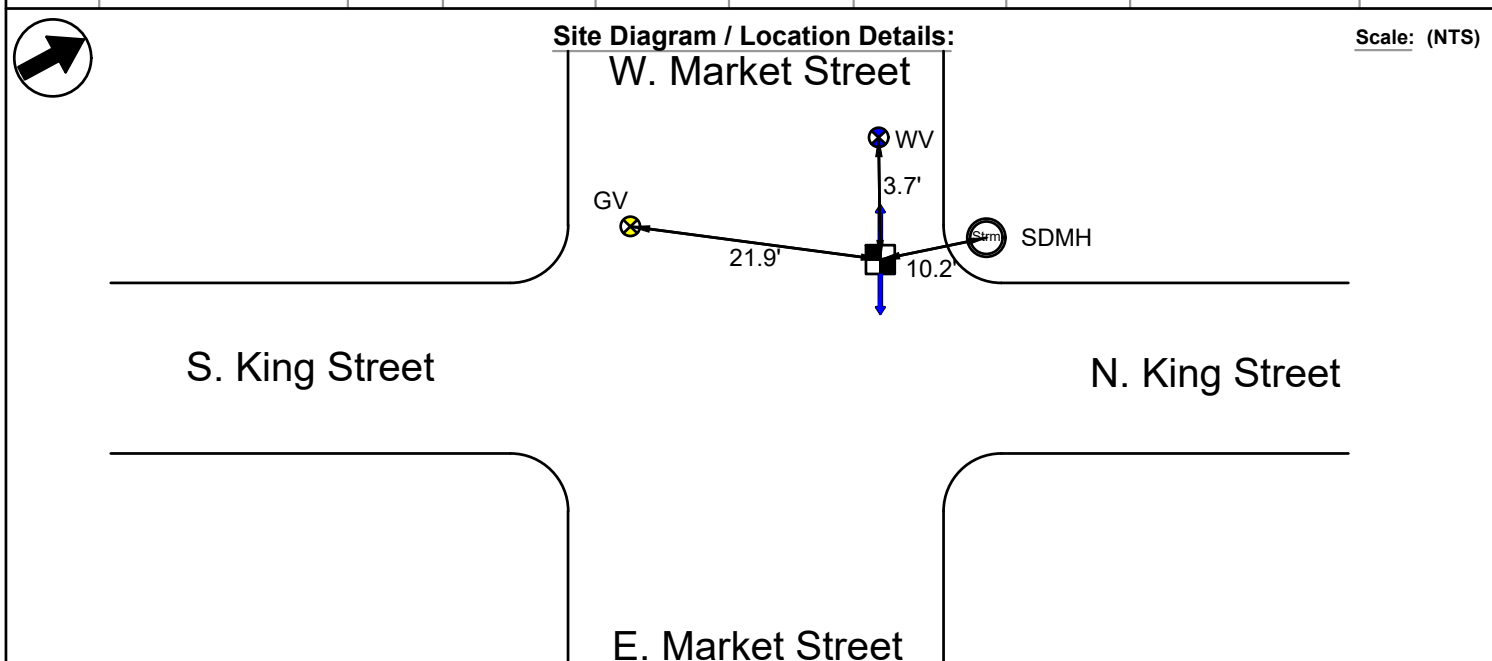

Note: This report depicts and describes the conduits or cables that were visible to our crew upon excavating the test hole. There may be additional conduits or cables located below this configuration which were not visible to the test hole crew.

Proud - Professional - Precise

Utility Test Hole Report - Quality Level "A"

Test Hole #:	<u>1</u>	Project Numbers:	<u>NV20-073</u>
Project Name:	<u>Downtown Leesburg Improvements, Phase IIIC</u>		
Client:	<u>Rinker Design Associates</u>	Project Location:	<u>Leesburg, Virginia</u>




LMB 09/03/20

ACCUMARK

Subsurface Utility Services


Proud - Professional - Precise
Utility Test Hole Report - Quality Level "A"

Test Hole #:	2	Accumark Job#:	NV20-073
Project Name:	Leesburg Downtown Improvements	Client Reference#:	N/A
Requested By:	Rinker Design Associates	Test Hole Date:	08/23/20
	Manassas, Virginia	Project Location:	King Street
Point of Contact:	Doug Mangin, PE	Soil Conditions:	Dry Rocky Clay, Gravel
	(703) 334-0843	Pavement Condition:	Good 0.8' Asphalt
Utility Requested:	Water 45° Bend		

<p style="text-align: center;">Test Hole Cross Section</p>  <p>Existing Grade</p> <p style="text-align: center;">"A"</p> <p>Overall Utility Width: See Notes</p>	<p style="text-align: center;">Elevation / Survey Information:</p> <p>Located By: Accumark, Inc. Vertical Datum: NAVD88</p> <p>Benchmarks Used:</p> <p>BM#1 Elev: 332.33' Description: Pt. #6</p> <p>BM#2 Elev: 337.20' Description: Pt. #7</p> <p>Test Hole Reference Mark</p> <p>Northing: 7090635.66 Easting: 11748371.37 Elevation: 332.22</p>
Drawn Facing: East	

General Notes:
Target utility found. PK set over concrete thrust block for 45° bend. Crew unable to visually verify bend due to concrete around the pipe.

Exposed Utility Information									
Utility	Utility Found	Utility Size	Material Type	Depth @ Top of Utility	Elevation @ Top	Duct Bank		Utility Owner	Condition
						Bottom Depth	Elevation		
A	Thrust Blocking	See Notes	Concrete	3.65	328.57	N/A	N/A	Town of Leesburg	Good

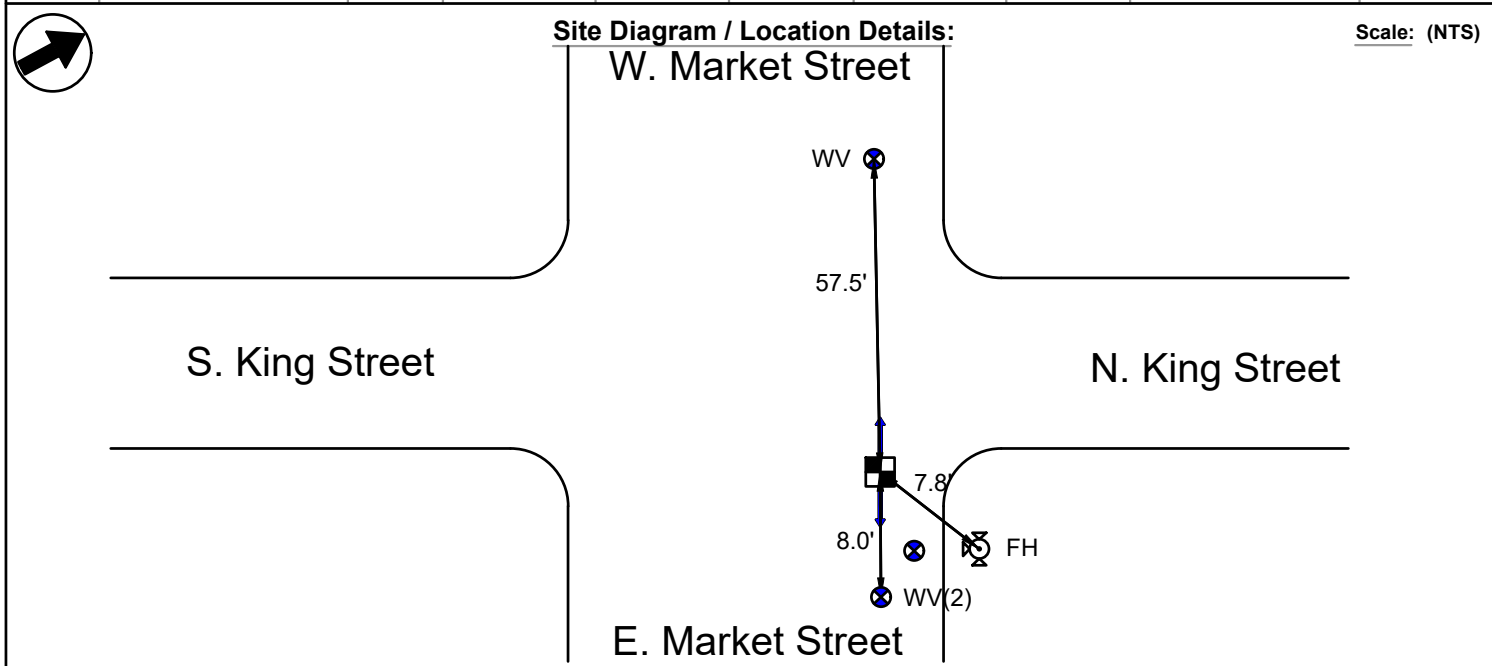

Note: This report depicts and describes the conduits or cables that were visible to our crew upon excavating the test hole. There may be additional conduits or cables located below this configuration which were not visible to the test hole crew.

Proud - Professional - Precise

Utility Test Hole Report - Quality Level "A"

Test Hole #:	<u>2</u>	Project Numbers:	<u>NV20-073</u>
Project Name:	<u>Downtown Leesburg Improvements, Phase IIIC</u>		
Client:	<u>Rinker Design Associates</u>	Project Location:	<u>Leesburg, Virginia</u>



LMB 09/03/20

ACCUMARK

Subsurface Utility Services

Proud - Professional - Precise
Utility Test Hole Report - Quality Level "A"


Test Hole #:	3	Accumark Job#:	NV20-073
Project Name:	Leesburg Downtown Improvements	Client Reference#:	N/A
Requested By:	Phase IIIC	Test Hole Date:	08/23/20
	Rinker Design Associates	Project Location:	King Street
Point of Contact:	Manassas, Virginia	Soil Conditions:	Dry Rocky Clay, Gravel
	Doug Mangin, PE	Pavement Condition:	Good 0.8' Asphalt
Utility Requested:	Water 45° Bend		

<p style="text-align: center;">Test Hole Cross Section</p> <p>Existing Grade</p> <p style="text-align: center;">"A"</p> <p>Overall Utility Width: See Notes</p>	<p style="text-align: center;">Elevation / Survey Information:</p> <p>Located By: Accumark, Inc. Vertical Datum: NAVD88</p> <p>Benchmarks Used:</p> <p>BM#1 Elev: 332.33' Description: Pt. #6</p> <p>BM#2 Elev: 337.20' Description: Pt. #7</p> <p>Test Hole Reference Mark</p> <p>Northing: 7090616.90 Easting: 11748326.31 Elevation: 331.55</p>
<p>Drawn Facing: South</p>	

General Notes:

Target utility found. PK set over the top of the mechanical joint on the 45° vertical bend. Crew notes concrete covering utility - unable to obtain utility size.

Exposed Utility Information									
Utility	Utility Found	Utility Size	Material Type	Depth @ Top of Utility	Elevation @ Top	Duct Bank		Utility Owner	Condition
						Bottom Depth	Elevation		
A	Water 45° Bend	See Notes	Cast Iron	3.36	328.19	N/A	N/A	Town of Leesburg	Good

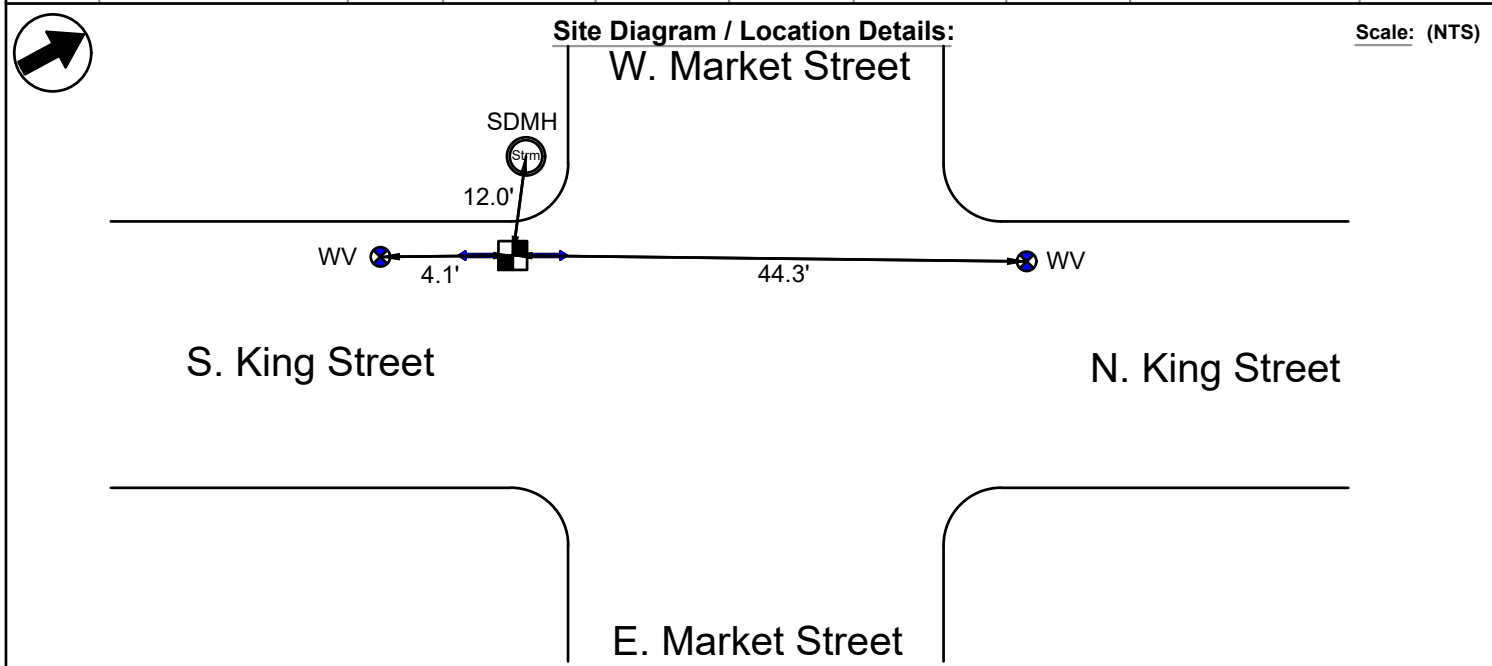

Note: This report depicts and describes the conduits or cables that were visible to our crew upon excavating the test hole. There may be additional conduits or cables located below this configuration which were not visible to the test hole crew.

Proud - Professional - Precise

Utility Test Hole Report - Quality Level "A"

Test Hole #:	<u>3</u>	Project Numbers:	<u>NV20-073</u>
Project Name:	<u>Downtown Leesburg Improvements, Phase IIIC</u>		
Client:	<u>Rinker Design Associates</u>	Project Location:	<u>Leesburg, Virginia</u>



LMB 09/03/20

ACCUMARK

Subsurface Utility Services


Proud - Professional - Precise
Utility Test Hole Report - Quality Level "A"

Test Hole #:	4	Accumark Job#:	NV20-073
Project Name:	Leesburg Downtown Improvements	Client Reference#:	N/A
Requested By:	Rinker Design Associates	Test Hole Date:	08/24/20
	Manassas, Virginia	Project Location:	King Street
Point of Contact:	Doug Mangin, PE	Soil Conditions:	Dry Clay, Gravel
	(703) 334-0843	Pavement Condition:	Good 0.7' Asphalt
Utility Requested:	Telephone / Electric		

<p style="text-align: center;">Test Hole Cross Section</p> <p style="text-align: right;">Overall Utility Width: 12" +/-</p>	<p style="text-align: center;">Elevation / Survey Information:</p> <p>Located By: <u>Accumark, Inc.</u> Vertical Datum: <u>NAVD88</u></p> <p>Benchmarks Used:</p> <p>BM#1 Elev: <u>332.33'</u> Description: <u>Pt. #6</u></p> <p>BM#2 Elev: <u>337.20'</u> Description: <u>Pt. #7</u></p> <p>Test Hole Reference Mark</p> <p>Northing: <u>7090612.81</u> Easting: <u>11748322.55</u> Elevation: <u>331.41</u></p>
---	--

General Notes:
Target utility found. PK set over the center of the utility configuration.

Exposed Utility Information									
Utility	Utility Found	Utility Size	Material Type	Depth @ Top of Utility	Elevation @ Top	Duct Bank		Utility Owner	Condition
						Bottom Depth	Elevation		
A	Electric (3)	4"	Plastic	1.91	329.50	N/A	N/A	VDOT	Good

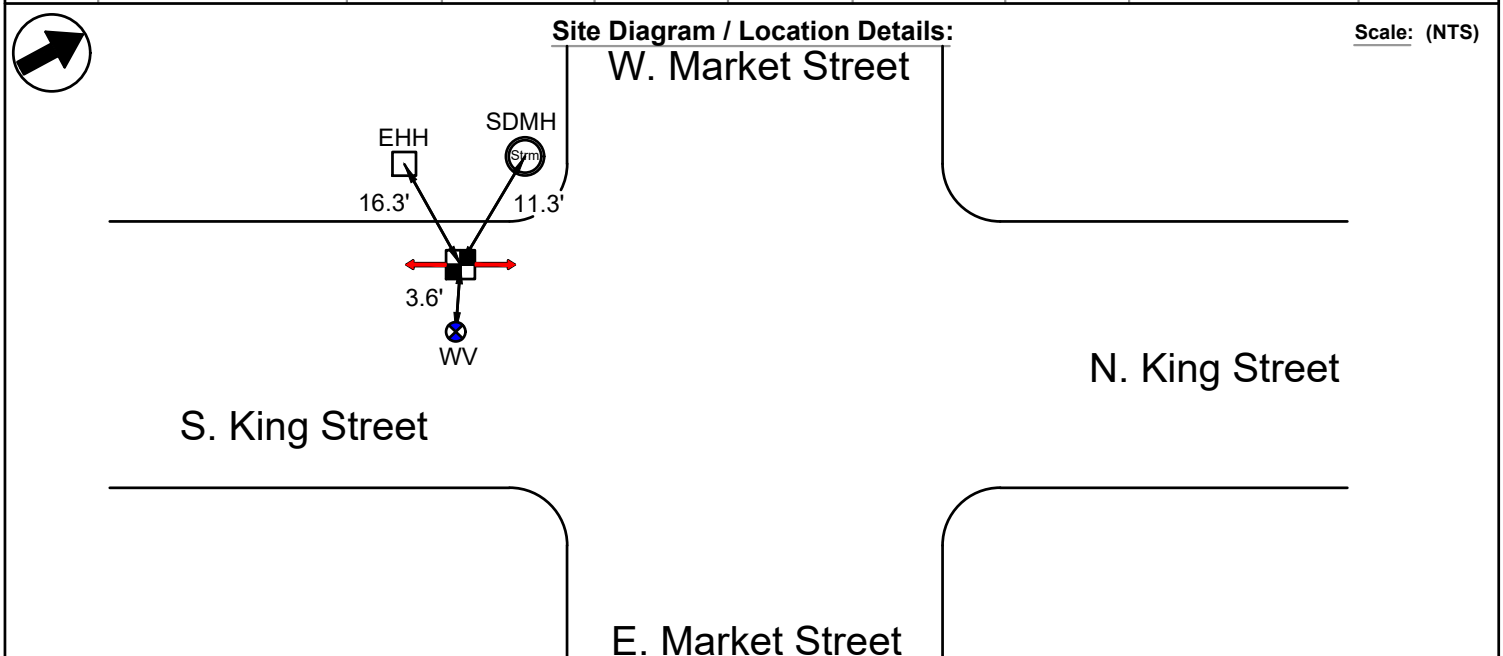

Note: This report depicts and describes the conduits or cables that were visible to our crew upon excavating the test hole. There may be additional conduits or cables located below this configuration which were not visible to the test hole crew.

Proud • Professional • Precise

Utility Test Hole Report - Quality Level "A"

Test Hole #:	<u>4</u>	Project Numbers:	<u>NV20-073</u>
Project Name:	<u>Downtown Leesburg Improvements, Phase IIIC</u>		
Client:	<u>Rinker Design Associates</u>	Project Location:	<u>Leesburg, Virginia</u>




LMB 09/03/20

ACCUMARK

Subsurface Utility Services


Proud - Professional - Precise
Utility Test Hole Report - Quality Level "A"

Test Hole #:	5	Accumark Job#:	NV20-073
Project Name:	Leesburg Downtown Improvements	Client Reference#:	N/A
Requested By:	Phase IIIC	Test Hole Date:	08/24/20
	Rinker Design Associates	Project Location:	King Street
Point of Contact:	Manassas, Virginia	Soil Conditions:	Dry Rocky Clay, Gravel
	Doug Mangin, PE	Pavement Condition:	Good 0.7' Asphalt
Utility Requested:	Water 45° Bend		

<p style="text-align: center;">Test Hole Cross Section</p>  <p>Existing Grade</p> <p style="text-align: center;">"A"</p> <p>Overall Utility Width: See Notes</p>	<p style="text-align: center;">Elevation / Survey Information:</p> <p>Located By: Accumark, Inc. Vertical Datum: NAVD88</p> <p>Benchmarks Used:</p> <p>BM#1 Elev: 332.33' Description: Pt. #6</p> <p>BM#2 Elev: 337.20' Description: Pt. #7</p> <p>Test Hole Reference Mark</p> <p>Northing: 7090657.14 Easting: 11748339.49 Elevation: 331.94</p>
Drawn Facing: North	

General Notes:
Target utility found. PK set over concrete thrust block for 45° bend. Crew unable to visually verify bend due to concrete around the pipe.

Exposed Utility Information									
Utility	Utility Found	Utility Size	Material Type	Depth @ Top of Utility	Elevation @ Top	Duct Bank		Utility Owner	Condition
						Bottom Depth	Elevation		
A	Thrust Blocking	See Notes	Concrete	3.05	328.89	N/A	N/A	Town of Leesburg	Good

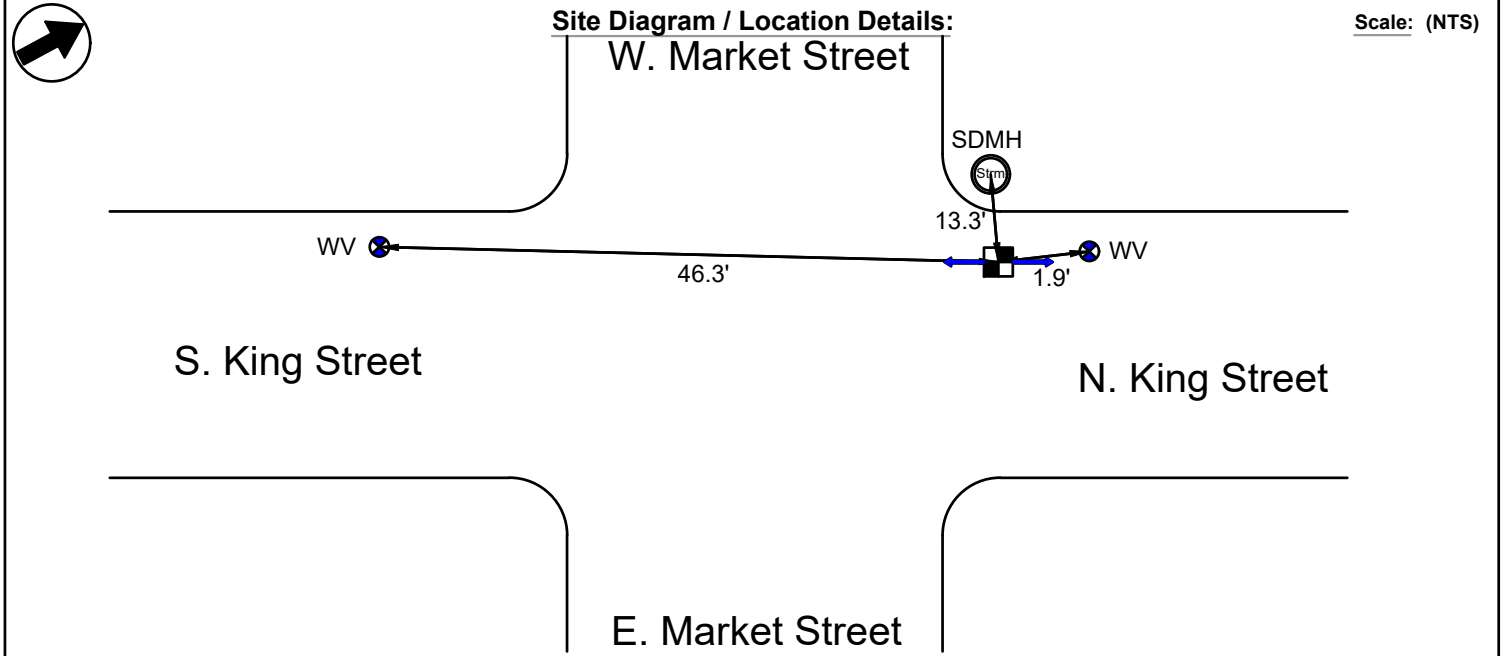

Note: This report depicts and describes the conduits or cables that were visible to our crew upon excavating the test hole. There may be additional conduits or cables located below this configuration which were not visible to the test hole crew.

Proud - Professional - Precise

Utility Test Hole Report - Quality Level "A"

Test Hole #:	<u>5</u>	Project Numbers:	<u>NV20-073</u>
Project Name:	<u>Downtown Leesburg Improvements, Phase IIIC</u>		
Client:	<u>Rinker Design Associates</u>	Project Location:	<u>Leesburg, Virginia</u>



ACCUMARK

Subsurface Utility Services


Proud - Professional - Precise
Utility Test Hole Report - Quality Level "A"

Test Hole #:	6	Accumark Job#:	NV20-073
Project Name:	Leesburg Downtown Improvements	Client Reference#:	N/A
Requested By:	Phase IIIC	Test Hole Date:	08/24/20
	Rinker Design Associates	Project Location:	King Street
Point of Contact:	Manassas, Virginia	Soil Conditions:	Dry Rocky Clay, Gravel
	Doug Mangin, PE	Pavement Condition:	Good 0.7' Asphalt
Utility Requested:	Gas		

<p style="text-align: center;">Test Hole Cross Section</p> <p style="text-align: right;">Overall Utility Width: 8.5" +/-</p>	<p style="text-align: center;">Elevation / Survey Information:</p> <p>Located By: <u>Accumark, Inc.</u> Vertical Datum: <u>NAVD88</u></p> <p>Benchmarks Used:</p> <p>BM#1 Elev: <u>332.33'</u> Description: <u>Pt. #6</u></p> <p>BM#2 Elev: <u>337.20'</u> Description: <u>Pt. #7</u></p> <p>Test Hole Reference Mark</p> <p>Northing: <u>7090663.72</u> Easting: <u>11748339.01</u> Elevation: <u>331.89</u></p>
---	--

General Notes:
Target utility found. PK set over the crown of the target utility. Crew uncovered what appears to be a joint or restraint.

Exposed Utility Information									
Utility	Utility Found	Utility Size	Material Type	Depth @ Top of Utility	Elevation @ Top	Duct Bank		Utility Owner	Condition
						Bottom Depth	Elevation		
A	Gas	8"	Steel	4.32	327.57	N/A	N/A	Washington Gas	Good

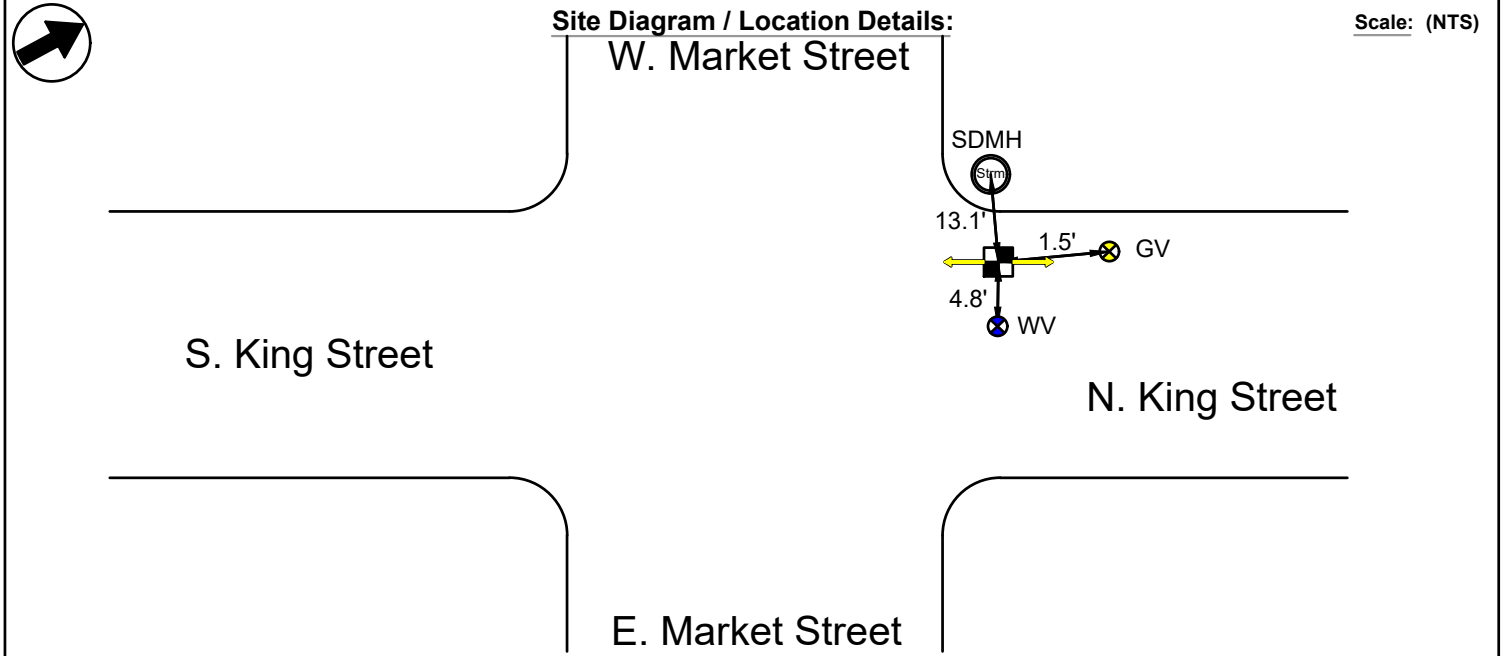

Note: This report depicts and describes the conduits or cables that were visible to our crew upon excavating the test hole. There may be additional conduits or cables located below this configuration which were not visible to the test hole crew.

Proud - Professional - Precise

Utility Test Hole Report - Quality Level "A"

Test Hole #:	<u>6</u>	Project Numbers:	<u>NV20-073</u>
Project Name:	<u>Downtown Leesburg Improvements, Phase IIIC</u>		
Client:	<u>Rinker Design Associates</u>	Project Location:	<u>Leesburg, Virginia</u>



ACCUMARK

Subsurface Utility Services


Proud - Professional - Precise
Utility Test Hole Report - Quality Level "A"

Test Hole #:	7	Accumark Job#:	NV20-073
Project Name:	Leesburg Downtown Improvements	Client Reference#:	N/A
Requested By:	Rinker Design Associates	Test Hole Date:	06/08/21
	Manassas, Virginia	Project Location:	King Street
Point of Contact:	Doug Mangin, PE	Soil Conditions:	Dry Hard Rocky Clay
	(703) 334-0843	Pavement Condition:	Good 0.7' Asphalt
Utility Requested:	Water (QLD)		

<p style="text-align: center;">Test Hole Cross Section</p> <p>Existing Grade</p> <p style="text-align: center;">"A"</p> <p>Overall Utility Width: 8.5" +/-</p> <p>Drawn Facing: East</p>	<p style="text-align: center;">Elevation / Survey Information:</p> <p>Located By: Accumark, Inc. Vertical Datum: NAVD88</p> <p>Benchmarks Used:</p> <p>BM#1 Elev: 332.33' Description: Pt. #6</p> <p>BM#2 Elev: 337.20' Description: Pt. #7</p> <p>Test Hole Reference Mark</p> <p>Northing: 7090671.87 Easting: 11748260.04 Elevation: 332.88</p>
---	---

General Notes:
Target utility found. PK Nail set over the crown of the target utility.

Exposed Utility Information									
Utility	Utility Found	Utility Size	Material Type	Depth @ Top of Utility	Elevation @ Top	Duct Bank		Utility Owner	Condition
						Bottom Depth	Elevation		
A	Water	8"	Plastic	3.70	329.18	N/A	N/A	Town of Leesburg	Good

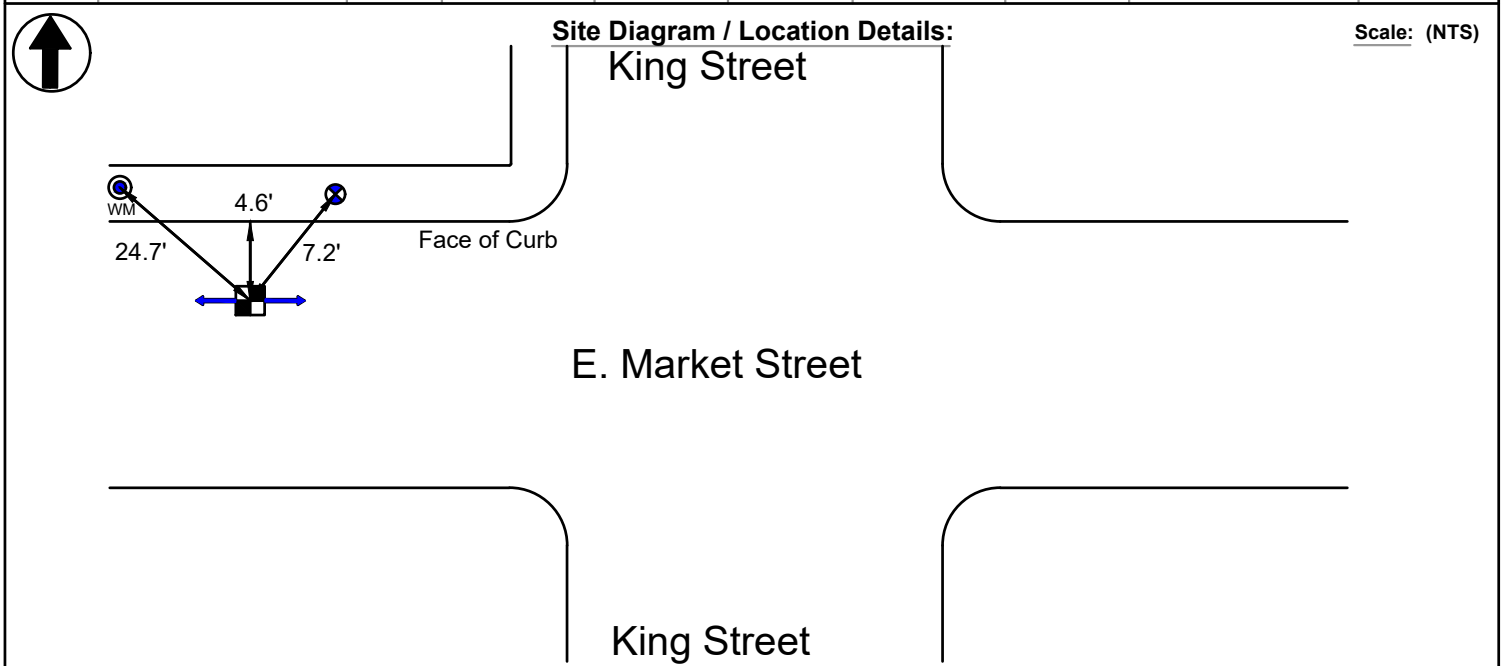


Note: This report depicts and describes the conduits or cables that were visible to our crew upon excavating the test hole. There may be additional conduits or cables located below this configuration which were not visible to the test hole crew.

Proud · Professional · Precise

Utility Test Hole Report - Quality Level "A"

Test Hole #:	<u>7</u>	Project Numbers:	<u>NV20-073</u>
Project Name:	<u>Downtown Leesburg Improvements, Phase IIIC</u>		
Client:	<u>Rinker Design Associates</u>	Project Location:	<u>Leesburg, Virginia</u>

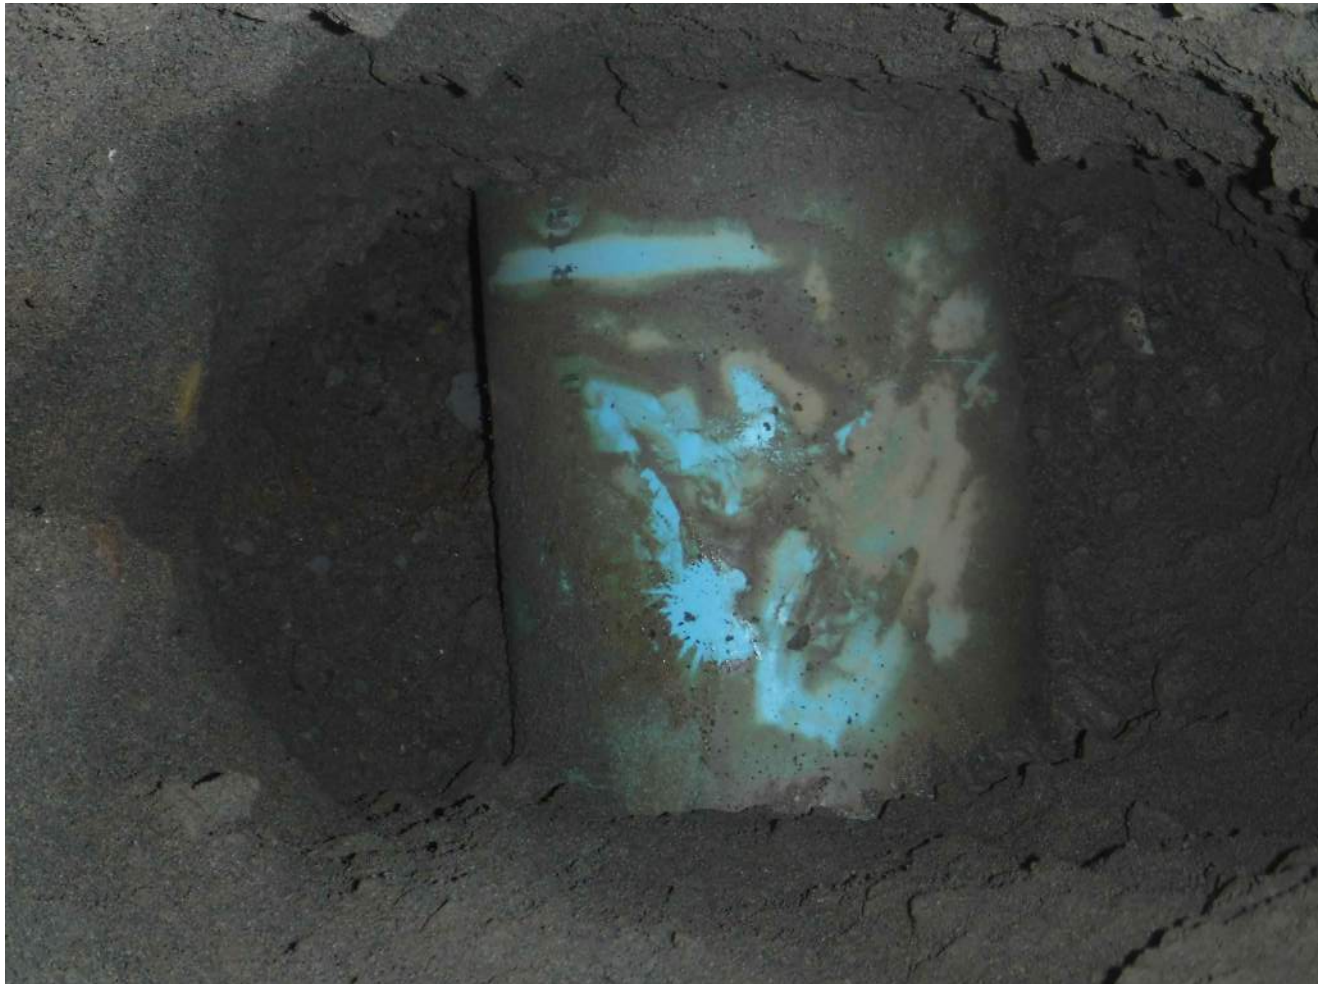

MCT 06/11/21

Impressed preformed thermoplastic crosswalks and traffic calming surfaces for asphalt

TrafficPatternsXD[®] preformed thermoplastic is an extremely durable material that incorporates a unique aggregate-reinforced formula with enhanced wear resistance. The result is a traffic-tough crosswalk that provides traditional bricklike aesthetics built to last.



PERFORMANCE-BASED FEATURES AND BENEFITS

- Designed for extreme use and wear in high-traffic crosswalks and traffic calming surfaces
- Engineered for a robust application system and enhanced durability at 150 miles
- Enhanced performance in all climates
- Applied to high-quality, stable asphalt with minimal substrate impact
- Fast installation and minimal traffic downtime
- High skid/slip resistant for safety – as material wears, new anti-skid elements are exposed
- ADA compliant – pedestrian and wheelchair friendly surface
- Eliminates the maintenance and safety concerns of loose pavers
- Made at Ennis-Flint's manufacturing facility which is ISO 9001:2015 certified for the design, development and manufacturing of preformed thermoplastic
- Markings designed for quality, value, and long-term performance
- Anti-skid elements added at time of manufacturing for optimized application at the jobsite


TrafficPatternsXD thermoplastic material is installed by a network of certified applicators so you can be confident that your design intentions will manifest on the job site. The 2 ft. x 2 ft. sheets of material are positioned on the non-stamped, prepared asphalt surface. The material is heated to allow proper embedment of the anti-skid elements. A specialized grid gently stamps a pattern into the material and just into the top layer of the asphalt.



STANDARD PATTERNS



STANDARD BORDERS



STANDARD COLORS



PREMIUM COLORS





TrafficScapes®

Surface Systems

CROSSWALKS • MEDIANS • ISLANDS • ROUNDABOUTS • ENTRYWAYS • LOGOS

TrafficScapes® preformed thermoplastic pavement marking materials portfolio is engineered for durability, safety, and aesthetics for the streetscape and traffic calming market. Each product offers its own unique application and performance approach to streetscape projects where shared roadway safety and aesthetic appeal need to work in conjunction.

TrafficPatterns®
Interconnected Surface System



TrafficPatternsLT®
Overlay Surface System



DecoMark®
Surface Signs



TrafficPatternsGF®
Grout-Free Surface System



TrafficPatternsXD®
Impressed Surface System



DuraTherm®
Inlaid Surface System




When used on public roadways and private properties open to public travel, decorative crosswalks require proper demarcation with white linear boundaries according to the Manual on Uniform Traffic Control Devices (MUTCD).




Step by Step Vendor Registration Instructions

Start by clicking the *Register Now* link on the eVA website homepage (www.eVA.virginia.gov).

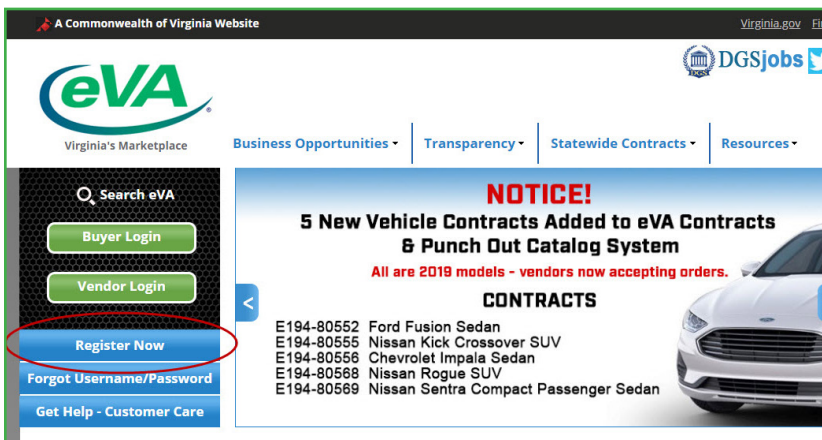

Registration Checklist

1. **Company name** – Be sure to list a name that buyers will easily recognize.
2. **Federal Tax Identification Number (TIN)** – The 9 digit TIN or Social Security number that identifies your organization.
3. **Addresses & Contact information**
You will need street and/or PO box addresses, phone & fax numbers, and email addresses for orders, payments, bills, solicitations (business opportunities), and physical location.
4. **Commodity Codes** – Describes to buyers what your company sells. Use the *NIGP Code Look Up* link on the left hand menu of the eVA home page.

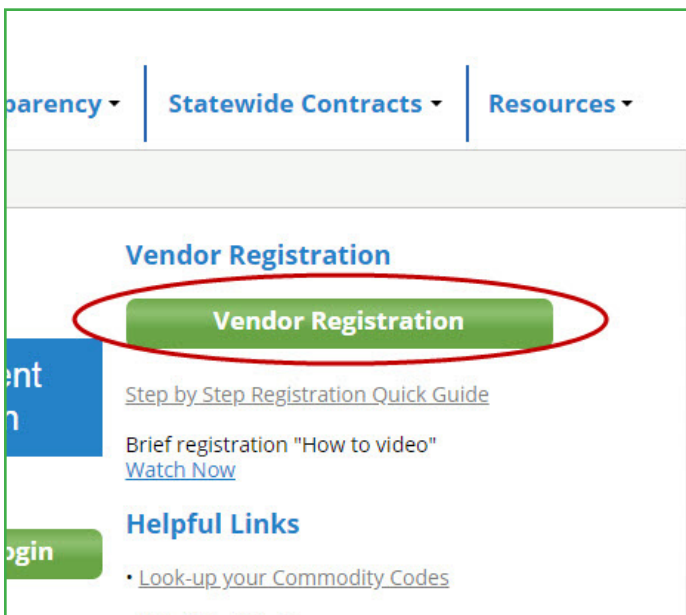

You can either begin a **New Registration**

Or you can choose **Add Location** or **Change Registration Type** to update an existing account

Search for your company location

Has your company done business with us in the past? If so, your company may already be in our database. Please use search.

Company Name:

Is your company listed ?

Yes, I found my Headquarters but not my Location → Click **Add Location** to create new Location for the existing Headq

Yes, my Account is activated but I don't know the login → Call Customer Care @ 1-866-289-7367 for help.

No, Register Now →

Headquarter Standard Name	Location Name	HQ Account	Registration Type	
Team MX	Tomahawk	No	Self-Registered	Add Location
Tom Gilbert	Michigan	Yes	Self-Registered	Add Location
Tom Tom Inc	Tom Tom Inc	Yes	Self-Registered	Add Location
✓ Tom's Taxidermy	HQ	Yes	State-Entered	Change Registration Type Add Location

For a new registration, you will start the registration process by reviewing & accepting eVA's Memorandum of Agreement then entering your company's EIN or SSN number.

eVA Memorandum Of Agreement (Effective 5/16/2006)

Thank you for joining the Commonwealth of Virginia eVA supplier community. You must agree to the terms defined below in order to:

- continue with the eVA registration process.
- avoid having an existing registration deactivated/canceled.

You are strongly encouraged to click on the "help & advice" button for more information.

This Memorandum Of Agreement (Agreement) sets forth the terms that have been established by the Commonwealth of Virginia, Department and Supply ("DPS") to govern all electronic procurement transactions made between your firm ("Vendor") and any agency or public body made, in whole or in part, utilizing the Commonwealth of Virginia's web-centric statewide electronic procurement solution (eVA).

For purposes of this Agreement:

- electronic procurement transaction is defined to include electronic quotations, bids, proposals, purchase orders, contracts, invoice procurement information, instruments and notices electronically transmitted, received, or posted using eVA in lieu of or in addition to paper.
- agency is defined as any department, authority, board, post, commission, division, institution, or office of State government of the Commonwealth of Virginia.
- public body is defined as any legislative, executive or judicial body, agency, office, department, authority, post, commission, committee, or board created by law in Virginia to exercise some sovereign power or to perform some governmental duty, and empowered by law to use eVA.
- eVA Fee Schedule is defined as a listing of eVA registration, transaction, and other fees (eVA fees) that are assessed to eVA users published on the eVA Website. Each fee set forth on the eVA Fee Schedule is effective dated so eVA users including Vendors can see the fee schedule.

Provide the following and continue

Taxpayer ID & Type: EIN SSN

Company Zip:

Department of General Services • Division of Purchases and Supply • eProcurement Bureau
 1111 East Broad Street • Richmond, VA 23218-1199 • Patrick Henry Building
 For additional information, contact evacustomer@dgsvirginia.gov or 1-866-289-7367.

Company Profile

Tell us about your company, including if you'd like to receive bidding opportunities and whether or not your company accepts charge cards.

Enter information as it appears on your W-9 form

▼ Company Profile

* Taxpayer ID Number(Type) : 451203698(EIN)

* Organization Type :

Supplemental Organization Type :

Company/DBA/Location Name: Check if same as above

* Company Legal Name :

* DBA/Location Name :

Web Address :

* Notification of Bids? :

* Accept Charge Cards? :

Tax Exempt :

Tax Address

* W-9 Address :

City/State/Zip :

Country :

Attachments - attach supporting files: W-9, W-8, etc.
Registration is not considered complete unless a Commonwealth of Virginia Substitute W-9 is received. Payments for goods or services may be impacted without a properly executed Commonwealth of Virginia Substitute W-9 form. Get the W-9 form here: http://www.doa.virginia.gov/General_Accounting/Forms/W9_COVSubstitute.pdf

Purchases under \$5,000 will be made via the Commonwealth's Small Purchase Charge Card (VISA). Standard vendor merchant fees apply.

Upload your W-9 here.

Registration is not considered complete unless the Commonwealth of Virginia Substitute W-9 is received. Payments for goods or services may be impacted without a properly executed Commonwealth of Virginia Substitute W-9 form found here:
http://www.doa.virginia.gov/General_Accounting/Forms/W9_COVSubstitute.pdf

User Information

By checking the box for *Notifications* you are requesting for the *User to be* sent bidding opportunities.

▼ Create your Login Profile

* First Name :

* Last Name :

* Email :

* Retype Email :

* Phone :

Fax :

Notifications : (Include this user for Bid Notifications)

* Password :

* Retype Password :

Department of General Services • Division of Purchases and Supply • eProcurement Bureau
1111 East Broad Street • Richmond, VA 23218-1199 • Patrick Henry Building
For additional information, contact evacustomer@dgcs.virginia.gov or 1-866-289-7367.

Ordering Information

If your *Ordering Address* is the same as the *W-9 address* you entered above, then click *Copy Tax Address*.

If your *Ordering Contact* is the same as the *Login Profile* you entered above, then click *Copy Login Profile Info*.

▼ Address Information

Ordering Address (Copy Tax Address)	Ordering Contact: (Copy Login Profile Info)
* Street 1 : <input type="text"/>	* Contact First Name : <input type="text"/>
Street 2 : <input type="text"/>	* Contact Last Name : <input type="text"/>
* City/State/Zip : <input type="text"/> <input type="text"/> <input type="text"/>	* Email : <input type="text"/>
* Country : <input type="text"/>	* Retype Email : <input type="text"/>
* Method of Notification : Email	* Phone : <input type="text"/>
	* Fax : <input type="text"/>

Receive bid notifications electronically by selecting *email* from the drop down menu.

Leave the default as “Yes” if your other addresses are the same as your *Ordering Address*.

If one of the addresses is NOT the same as your *Ordering Address* then select “No” from the drop down menu for that address type and complete all required fields.

Solicitation Address/Contact(same as Ordering?) Yes	
Physical Address/Contact(same as Ordering?) No	Physical Contact: (Copy Login Profile Info)
* Street 1 : <input type="text"/>	* Contact First Name : <input type="text"/>
Street 2 : <input type="text"/>	* Contact Last Name : <input type="text"/>
* City/State/Zip : <input type="text"/> <input type="text"/> <input type="text"/>	* Email : <input type="text"/>
* Country : <input type="text"/>	* Retype Email : <input type="text"/>
* Method of Notification : <input type="text"/>	* Phone : <input type="text"/>
	* Fax : <input type="text"/>
Payment Address/Contact(same as Ordering?) Yes	
Billing Address/Contact(same as Ordering?) Yes	


Department of General Services • Division of Purchases and Supply • eProcurement Bureau
1111 East Broad Street • Richmond, VA 23218-1199 • Patrick Henry Building
For additional information, contact evacustomer@dgcs.virginia.gov or 1-866-289-7367.

Order Delivery Options

Receive your Orders Electronically

The Commonwealth of Virginia uses the Ariba Network, an Internet based service, to transmit Purchase Orders to our Vendors electronically. Electronic order routing is the preferred method of the Commonwealth.

If you have an Ariba Network Account choose “Electronic.” Select “Yes” to *Do you have an Ariba Network account?* and be sure to list your Ariba Network ID.



▼ Order Delivery Options

* How do you want to get your Orders ? : Electronic ▼


* Do you have an Ariba Network account ? : Yes ▼

Ariba Network ID (if known) : AN01000032826

If you do not have an Ariba Network Account choose “Electronic.” Select “No” to *Do you have an Ariba Network Account?* and select Email or Fax as your Delivery method. Orders will be routed to the Email or Fax you listed in your Ordering Address details.

By selecting “Electronic,” a free Ariba Network account will be pre-enabled for you. You will receive instructions on how to activate your Ariba account with your first order. With an Ariba account you will have access to Ariba’s vast network of users to whom you can also market your goods and services.

Choose “US Mail” only if the above methods do not fit your needs.



▼ Order Delivery Options

* How do you want to get your Orders ? : Electronic ▼

* Do you have an Ariba Network account ? : No ▼

* Select Delivery Method : ▼

- Email (using Ordering Address email)
- Fax (using Ordering Address fax)
- CXML/EDI Transaction

Service Area(s)

Tell Buyers where you do business

By choosing Zone 10, Statewide, you'll receive bid notifications from all over the state, not only from your area—providing you greater access to opportunities.

▼ **Service Area(s) and Commodity Profile**

Select Area(s) where you sell goods/services

Select Area(s)

Delete Service Area Zone

Choose

Select one or more Service Areas to associate to your company. To search for your Service Area, enter in a valid service area and click Search. Please click OK to save your changes.

Clear

Service Area Zone : Search

Service Area Zone
<input checked="" type="checkbox"/> Statewide
<input type="checkbox"/> Cities: Chesapeake, Franklin, Hampton, Newport News, Norfolk, Poquoson, Portsmouth, Suffolk, Virginia Beach, and Williamsburg. Counties: Isle of Wight, James City, Southampton, Surry, Sussex, and York.
<input type="checkbox"/> Cities: Colonial Heights, HopeWell, Petersburg, and City of Richmond. Counties: Charles City, Chesterfield, Dinwiddie, Goochland, Hanover, Henrico, King William, New Kent, Powhatan, and Prince George's.
<input type="checkbox"/> City: Fredericksburg. Counties: Caroline, Culpeper, Essex, Gloucester, King and Queen, King George, Lancaster, Madison, Mathews, Middlesex, Northumberland, Orange, Richmond County, Spotsylvania, and Stafford.
<input type="checkbox"/> Cities: Alexandria, Fairfax, Falls Church, Manassas, Manassas Park and Winchester. Counties: Arlington, Clarke, Fairfax, Fauquier, Frederick, Loudoun, Page, Prince William, Rappahannock, Shenandoah, and Stafford.
<input type="checkbox"/> Cities: Charlottesville, Harrisonburg, Staunton, and Waynesboro. Counties: Albemarle, Augusta, Fluvanna, Greene, Highland, Louisa, Nelson, and Rockingham.
<input type="checkbox"/> City: Emporia. Counties: Amelia, Brunswick, Buckingham, Charlotte, Cumberland, Greensville, Halifax, Lunenburg, Mecklenburg, Nottoway, and Prince Edward.
<input type="checkbox"/> Cities: City of Bedford, Buena Vista, Clifton Forge, Covington, Danville, Lexington, and Lynchburg. Counties: Alleghany, Amherst, Appomattox, Bath, Bedford County, Botetourt, Campbell, Pittsylvania, and Shenandoah.
<input type="checkbox"/> Cities: Galax, Martinsville, Radford, City of Roanoke, and Salem. Counties: Carroll, Craig, Floyd, Franklin, Giles, Henry, Montgomery, Patrick, Pulaski, and Roanoke County.
<input type="checkbox"/> Cities: Bristol and Norton. Counties: Bland, Buchanan, Dickenson, Grayson, Lee, Russell, Scott, Smyth, Tazewell, Washington, Wise, and Wythe.
<input type="checkbox"/> Counties: Accomack and Northampton

First Prev Next Last

OK Cancel

Department of General Services • Division of Purchases and Supply • eProcurement Bureau
1111 East Broad Street • Richmond, VA 23218-1199 • Patrick Henry Building
For additional information, contact evacustomer@dgsc.virginia.gov or 1-866-289-7367.

Commodity Codes

Enter the Commodity Codes that best describe what you sell.

TIPS! Do you provide all of the goods/services listed under a main category? If you said yes, then simply select only the main class code for your Vendor Account and you will receive notification for every opportunity for every item code under that main class!

(Required) Select NIGP codes to describe goods/services you sell

Delete	NIGP Code	Description
<input type="checkbox"/>	23227	Dried Flowers and Plants
<input type="checkbox"/>	23235	Floral Supplies: Artificial Flowers, Floral Tape, etc.
	flower	
	39367	Nuts, Edible (Incl. Sunflower Seeds)
	59515	Bulbs and Seeds (Incl. Flower Seeds)
	59528	Flowers, Fresh
	59557	Plants, Non-Flowering
	59566	Shrubbery, Flowering
	59588	Vases, Flower Pots, Pottery, etc.

For help understanding how Commodity Codes are categorized and used, reference the [Understanding Commodity Codes](#) guide located in the *Vendor Resource Center* under *Tools*.

If you need help identifying your Commodity Codes, use the [NIGP Code Lookup](#) located on the *I Sell to Virginia* page of the eVA website also found under the *Tools* section.

NIGP Code Starting With: Please enter a NIGP Code or leave blank!

Search Description:

[Search](#) [View All](#)

Class	Description
28500	ELECTRICAL EQUIPMENT AND SUPPLIES (EXCEPT CABLE AND WIRE)
NIGP Code	Description
28500	ELECTRICAL EQUIPMENT AND SUPPLIES (EXCEPT CABLE AND WIRE)
28501	Automated Meter Reading Systems (AMR)
28502	Analyzer, Electric Power Demand
28503	Arresters, Lightning
28504	Back-up Systems, Battery Operated (Emergency)
28505	Beacon Light Systems Complete For Buildings, Roadside, etc. (See Class 120 for Marine Beacons)

Change your mind?
It's easy to edit the Commodity Codes you have selected!

(Required) Select NIGP codes to describe goods/services you sell

Delete	NIGP Code	Description
<input checked="" type="checkbox"/>	23227	Dried Flowers and Plants
<input type="checkbox"/>	23235	Floral Supplies: Artificial Flowers, Floral Tape, etc.

Submit Registration!

Your eVA registration is complete and a username has been created for you.

Welcome aboard!

Thank You! [help & advice](#)

Congratulations, you have completed the registration process. You may now login to VSS using the User Name and Password you just created.

Your User Name is: tjohn

You Should

- Review your confirmation email from eVA (NoReturn@dgs.virginia.gov)
- Obtain an Ariba account for electronic orders (see guidance below)
- Login to review Account Maintenance features

[Login](#)

Department of General Services • Division of Purchases and Supply • eProcurement Bureau
1111 East Broad Street • Richmond, VA 23218-1199 • Patrick Henry Building
For additional information, contact evacustomer@dgsc.virginia.gov or 1-866-289-7367.




Quick Steps for Submitting an Electronic Response to an IFB Solicitation



Need help? Call eVA Customer Care at 866-289-7367 or Email eVACustomerCare@dgs.virginia.gov

General Requirements

- Your business must be eVA registered and in active status.
- **AVOID waiting until the day the solicitation closes to submit your response.**
- **Delaying submission could put your response at risk of not being accepted on time.**

1	Login to eVA	Login with your eVA account <i>user name</i> and <i>password</i> @ https://vendor.epro.cgipdc.com/loginEngine/index.jsp ** If you have not registered, use the <i>Register</i> button.
2	Find the Solicitation	<ol style="list-style-type: none">Enter solicitation number/description into the Search field.Click the Search iconClick the View Opportunity button on the solicitation you wish to view. Didn't find it? Use the Advanced Search filters.
3	Review Solicitation & begin the response	<ol style="list-style-type: none">Review the solicitation posting and attachments.Click Respond Online
4	Response Steps: 1: Solicitation Response 2: Line Items	<ol style="list-style-type: none">Click on +Solicitation Summary for a summary of the solicitation.Attach Your Files (Optional). *The maximum size allowed for each file is 60.0MB.<ol style="list-style-type: none">Click Attach Files buttonClick Browse/Choose File, locate the file you want to attach, and click Open, select file attachment Type: Standard, or Proprietary; repeat this step as necessary to attach more files.Click Attach File(s) buttonNOTE: If you need to attach more than five files, repeat a-c.Respond to Evaluation Criteria, Reminders, Discounts (Optional), and enter any Overall Response Comments as applicable.Click Next: Line Items NOTE: A warning pop-up confirmation message will appear if there were no attachment/s added. Click Cancel to edit response and add an attachment or click Continue to respond to the Line Items. <ol style="list-style-type: none">Click No Bid Lot to No Bid a Lot or Click Undo No Bid Lot to Undo No Bid a Lot (if applicable).For lines, you would like to respond to, enter your responses in Unit Price and Delivery Days. NOTE: Additional per line item information, can be provided by expanding the Comments, Product Specs, and Shipping/Handling Details links. <ol style="list-style-type: none">For lines, you do not wish to respond to, select No Response from the Response Type drop-down box.

<p>2: Lines Items (cont'd)</p> <p>3: Subcontractor Plan</p> <p>4: Response Summary</p>	<p>iv. Click Next: Subcontractor Plan</p> <p>NOTE: Small Business Subcontracting Plan Submission, refer to the instructions provided in the solicitation.</p> <p>i. Click Next: Review & Submit</p> <p>NOTE: A warning pop-up confirmation message will appear if you have not answered the subcontractor plan questions, “Who will be doing the work?”. Click Cancel to edit response and add a subcontractor plan or click Continue to review and submit the respond.</p> <p>i. Review response and click Submit</p> <p>ii. Confirm submission of response by clicking the Submit button on the pop up.</p> <p>NOTE: You will receive an “Action is complete. Click Close to exit.” confirmation screen once your response has successfully submitted.</p>  <p>iii. Click Close</p>
<p>5 Verify Acceptance / Review Response</p>	<p>i. From the Home page, Click the My Business dropdown box and click the Responses link (top of page)</p> <p>ii. Find the solicitation number and corresponding Response ID, if labeled “Accepted” your response has been accepted.</p> <p>iii. To Review the response, click the View/Edit Response button</p>
<p>6 Amend Response</p>	<p>i. From the Home page, click the My Business dropdown box and click the Responses link (top of page).</p> <p>ii. Find the latest version of your solicitation response and click the View/Edit Response button.</p> <p>iii. Click Edit button (top of page), status will now be showing “In Progress”</p> <p>iv. Update information as necessary to this page</p> <p>v. Click Next: Line Items</p> <p>NOTE: A warning pop-up confirmation message will appear if there were no attachment/s added. Click Cancel to edit response and add an attachment or click Continue to navigate to the Line Items.</p> <p>vi. Update information as necessary to this page</p> <p>vii. Click Next: Subcontractor Plan</p> <p>NOTE: Small Business Subcontracting Plan Submission, refer to the instructions provided in the solicitation.</p> <p>viii. Click Next: Review & Submit</p> <p>NOTE: A warning pop-up confirmation message will appear if you have not answered the subcontractor plan questions, “Who will be doing the work?”. Click Cancel to edit response and add a subcontractor plan or click Continue to review and submit the respond.</p>

<p>Amend Response (cont'd)</p>	<p>ix. Review response and click Submit</p> <p>x. Confirm submission of response by clicking the Submit button on pop up.</p> <p>NOTE: You will receive an “Action is complete. Click Close to exit.” confirmation screen once your response has successfully submitted.</p>  <p>xi. Click Close</p>
<p>7 Withdraw Response</p>	<p>i. From the Home page, click the My Business dropdown box and click the Responses link (top of page).</p> <p>ii. Find the latest version of your solicitation response and click the View/Edit Response button.</p> <p>iii. Click Withdraw (top of page)</p> <p>iv. Confirm and click Withdraw on pop up</p> <p>NOTE: You will receive an “Action is complete. Click Close to exit.” confirmation screen once your response has successfully submitted.</p>  <p>v. Click Close</p> <p>vi. Status under Response will now be Withdrawn</p>
<p>8 Print Response</p>	<p>i. From the Home page, click the My Business dropdown box and click the Responses link (top of page).</p> <p>ii. Find the latest version of your solicitation response and click the View/Edit Response button.</p> <p>iii. Click Next: Line Items</p> <p>iv. Click Next: Subcontractor Plan</p> <p>v. Click Next: Review & Submit</p> <p>vi. Click Print</p> <p>vii. Click Exit</p>
